Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
Contract Milestones												
Construction												
General												
General Requirements												
M1800	Notice to proceed	0	0	0	100%					06-Apr-15	20-May-15	23-Oct-14
M900	SUCF MS1: Emergency Power System (27NOV15)	0	0	0	0%	-18				26-Nov-15	23-Dec-15	
M1010	SUCF MS2: Fire Alarm: MART, Bed Tower 1-5, and 10 (10FEB16)	0	0	0	0%	-81				22-Mar-16	02-Jun-16	
M1830	SUCF MS2b: Zone 5A Substantial Completion (N/R)	0	0	0	0%	-50				23-Jun-16	01-Aug-16	
M1020	SUCF MS3: Systems & Finishes MART Wing 100% (31MAR16)	0	0	0	0%	-92				12-May-16	05-Aug-16	
M1030	SUCF MS4: Substantial Completion: MART & Bed Tower 1-5, 10 (20MAY:	0	0	0	0%	-75				29-Jun-16	02-Sep-16	
M1810	SUCF MS2a: Fire Alarm: Bed Tower 6-9 (N/R)	0	0	0	0%	-27				15-Sep-16	21-Oct-16	
M1050	Punch-list	58	58	0	0%	-40	15-Sep-16	10-Nov-16		06-Dec-16	31-Jan-17	
M1040	SUCF MS5: Completion (6DEC16)	0	0	0	0%	-40				06-Dec-16	31-Jan-17	
Milestones												
Project Deliverables												
General												
FBO Equipment Schedules												
B2510	Owner Equipment schedule: preliminary	5	1	67	80%	-28		03-Jul-15	16-Feb-15	22-May-15	03-Jul-15	
B2810	Owner Equipment schedule: final	5	1	67	80%	-28		06-Jul-15	16-Feb-15	22-May-15	06-Jul-15	
Fabrication												
General												
Work by Owner												
B2830	FBO Minor Medical Equipment on-site	0	0	0	0%	-28				06-Nov-15	21-Dec-15	
Construction												
General												
Work by Owner												
M1820	Provide tie-in to COMMS/FA back-bone head-end	10	8	25	25%	153	09-Apr-15	20-May-15	15-Apr-15		29-May-15	
Pre-Construction												
Premobilization												
General												
General Requirements												
B2360	Owner kick-off meeting	1	0	0	100%		06-Apr-15	20-May-15	12-Nov-14	06-Apr-15	20-May-15	12-Nov-14
B2480	Subcontractor Kick Off Meeting	1	0	0	100%		06-Apr-15	20-May-15	03-Feb-15	06-Apr-15	20-May-15	03-Feb-15
B2490	Subcontractor Safety Orientation (first-in)	15	8	71	45%	-89	06-Apr-15	20-May-15	10-Feb-15	16-Apr-15	01-Jun-15	
B1090	LEED review	30	27	5	10%	8	06-Apr-15	20-May-15	13-May-15	14-May-15	25-Jun-15	
B2570	Site Logistics Plan/Subcontractor Trailer Mobilization	30	0	0	100%		16-Apr-15	01-Jun-15	27-Oct-14	16-Apr-15	01-Jun-15	27-Oct-14
Master Schedule												
SCH1000	Set-up data base	10	0	5	100%		06-Apr-15	20-May-15	11-Nov-14	06-Apr-15	20-May-15	18-Nov-14
SCH1010	Structure layout	5	0	2	100%		06-Apr-15	20-May-15	18-Nov-14	06-Apr-15	20-May-15	20-Nov-14
SCH1020	Activities & Relationships	20	0	20	100%		06-Apr-15	20-May-15	21-Nov-14	06-Apr-15	20-May-15	19-Dec-14
SCH1060	Final CPM issue to CM	8	0	6	100%		06-Apr-15	20-May-15	04-Mar-15	06-Apr-15	20-May-15	12-Mar-15
SCH1040	Preliminary CPM to CM	0	0	0	100%		06-Apr-15	20-May-15	24-Feb-15			

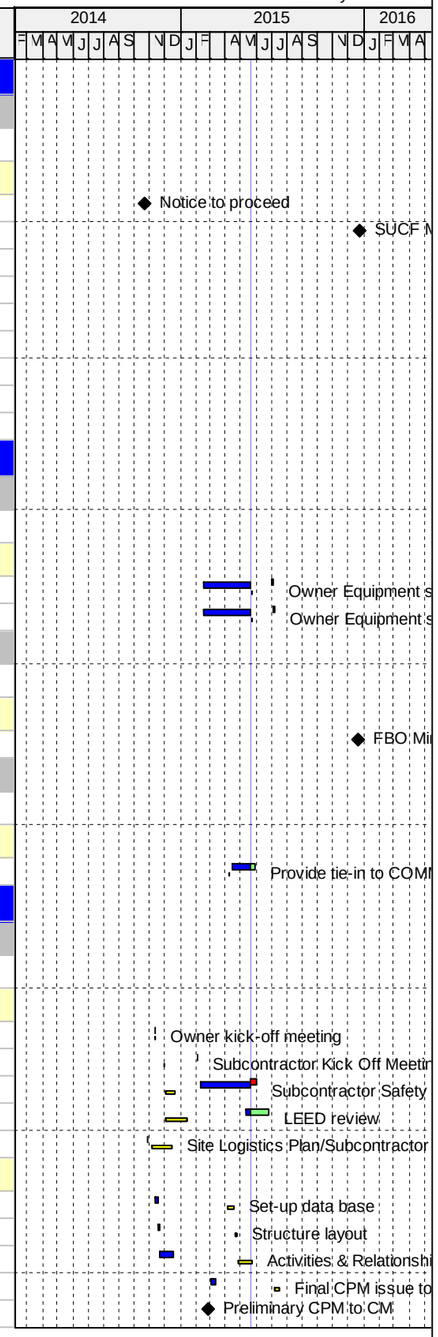

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
SCH1030	Incorporate major trade schedules into master schedule	42	0	37	100%		06-Apr-15	20-May-15	02-Jan-15	06-Apr-15	20-May-15	24-Feb-15
SCH1050	Incorporate second tier trade & equipment schedules into master schedu	5	0	21	100%		06-Apr-15	20-May-15	26-Jan-15	06-Apr-15	20-May-15	24-Feb-15
SCH1070	CPM Approval	5	0	14	100%		06-Apr-15	20-May-15	13-Mar-15	06-Apr-15	20-May-15	02-Apr-15
Sub-Contractor Schedules												
SC1010	Carpentry/GWB Partitions schedule	0	0	0	100%					06-Apr-15	20-May-15	05-Mar-15
SC1030	HVAC schedule	0	0	0	100%					06-Apr-15	20-May-15	17-Dec-14
SC1040	Electrical schedule	0	0	0	100%					06-Apr-15	20-May-15	26-Dec-14
SC1050	Plumbing schedule	0	0	0	100%					06-Apr-15	20-May-15	09-Dec-14
SC1000	Fire Suppression schedule	0	0	0	100%					06-Apr-15	20-May-15	23-Dec-14
SC1080	Low-voltage Systems schedule	0	0	0	100%					06-Apr-15	20-May-15	26-Dec-14
FBO Equipment Schedules												
FBO1000	Kick Off Meeting - Hospital Equipment Review/Verification	20	18	35	10%	8	14-May-15	26-Jun-15	01-Apr-15	11-Jun-15	21-Jul-15	
FBO1010	Architectural Review of OFCI	21	21	0	0%	8	14-May-15	26-Jun-15		12-Jun-15	24-Jul-15	
FBO1020	Development of OFCI Schedule - Procurement/Delivery	60	0	23	100%		12-Jun-15	24-Jul-15	02-Mar-15	12-Jun-15	24-Jul-15	02-Apr-15
FBO1030	Development of CFCI Schedule - Procurement/Delivery	60	0	23	100%		12-Jun-15	24-Jul-15	02-Mar-15	12-Jun-15	24-Jul-15	02-Apr-15
FBO1040	Subcontractor Coordination of OFCI/CFCI Equipment	30	30	0	0%	326	12-Jun-15	27-Jul-15		24-Jul-15	04-Sep-15	
Owner Commissioning/LEED Kick Off Meeting												
B2790	Commissioning Kick Off	1	1	0	0%	399	06-Apr-15	20-May-15		06-Apr-15	20-May-15	
B2800	A/E LEED Kick Off (NOT LINKED)	5	5	0	0%	399	06-Apr-15	20-May-15		10-Apr-15	26-May-15	
Procurement												
General												
Buy-outs												
PROC1050	Carpentry buy-out	0	0	0	100%					06-Apr-15	20-May-15	06-Feb-15
PROC1060	Masonry buy-out	0	0	0	100%					06-Apr-15	20-May-15	20-Mar-15
PROC1110	Wood doors buy-out	0	0	0	100%					06-Apr-15	20-May-15	13-Feb-15
PROC1070	HVAC buy-out	0	0	0	100%					06-Apr-15	20-May-15	16-Dec-14
PROC1080	Electrical buy-out	0	0	0	100%					06-Apr-15	20-May-15	16-Dec-14
PROC1090	Plumbing buy-out	0	0	0	100%					06-Apr-15	20-May-15	16-Dec-14
PROC1000	Fire Suppression buy-out	0	0	0	100%					06-Apr-15	20-May-15	16-Dec-14
PROC1150	Ornamental Metal buy-out	0	0	0	100%					06-Apr-15	20-May-15	31-Mar-15
PROC1120	HCM Doors buy-out	0	0	0	100%					06-Apr-15	20-May-15	13-Feb-15
PROC1130	Low-voltage Systems buy-out	0	0	0	100%					06-Apr-15	20-May-15	16-Dec-14
PROC1100	Pneumatic tube system buy-out	0	0	0	100%					06-Apr-15	20-May-15	29-Dec-14
PROC1040	GFRC buy-out	0	0	0	100%					06-Apr-15	20-May-15	06-Feb-15
PROC1270	Structural Steel buy-out	21	0	0	100%		06-Apr-15	20-May-15	06-Apr-15	06-Apr-15	20-May-15	06-Apr-15
PROC1280	Alertron buy-out	0	0	0	100%					06-Apr-15	20-May-15	16-Dec-14
PROC1160	Interior Glazing buy-out	0	0	0	0%	6				06-Apr-15	20-May-15	
PROC1170	Epoxy Flooring buy-out	0	0	0	0%	23				06-Apr-15	20-May-15	
PROC1180	Resilient Flooring buy-out	21	21	0	0%	35	15-Apr-15	20-May-15		13-May-15	17-Jun-15	
PROC1190	DIV 10 Accessories buy-out	0	0	0	0%	-32				06-Apr-15	20-May-15	
PROC1140	Radiation protection buy-out	0	0	0	0%	68				06-Apr-15	20-May-15	
PROC1010	Concrete buy-out	0	0	0	0%	66				06-Apr-15	20-May-15	
PROC1020	Manufactured casework buy-out	0	0	0	0%	17				06-Apr-15	20-May-15	
PROC1030	Interior Storefront buy-outs	0	0	0	0%	4				06-Apr-15	20-May-15	
PROC1200	Painting buy-out	0	0	0	0%	45				06-Apr-15	20-May-15	
PROC1210	Exterior Improvement buy-out	0	0	0	0%	47				06-Apr-15	20-May-15	

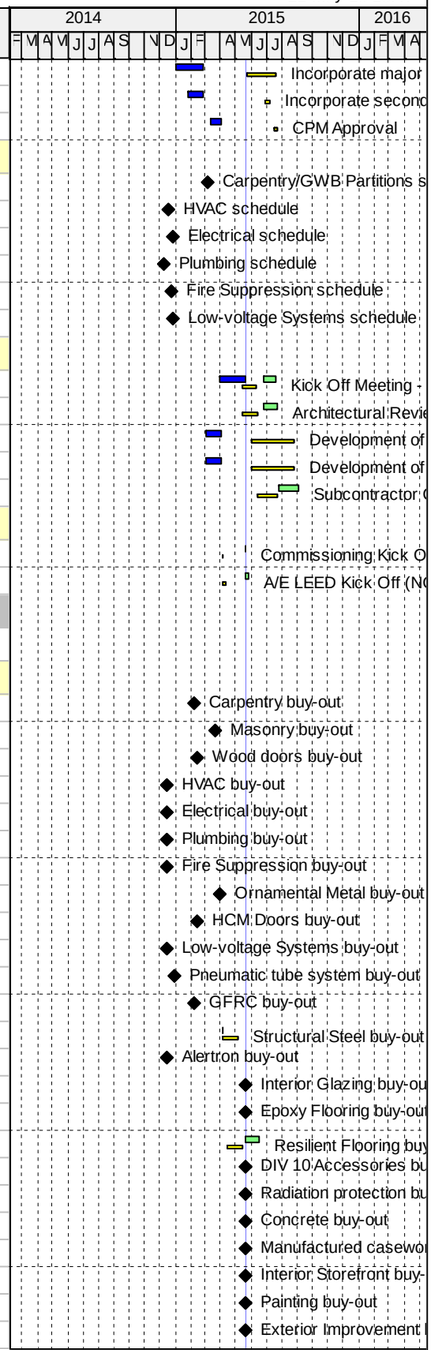

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
PROC1220	Landscaping buy-out	0	0	0	0%	47				06-Apr-15	20-May-15	
PROC1230	MRI shielding buy-out	0	0	0	0%	26				06-Apr-15	20-May-15	
PROC1240	Wood flooring buy-out	0	0	0	0%	128				06-Apr-15	20-May-15	
PROC1250	Carpet buy-out	0	0	0	0%	-5				06-Apr-15	20-May-15	
PROC1260	ACM buy-out	0	0	0	0%	6				06-Apr-15	20-May-15	
PROC1290	Environmental Control Room buy-out	0	0	0	0%	16				06-Apr-15	20-May-15	
Submittals & Approvals												
SUBM1005	SOV Preparation/Submittal	30	0	31	100%		06-Apr-15	20-May-15	16-Feb-15	06-Apr-15	20-May-15	31-Mar-15
SUBM1015	SOV Review Approval	5	0	25	100%		06-Apr-15	20-May-15	24-Feb-15	06-Apr-15	20-May-15	31-Mar-15
Laboratory Equipment												
B1040	Owner Medical Equipment buyout	30	27	25	10%	-28	06-Apr-15	20-May-15	15-Apr-15	15-May-15	25-Jun-15	
B3870	Owner Medical FF&E buyout	30	21	25	30%	-15	06-Apr-15	20-May-15	15-Apr-15	15-May-15	17-Jun-15	
Submittals & Approvals												
General												
General Requirements												
B1030	Retain Scheduler	0	0	0	100%					06-Apr-15	20-May-15	12-Dec-14
Abatement												
SUBM1900	ACM submittals	30	30	0	0%	6	29-Jun-15	12-Aug-15		07-Aug-15	22-Sep-15	
SUBM1910	ACM review	60	60	0	0%	6	10-Aug-15	23-Sep-15		30-Oct-15	15-Dec-15	
Concrete												
SUBM1360	Concrete submittals	20	20	0	0%	66	15-Jun-15	29-Jul-15		10-Jul-15	25-Aug-15	
SUBM1420	Concrete review	30	30	0	0%	66	13-Jul-15	26-Aug-15		21-Aug-15	06-Oct-15	
Masonry												
SUBM1620	Masonry submittals	20	20	0	0%	-3	06-Apr-15	20-May-15		01-May-15	16-Jun-15	
SUBM1430	Masonry review	30	30	0	0%	-3	04-May-15	17-Jun-15		12-Jun-15	28-Jul-15	
Structural Steel												
SUBM1920	Structural steel submittals	20	15	20	25%	-7	17-Apr-15	20-May-15	22-Apr-15	14-May-15	09-Jun-15	
SUBM1930	Structural steel review	30	30	0	0%	-17	10-Apr-15	20-May-15		21-May-15	30-Jun-15	
Steel Stairs												
SUBM2240	Stair submittals	20	10	19	50%	-12	06-Apr-15	20-May-15	23-Apr-15	01-May-15	02-Jun-15	
SUBM2250	Stair review	30	30	0	0%	-12	20-Apr-15	20-May-15		29-May-15	30-Jun-15	
Metal Composite Panels												
SUBM2150	Column enclosures submittals	20	20	0	0%	-51	06-Apr-15	30-Jun-15		01-May-15	27-Jul-15	
SUBM2160	Column enclosures review	30	30	0	0%	-51	04-May-15	28-Jul-15		12-Jun-15	07-Sep-15	
Ornamental Handrails and Railings												
SUBM1340	Ornamental Metal submittals	20	20	0	0%	38	19-Aug-15	19-Aug-15		15-Sep-15	15-Sep-15	
SUBM1410	Ornamental Metal review	30	30	0	0%	38	16-Sep-15	16-Sep-15		27-Oct-15	27-Oct-15	
Carpentry												
SUBM1630	Carpentry submittals	20	10	85	50%	-65	06-Apr-15	20-May-15	21-Jan-15	24-Apr-15	02-Jun-15	
SUBM1640	Carpentry review	15	11	76	25%	-65	27-Apr-15	03-Jun-15	03-Feb-15	12-May-15	18-Jun-15	
Hollow Metal Doors												
SUBM1090	HCM door submittals	20	0	21	100%		06-Apr-15	20-May-15	25-Mar-15	07-Apr-15	20-May-15	23-Apr-15
SUBM1180	HCM door review	15	15	0	0%	44	08-Apr-15	20-May-15		28-Apr-15	09-Jun-15	
Wood Doors												

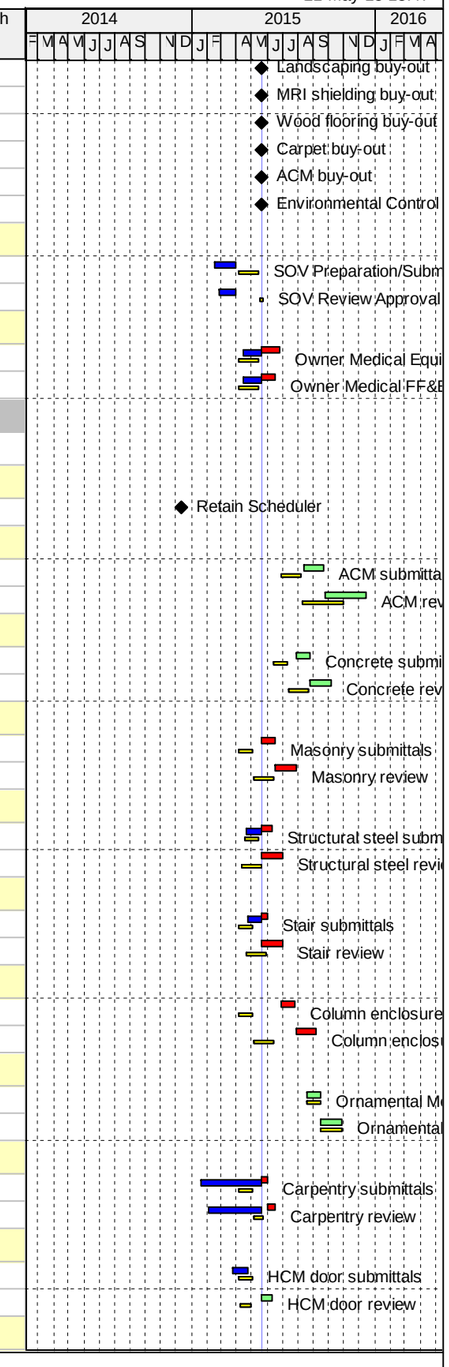

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
SUBM1100	Wood Doors submittals	20	0	21	100%		06-Apr-15	20-May-15	25-Mar-15	07-Apr-15	20-May-15	23-Apr-15
SUBM1190	Wood Doors review	15	15	0	0%	60	08-Apr-15	20-May-15		28-Apr-15	09-Jun-15	
Specialty Doors & Frames												
SUBM1690	ICU door assembly submittals	20	20	0	0%	8	12-Jun-15	27-Jul-15		10-Jul-15	21-Aug-15	
SUBM1700	ICU door assembly review	30	30	0	0%	8	10-Jul-15	24-Aug-15		21-Aug-15	02-Oct-15	
Overhead Coiling Doors												
SUBM2080	Overhead coiling door submittals	20	20	0	0%	-27	06-Apr-15	20-May-15		01-May-15	16-Jun-15	
SUBM2090	Overhead coiling door review	30	30	0	0%	-27	04-May-15	17-Jun-15		12-Jun-15	28-Jul-15	
Door Hardware												
SUBM2180	Door hardware submittals	20	2	47	90%	50	06-Apr-15	20-May-15	16-Mar-15	07-Apr-15	21-May-15	
SUBM2190	Door hardware review	30	27	42	10%	50	08-Apr-15	22-May-15	23-Mar-15	14-May-15	29-Jun-15	
Aluminum Storefront												
SUBM1310	Interior Storefront submittals	20	20	0	0%	4	20-May-15	03-Jul-15		16-Jun-15	30-Jul-15	
SUBM1390	Interior Storefront review	30	30	0	0%	4	17-Jun-15	31-Jul-15		28-Jul-15	10-Sep-15	
Light-gauge Metal Framing												
SUBM1040	Gypsum Board Assembly submittals	20	0	9	100%		06-Apr-15	20-May-15	21-Jan-15	06-Apr-15	20-May-15	03-Feb-15
SUBM1110	Gypsum Board Assembly review	30	24	79	20%	52	06-Apr-15	20-May-15	29-Jan-15	07-May-15	22-Jun-15	
Acoustical Wall & Ceiling Panels												
SUBM1860	Acoustical wall panels submittals	20	10	42	50%	90	16-Nov-15	16-Nov-15	23-Mar-15	11-Dec-15	27-Nov-15	
SUBM1870	Acoustical wall panels review	30	15	24	50%	90	14-Dec-15	30-Nov-15	16-Apr-15	22-Jan-16	18-Dec-15	
Suspended Acoustical Ceiling												
SUBM1200	ACT submittals	20	17	73	15%	45	06-Apr-15	20-May-15	06-Feb-15	28-Apr-15	11-Jun-15	
SUBM1270	ACT review	30	30	53	0%	45	29-Apr-15	12-Jun-15	06-Mar-15	09-Jun-15	23-Jul-15	
Finish Carpentry: Casework, Paneling & Trims												
SUBM1840	Finish carpentry submittals	20	11	53	45%	145	05-Aug-15	20-May-15	06-Mar-15	01-Sep-15	03-Jun-15	
SUBM1850	Finish carpentry review	30	24	45	20%	145	02-Sep-15	04-Jun-15	18-Mar-15	13-Oct-15	07-Jul-15	
Painting												
SUBM1400	Painting submittals	20	20	0	0%	77	13-Aug-15	13-Aug-15		09-Sep-15	09-Sep-15	
SUBM1440	Painting review	30	30	0	0%	77	10-Sep-15	10-Sep-15		21-Oct-15	21-Oct-15	
GFRC												
SUBM1260	GFRC submittals	20	20	0	0%	38	19-Oct-15	19-Oct-15		13-Nov-15	13-Nov-15	
SUBM1370	GFRC review	30	30	0	0%	38	16-Nov-15	16-Nov-15		25-Dec-15	25-Dec-15	
Wall Coverings												
SUBM2200	Wall covering submittals	20	20	0	0%	45	06-Apr-15	20-May-15		01-May-15	16-Jun-15	
SUBM2210	Wall covering review	30	30	0	0%	45	04-May-15	17-Jun-15		12-Jun-15	28-Jul-15	
Interior Glazing												
SUBM1290	Interior Glazing submittals	20	20	0	0%	6	05-May-15	18-Jun-15		01-Jun-15	15-Jul-15	
SUBM1450	Interior Glazing review	30	30	0	0%	6	25-Aug-15	08-Oct-15		05-Oct-15	18-Nov-15	
Carpet												
SUBM1880	Carpet submittals	20	20	0	0%	-5	06-Apr-15	15-Jun-15		01-May-15	10-Jul-15	
SUBM1890	Carpet review	30	30	0	0%	-5	04-May-15	13-Jul-15		12-Jun-15	21-Aug-15	
Resilient Flooring & Carpeting												
SUBM1250	Resilient Flooring submittals	20	20	0	0%	35	01-Jun-15	15-Jun-15		26-Jun-15	10-Jul-15	
SUBM1330	Resilient Flooring review	30	30	0	0%	35	29-Jun-15	13-Jul-15		07-Aug-15	21-Aug-15	

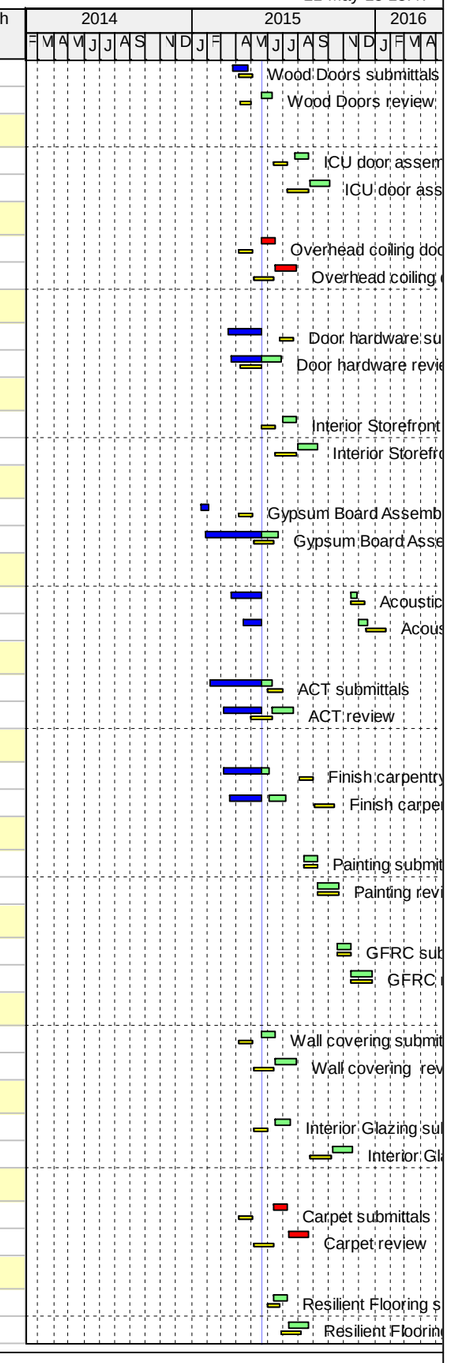

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
Ceramic Tile												
SUBM1580	Ceramic tile submittals	20	20	0	0%	23	06-Apr-15	15-Jun-15		01-May-15	10-Jul-15	
SUBM1590	Ceramic tile review	30	30	0	0%	23	04-May-15	13-Jul-15		12-Jun-15	21-Aug-15	
Terrazzo Flooring												
SUBM1220	Terrazzo Flooring submittals	20	20	0	0%	98	10-Aug-15	15-Jun-15		04-Sep-15	10-Jul-15	
SUBM1280	Terrazzo Flooring review	30	30	0	0%	98	07-Sep-15	13-Jul-15		16-Oct-15	21-Aug-15	
Wood Flooring												
SUBM1820	Wood flooring submittals	20	20	0	0%	128	21-Sep-15	15-Jun-15		16-Oct-15	10-Jul-15	
SUBM1830	Wood flooring review	30	30	0	0%	128	19-Oct-15	13-Jul-15		27-Nov-15	21-Aug-15	
Epoxy Flooring												
SUBM2060	Epoxy Flooring submittals	20	20	0	0%	117	10-Aug-15	15-Jun-15		04-Sep-15	10-Jul-15	
SUBM2070	Epoxy Flooring review	30	30	0	0%	117	07-Sep-15	13-Jul-15		16-Oct-15	21-Aug-15	
Specialties/Accessories												
SUBM1320	Operable Partition submittals	20	20	0	0%	-12	06-Apr-15	01-Jun-15		01-May-15	26-Jun-15	
SUBM2280	Operable Partition review	30	30	0	0%	-12	04-May-15	29-Jun-15		12-Jun-15	07-Aug-15	
SUBM2260	HD Shelving submittals	20	20	0	0%	-32	06-Apr-15	19-Aug-15		01-May-15	15-Sep-15	
SUBM1300	Accessories submittals	20	20	0	0%	36	08-Jul-15	21-Aug-15		04-Aug-15	17-Sep-15	
SUBM2270	HD Shelving review	30	30	0	0%	-32	04-May-15	16-Sep-15		12-Jun-15	27-Oct-15	
SUBM1380	Accessories review	30	30	0	0%	36	05-Aug-15	18-Sep-15		15-Sep-15	29-Oct-15	
Manufactured Casework												
SUBM1120	Manufactured Casework submittals	20	20	53	0%	17	20-Apr-15	03-Jun-15	06-Mar-15	15-May-15	30-Jun-15	
SUBM1210	Manufactured Casework review	30	30	45	0%	17	18-May-15	01-Jul-15	18-Mar-15	26-Jun-15	11-Aug-15	
Controlled Environment Rooms												
SUBM2120	Environmental Control Room submittals	20	20	0	0%	16	06-Apr-15	20-May-15		01-May-15	16-Jun-15	
SUBM2130	Environmental Control Room review	30	30	0	0%	16	04-May-15	17-Jun-15		12-Jun-15	28-Jul-15	
Radiation Protection												
SUBM1130	Radiation protection submittals	20	20	0	0%	68	04-May-15	01-Jun-15		29-May-15	26-Jun-15	
SUBM1230	Radiation protection review	30	30	0	0%	68	01-Jun-15	29-Jun-15		10-Jul-15	07-Aug-15	
Environmental Shielding												
SUBM1780	MRI shielding submittals	20	20	0	0%	26	06-Apr-15	01-Jun-15		01-May-15	26-Jun-15	
SUBM1790	MRI shielding review	30	30	0	0%	26	04-May-15	29-Jun-15		12-Jun-15	07-Aug-15	
Pneumatic Tube Systems												
SUBM1070	Pneumatic tube system submittals	20	18	55	10%	-7	06-Apr-15	20-May-15	04-Mar-15	29-Apr-15	12-Jun-15	
SUBM1160	Pneumatic tube system review	30	30	0	0%	-7	30-Apr-15	15-Jun-15		10-Jun-15	24-Jul-15	
Wet Standpipe System Piping												
SUBM1010	Wet Fire Suppression submittals	20	5	116	75%	-65	06-Apr-15	20-May-15	09-Dec-14	14-Apr-15	26-May-15	
SUBM1030	Wet Fire Suppression review	15	4	98	75%	39	15-Apr-15	27-May-15	02-Jan-15	23-Apr-15	01-Jun-15	
Clean-Agent Fire Suppression												
SUBM1720	Clean-agent Fire Suppression submittals	20	5	43	75%	38	06-Apr-15	20-May-15	20-Mar-15	20-Apr-15	26-May-15	
SUBM1730	Clean-agent Fire Suppression review	15	4	31	75%	38	21-Apr-15	27-May-15	07-Apr-15	11-May-15	01-Jun-15	
Plumbing												
SUBM1080	Plumbing submittals	20	18	78	10%	-65	06-Apr-15	20-May-15	30-Jan-15	29-Apr-15	12-Jun-15	
SUBM1170	Plumbing review	15	14	65	10%	61	24-Apr-15	09-Jun-15	18-Feb-15	13-May-15	26-Jun-15	
General Requirements for Mechanical Work												

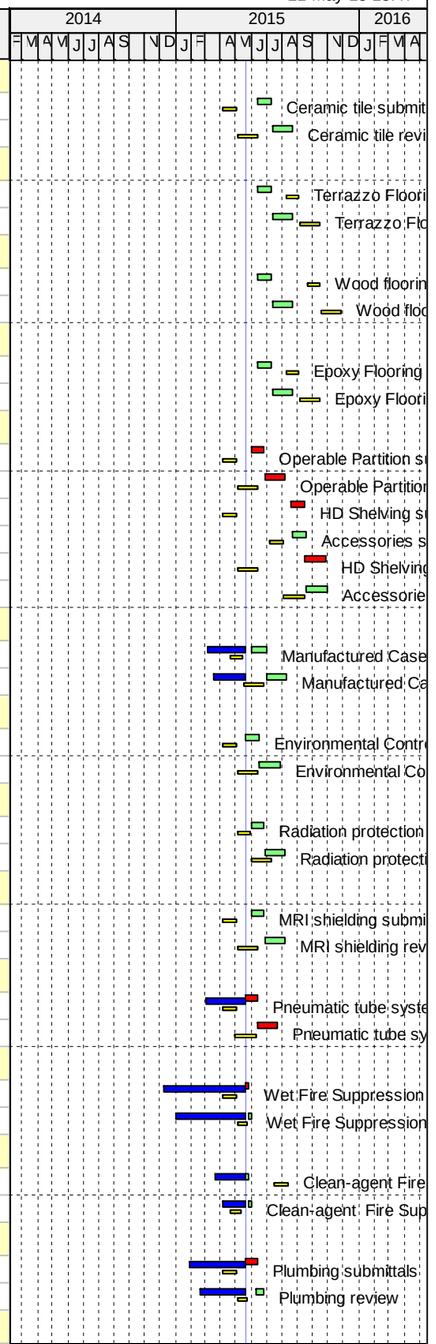

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
SUBM1460	MEP Coordination	40	40	0	0%	-76	25-May-15	04-Jun-15		20-Jul-15	30-Jul-15	
Hydronic Piping												
SUBM1000	HW/CHW/S/R/CD submittals	20	16	53	20%	-65	06-Apr-15	20-May-15	06-Mar-15	29-Apr-15	10-Jun-15	
SUBM1020	HW/CHW/S/R/CD review	15	12	53	20%	68	30-Apr-15	11-Jun-15	06-Mar-15	20-May-15	26-Jun-15	
Steam & Condensate Piping												
SUBM1800	Steam/condensate submittals	20	15	53	25%	20	06-Apr-15	20-May-15	06-Mar-15	01-May-15	09-Jun-15	
SUBM1810	Steam/condensate review	15	11	35	25%	20	04-May-15	10-Jun-15	01-Apr-15	22-May-15	25-Jun-15	
HVAC Ductwork												
SUBM1050	Ductwork shop drawings	20	14	131	30%	-92	06-Apr-15	20-May-15	18-Nov-14	27-Apr-15	08-Jun-15	
SUBM1140	Ductwork review	15	11	120	25%	-92	28-Apr-15	09-Jun-15	03-Dec-14	14-May-15	24-Jun-15	
HVAC Equipment												
SUBM1470	HVAC Equipment submittals	20	10	132	50%	-17	06-Apr-15	20-May-15	15-Nov-14	01-May-15	02-Jun-15	
SUBM1480	HVAC Equipment review	15	8	97	45%	-17	04-May-15	03-Jun-15	05-Jan-15	22-May-15	15-Jun-15	
HVAC DDC & Secondary Controls												
SUBM1510	HVAC control wiring diagram submittals	30	0	24	99%	-5	06-Apr-15	20-May-15	16-Apr-15	15-May-15	20-May-15	
SUBM1520	HVAC control wiring diagram review	15	15	0	0%	-5	18-May-15	28-May-15		05-Jun-15	17-Jun-15	
Conduits, Troughs, Boxes and Fittings												
SUBM1060	Basic Electrical submittals	20	6	113	70%	-65	06-Apr-15	20-May-15	12-Dec-14	01-May-15	27-May-15	
SUBM1150	Basic Electrical review	15	8	83	50%	-7	04-May-15	28-May-15	23-Jan-15	22-May-15	08-Jun-15	
Electrical Light Fixtures												
SUBM1960	Lighting fixture submittals	20	5	12	75%	5	04-May-15	28-May-15	04-May-15	29-May-15	03-Jun-15	
SUBM1350	Lighting fixture review	30	30	0	0%	5	01-Jun-15	04-Jun-15		10-Jul-15	15-Jul-15	
Packaged Generators												
SUBM1560	Generator submittals	20	0	45	100%		06-Apr-15	20-May-15	26-Jan-15	06-Apr-15	20-May-15	30-Mar-15
SUBM1570	Generator review	15	0	45	100%		06-Apr-15	20-May-15	04-Feb-15	06-Apr-15	20-May-15	08-Apr-15
UPS												
SUBM1970	UPS submittals	20	0	26	100%		24-Apr-15	20-May-15	19-Jan-15	24-Apr-15	20-May-15	24-Feb-15
SUBM1980	UPS review	15	15	40	0%	-18		20-May-15	25-Mar-15		09-Jun-15	
Lighting Control Systems												
SUBM1740	Lighting control submittals	20	20	0	0%	-12	06-Apr-15	20-May-15		01-May-15	16-Jun-15	
SUBM1750	Lighting control review	15	15	0	0%	-12	04-May-15	17-Jun-15		22-May-15	07-Jul-15	
Fire Detection and Alarm System												
SUBM1530	Fire alarm submittals	20	10	61	50%	-22	06-Apr-15	20-May-15	24-Feb-15	01-May-15	02-Jun-15	
SUBM1540	Fire alarm review	15	12	40	20%	-22	04-May-15	03-Jun-15	25-Mar-15	22-May-15	18-Jun-15	
Alerton Systems												
SUBM2000	Alertron/DDC submittals	60	1	24	99%	31	06-Apr-15	20-May-15	16-Apr-15	26-Jun-15	20-May-15	
SUBM2010	Alertron/DDC review	15	15	0	0%	31	29-Jun-15	20-May-15		17-Jul-15	10-Jun-15	
Communications (work-by-owner)												
Security & Access Control (work-by-owner)												
Exterior Improvements												
SUBM1760	Landscaping submittals	20	20	0	0%	47	03-Feb-16	18-Mar-16		01-Mar-16	14-Apr-16	
SUBM1770	Landscaping review	30	30	0	0%	47	02-Mar-16	15-Apr-16		12-Apr-16	26-May-16	
General Construction												

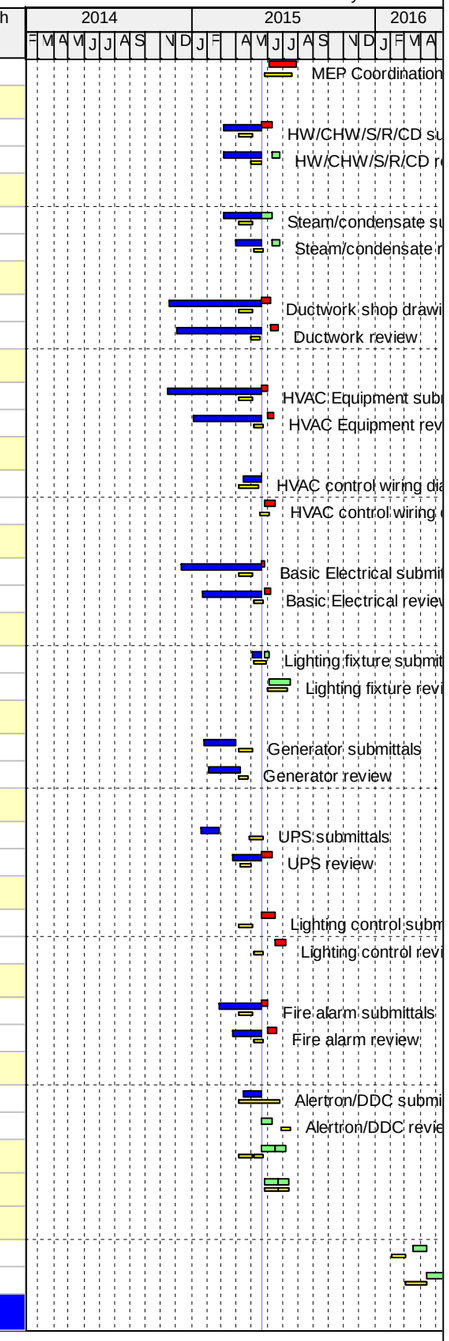

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
Fabrication												
MART Building												
Steel Stairs												
FABM1040	Greeter Stair fabrication	60	60	0	0%	16	01-Jun-15	01-Jul-15		21-Aug-15	22-Sep-15	
Aluminum Storefront												
FABM1060	Interior Storefront fabrication & Delivery Window MART	60	60	0	0%	4	29-Jul-15	11-Sep-15		20-Oct-15	03-Dec-15	
Laboratory Equipment												
FABM1020	FBO Medical FF&E fabrication and delivery window MART	120	120	0	0%	-28	25-May-15	07-Jul-15		06-Nov-15	21-Dec-15	
Medical Equipment: Major												
FABM1110	FBO PET Scan fabrication and delivery window: MART	120	120	0	0%	9	18-May-15	26-Jun-15		30-Oct-15	10-Dec-15	
FABM1010	FBO Cyclotron fabrication and delivery window: MART	90	90	0	0%	-3	25-May-15	07-Jul-15		25-Sep-15	09-Nov-15	
Manufactured Casework												
FABM1090	Manufactured Casework fabrication and delivery window MART	90	90	0	0%	17	10-Aug-15	23-Sep-15		11-Dec-15	26-Jan-16	
HVAC Ductwork												
FABM1000	Fabricate ductwork, MART	113	96	98	15%	-92	25-May-15	09-Jun-15	02-Jan-15	16-Oct-15	20-Oct-15	
HVAC Equipment												
FABM1050	HVAC Equipment fabrication & delivery, MART	113	56	30	50%	42	25-May-15	15-Jun-15	08-Apr-15	28-Oct-15	01-Sep-15	
Electrical Light Fixtures												
FABM1080	Lighting fixture fabrication & delivery, MART	120	120	0	0%	5	13-Jul-15	16-Jul-15		25-Dec-15	30-Dec-15	
Lighting Control Systems												
FABM1070	Lighting control system fabrication & delivery, MART	120	120	0	0%	28	17-Aug-15	30-Sep-15		29-Jan-16	15-Mar-16	
Fire Detection and Alarm System												
FABM1030	Fire Alarm system fabrication & delivery, MART	90	90	0	0%	16	25-May-15	19-Jun-15		25-Sep-15	22-Oct-15	
Bed Tower												
Steel Stairs												
FABBT1000	Circular stair fabrication	90	90	0	0%	-12	01-Jun-15	01-Jul-15		02-Oct-15	03-Nov-15	
Aluminum Storefront												
FABBT1060	Interior Storefront fabrication & Delivery Window Bed Tower	120	120	0	0%	21	29-Jul-15	11-Sep-15		12-Jan-16	25-Feb-16	
Laboratory Equipment												
FABBT1030	FBO Medical FF&E fabrication and delivery window: Bed Tower	120	120	0	0%	11	10-Aug-15	18-Sep-15		22-Jan-16	03-Mar-16	
Medical Equipment: Major												
FABM1100	FBO MRI 3T fabrication and delivery window	120	120	0	0%	-21	18-May-15	26-Jun-15		30-Oct-15	10-Dec-15	
FABM1120	FBO MRI 1.5T fabrication and delivery window	120	120	0	0%	-21	18-May-15	26-Jun-15		30-Oct-15	10-Dec-15	
HVAC Ductwork												
FABBT1010	Fabricate ductwork, Bed Tower	90	90	0	0%	-81	25-Jun-15	25-Jun-15		29-Oct-15	29-Oct-15	
HVAC Equipment												
FABBT1050	HVAC Equipment fabrication & delivery, Bed Tower	94	94	0	0%	-17	25-May-15	15-Jun-15		01-Oct-15	22-Oct-15	
Electrical Light Fixtures												
FABBT1080	Lighting fixture fabrication & delivery, Bed Tower (inc. Specialty Fixtures)	90	90	0	0%	7	13-Jul-15	16-Jul-15		13-Nov-15	18-Nov-15	
Lighting Control Systems												
FABBT1070	Lighting control system fabrication & delivery, Bed Tower	60	60	0	0%	-12	31-Aug-15	14-Oct-15		20-Nov-15	05-Jan-16	
Fire Detection and Alarm System												

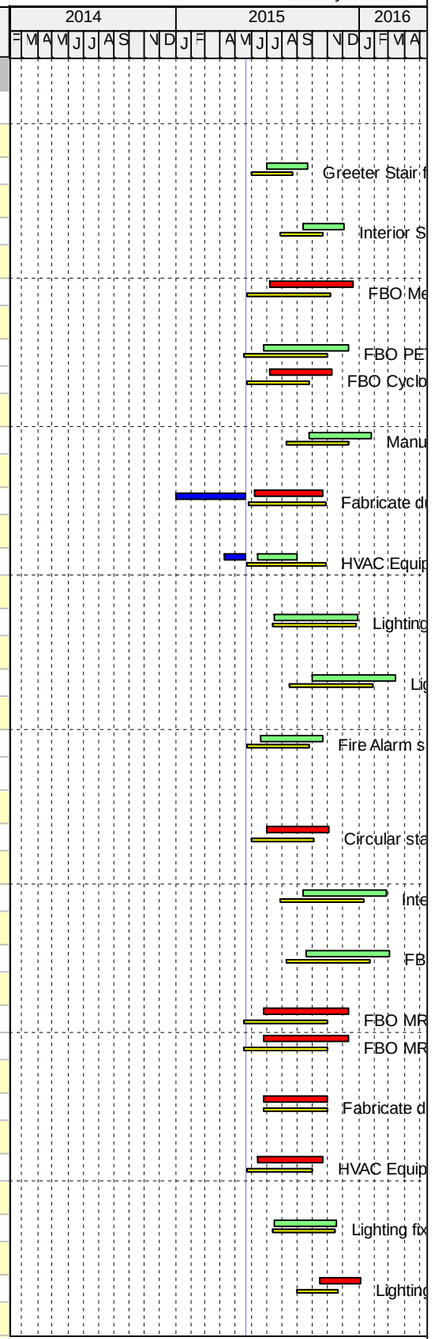

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
FABBT1040	Fire Alarm system fabrication & delivery, Bed Tower	90	90	0	0%	-22	06-Jul-15	31-Jul-15		06-Nov-15	03-Dec-15	
Canopy												
Structural Steel												
GENFAB10	Canopy steel fabrication & delivery	90	90	0	0%	38	03-Jul-15	12-Aug-15		05-Nov-15	15-Dec-15	
Generator Building												
Structural Steel												
GNTRFAB1	Generator house fabrication & delivery	60	60	0	0%	-17	22-May-15	01-Jul-15		13-Aug-15	22-Sep-15	
Packaged Generators												
GNTRFAB1	Mechanical Generator fabrication & delivery	90	90	0	0%	-7	06-Apr-15	20-May-15		07-Aug-15	22-Sep-15	
GNTRFAB1	Electrical Generator fabrication & delivery	90	72	75	20%	12	06-Apr-15	20-May-15	04-Feb-15	14-Jul-15	27-Aug-15	
General												
Ornamental Handrails and Railings												
GENFAB11	Ornamental Metal Fabrication	90	90	0	0%	33	28-Oct-15	04-Nov-15		01-Mar-16	08-Mar-16	
Specialty Doors & Frames												
GENFAB10	ICU door assembly fabrication & delivery	60	60	0	0%	8	02-Oct-15	16-Nov-15		25-Dec-15	05-Feb-16	
Overhead Coiling Doors												
GENFAB11	Overhead Coiling Door fabrication & delivery	80	80	0	0%	-27	30-Nov-15	13-Jan-16		18-Mar-16	03-May-16	
Finish Carpentry: Casework, Paneling & Trims												
GENFAB10	Column enclosure fabrication & delivery	60	60	0	0%	-51	02-Nov-15	26-Jan-16		22-Jan-16	18-Apr-16	
Specialties/Accessories												
GENFAB10	Operable partition fabrication	40	40	0	0%	-12	19-Oct-15	14-Dec-15		11-Dec-15	05-Feb-16	
GENFAB10	High Density Shelving Fabrication	40	40	0	0%	-32	30-Nov-15	13-Apr-16		22-Jan-16	07-Jun-16	
Controlled Environment Rooms												
GENFAB10	Environmental Control Room fabrication & delivery	120	120	0	0%	16	29-Jun-15	12-Aug-15		11-Dec-15	26-Jan-16	
HVAC Equipment												
GENFAB10	Chiller fabrication & delivery, MART	113	113	0	0%	16	25-May-15	15-Jun-15		28-Oct-15	18-Nov-15	
HVAC DDC & Secondary Controls												
GENFAB10	DDC fabrication & delivery	130	130	0	0%	-5	08-Jun-15	18-Jun-15		04-Dec-15	16-Dec-15	
HVAC Grilles												
GENFAB10	Generator house louver fabrication	70	70	0	0%	43	06-Apr-15	20-May-15		10-Jul-15	25-Aug-15	
Motor Connections												
GENFAB11	Switchgear fabrication & delivery	101	101	0	0%	-7	25-May-15	08-Jun-15		12-Oct-15	27-Oct-15	
UPS												
GENFAB11	UPS fabrication & delivery	101	101	0	0%	-18	30-Apr-15	10-Jun-15		17-Sep-15	28-Oct-15	
Alerton Systems												
GENFAB10	Alertron fabrication & delivery	120	120	0	0%	31	20-Jul-15	10-Jun-15		01-Jan-16	25-Nov-15	
Construction												
MART Building												
General Requirements												
CON6340	C&S Concrete Deck & Fireproofing: MART 6	10	0	104	100%		06-Apr-15	20-May-15	05-Nov-14	06-Apr-15	20-May-15	31-Mar-15
Concrete												
CON6330	Concrete 5 MART	20	20	0	0%	16	16-Nov-15	16-Dec-15		11-Dec-15	12-Jan-16	

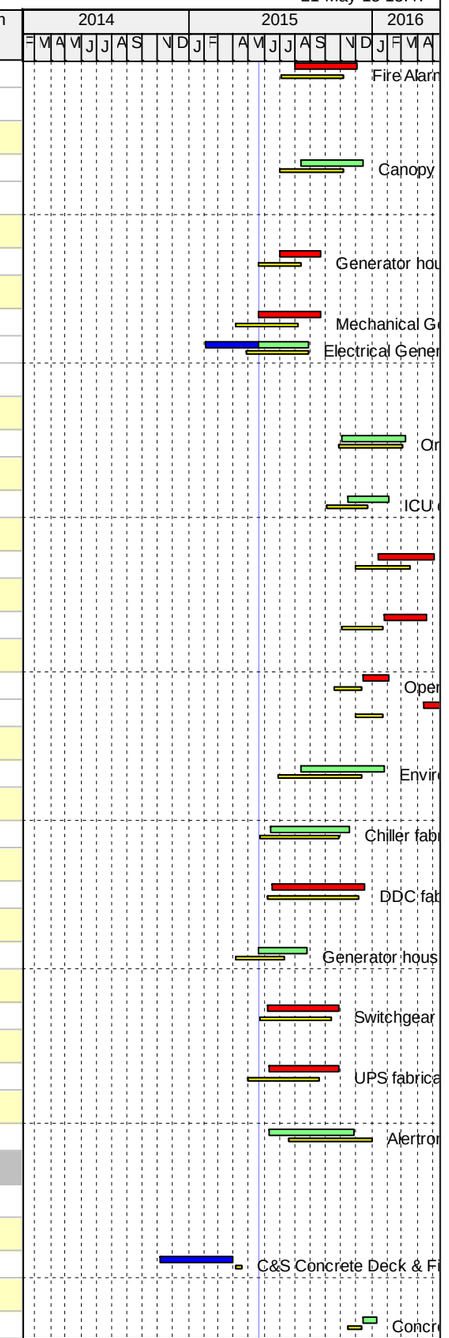

Remaining Level of Effort | Actual Level of Effort | Project Baseline Bar | Primary Baseline | Actual Work | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
CON6280	Concrete 6 MART	20	20	0	0%	16	16-Nov-15	16-Dec-15		11-Dec-15	12-Jan-16	
Masonry												
CON5520	CMU Partitions: 3 MART	20	20	0	0%	-3	26-Jun-15	11-Aug-15		24-Jul-15	08-Sep-15	
EQTIEM1490	CMU walls at Freezer Farm 3 MART	20	20	0	0%	-3	24-Jul-15	08-Sep-15		21-Aug-15	06-Oct-15	
Miscellaneous Metal												
MMETM1110	Millwork Steel Supports 7 MART	15	15	0	0%	62	27-Aug-15	30-Jul-15		17-Sep-15	19-Aug-15	
MMETM1050	Medical Equipment Slotted Framing Support 7 (ceiling)	30	30	0	0%	60	27-Aug-15	30-Jul-15		08-Oct-15	09-Sep-15	
MMETM1060	Medical Equipment Slotted Framing Support 8 (ceiling)	30	30	0	0%	68	22-Sep-15	13-Aug-15		03-Nov-15	23-Sep-15	
MMETM1120	Millwork Steel Supports 8 MART	10	10	0	0%	72	22-Sep-15	20-Aug-15		06-Oct-15	02-Sep-15	
MMETM1020	Medical Equipment Slotted Framing Support 4 (ceiling)	30	30	0	0%	-16	30-Sep-15	28-Aug-15		11-Nov-15	08-Oct-15	
MMETM1030	Medical Equipment Slotted Framing Support 5 (ceiling)	30	30	0	0%	13	01-Oct-15	31-Aug-15		12-Nov-15	09-Oct-15	
MMETM1130	Millwork Steel Supports 9 MART	10	10	0	0%	57	13-Oct-15	10-Sep-15		27-Oct-15	23-Sep-15	
MMETM1070	Medical Equipment Slotted Framing Support 9 (ceiling)	30	30	0	0%	57	13-Oct-15	10-Sep-15		24-Nov-15	21-Oct-15	
MMETM1010	Medical Equipment Slotted Framing Support 3 (ceiling)	30	30	0	0%	63	20-Oct-15	17-Sep-15		01-Dec-15	28-Oct-15	
MMETM1080	Millwork Steel Supports 4 MART	10	10	0	0%	-16	28-Oct-15	25-Sep-15		11-Nov-15	08-Oct-15	
MMETM1090	Millwork Steel Supports 5 MART	10	10	0	0%	-3	20-Nov-15	20-Oct-15		04-Dec-15	02-Nov-15	
MMETM1100	Millwork Steel Supports 6 MART	10	10	0	0%	-24	09-Oct-15	21-Oct-15		23-Oct-15	04-Nov-15	
MMETM1040	Medical Equipment Slotted Framing Support 6 (ceiling)	30	30	0	0%	-9	09-Oct-15	21-Oct-15		20-Nov-15	02-Dec-15	
MMETM1000	CMU Steel cornerguards 3 MART	5	5	0	0%	-2	10-Mar-16	28-Mar-16		17-Mar-16	01-Apr-16	
Steel Stairs												
CON7250	Greeter Stair installation 6 MART	60	60	0	0%	16	24-Aug-15	23-Sep-15		13-Nov-15	15-Dec-15	
Carpentry												
CON430	Partition Layout: MART (to be CONSTRAINED ACTIVITY ES 11MAY)	60	36	7	40%	-89	11-May-15	01-Jun-15	11-May-15	03-Aug-15	21-Jul-15	
CON2600	Install radiation shielding, light-gauge	30	30	0	0%	-24	02-Oct-15	14-Oct-15		13-Nov-15	25-Nov-15	
Hollow Metal Doors												
HCMM1020	HCM doors & Frames 5 MART	20	20	0	0%	38	04-Dec-15	03-Nov-15		01-Jan-16	30-Nov-15	
HCMM1030	HCM doors & Frames 6 MART	20	20	0	0%	44	04-Dec-15	06-Nov-15		01-Jan-16	03-Dec-15	
HCMM1010	HCM doors & Frames 4 MART	20	20	0	0%	52	11-Nov-15	11-Nov-15		09-Dec-15	09-Dec-15	
HCMM1040	HCM doors & Frames 7 MART	20	20	0	0%	44	18-Dec-15	20-Nov-15		15-Jan-16	17-Dec-15	
HCMM1050	HCM doors & Frames 8 MART	20	20	0	0%	44	18-Dec-15	20-Nov-15		15-Jan-16	17-Dec-15	
HCMM1060	HCM doors & Frames 9 MART	20	20	0	0%	44	01-Jan-16	04-Dec-15		29-Jan-16	31-Dec-15	
HCMM1000	10 HCM doors & Frames 10 MART	20	20	0	0%	44	01-Jan-16	04-Dec-15		29-Jan-16	31-Dec-15	
PLAM Doors												
PLAMM1020	PLAM doors 5 MART	20	20	0	0%	38	04-Dec-15	03-Nov-15		01-Jan-16	30-Nov-15	
PLAMM1030	PLAM doors 6 MART	20	20	0	0%	46	04-Dec-15	04-Nov-15		01-Jan-16	02-Dec-15	
PLAMM1010	PLAM doors 4 MART	20	20	0	0%	52	04-Dec-15	11-Nov-15		01-Jan-16	09-Dec-15	
PLAMM1040	PLAM doors 7 MART	20	20	0	0%	46	18-Dec-15	18-Nov-15		15-Jan-16	16-Dec-15	
PLAMM1050	PLAM doors 8 MART	20	20	0	0%	46	18-Dec-15	18-Nov-15		15-Jan-16	16-Dec-15	
PLAMM1060	PLAM doors 9 MART	20	20	0	0%	46	01-Jan-16	02-Dec-15		29-Jan-16	30-Dec-15	
PLAMM1000	PLAM doors 10 MART	20	20	0	0%	66	01-Jan-16	02-Dec-15		29-Jan-16	30-Dec-15	
Specialty Doors & Frames												
CON11660	Rough frame pass-thru chamber 6 MART	5	5	0	0%	6	26-Oct-15	04-Nov-15		02-Nov-15	11-Nov-15	
CON6810	Install ICU door assemblies MART 4	30	30	0	0%	8	25-Dec-15	08-Feb-16		05-Feb-16	18-Mar-16	
CON11050	Accordion Security Door Assemblies 5 MART	30	30	0	0%	8	25-Dec-15	08-Feb-16		05-Feb-16	18-Mar-16	
CON11670	Finishes pass-thru chamber 6 MART	5	5	0	0%	3	17-Mar-16	21-Mar-16		24-Mar-16	25-Mar-16	

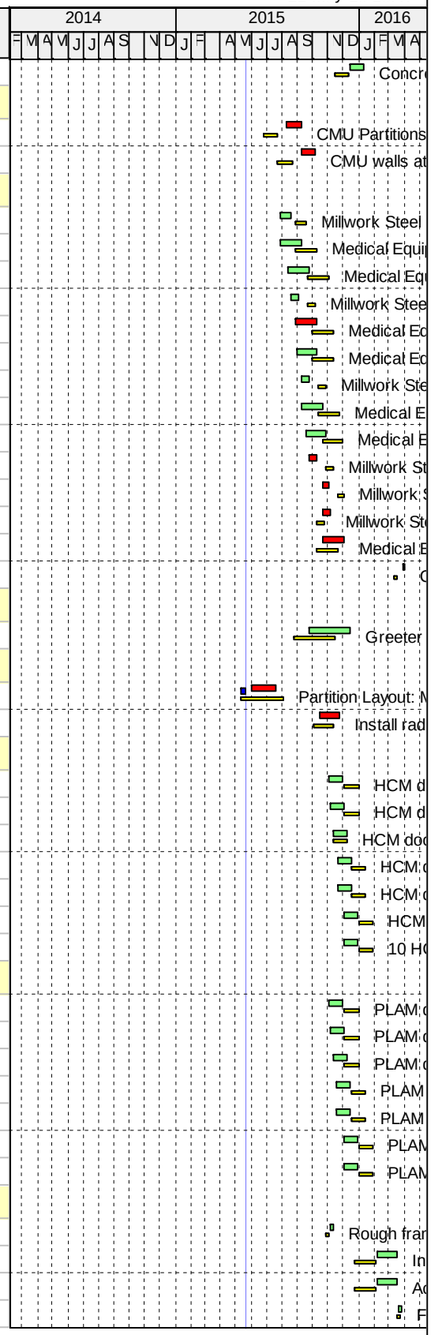

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
CON11110	Install Darkroom doors 8 MART	5	5	0	0%	-29	24-Mar-16	04-May-16		31-Mar-16	11-May-16	
Door Hardware												
HWRM1000	Door hardware 4 MART	20	20	0	0%	52	04-Dec-15	11-Nov-15		01-Jan-16	09-Dec-15	
HWRM1010	Door hardware 5 MART	20	20	0	0%	38	01-Jan-16	01-Dec-15		29-Jan-16	28-Dec-15	
HWRM1020	Door hardware 6 MART	20	20	0	0%	38	29-Jan-16	29-Dec-15		26-Feb-16	25-Jan-16	
HWRM1030	Door hardware 7 MART	20	20	0	0%	38	29-Jan-16	29-Dec-15		26-Feb-16	25-Jan-16	
HWRM1040	Door hardware 8 MART	20	20	0	0%	38	11-Feb-16	11-Jan-16		10-Mar-16	08-Feb-16	
HWRM1050	Door hardware 9 MART	20	20	0	0%	38	11-Feb-16	11-Jan-16		10-Mar-16	08-Feb-16	
HWRM1060	Door hardware 10 MART	20	20	0	0%	38	11-Feb-16	11-Jan-16		10-Mar-16	08-Feb-16	
Aluminum Storefront												
SFM1000	Interior Storefront installations MART (rated) 5 MART	40	40	0	0%	4	04-Dec-15	04-Dec-15		29-Jan-16	28-Jan-16	
SFM1020	Interior Storefront installations MART 5 (non-rated) 5 MART	40	40	0	0%	4	04-Dec-15	04-Dec-15		29-Jan-16	28-Jan-16	
SFM1010	Interior Storefront installations MART (rated) 6 MART	40	40	0	0%	4	29-Jan-16	29-Jan-16		25-Mar-16	24-Mar-16	
SFM1030	Interior Storefront installations MART 5 (non-rated) 6 MART	40	40	0	0%	4	29-Jan-16	29-Jan-16		25-Mar-16	24-Mar-16	
Light-gauge Metal Framing												
GWBM1000	Interior Framing: Level 4 MART	40	40	0	0%	-43	25-May-15	04-Jun-15		20-Jul-15	30-Jul-15	
GWBM1010	Interior Framing: Level 5 MART	20	20	0	0%	-13	25-May-15	04-Jun-15		22-Jun-15	02-Jul-15	
GWBM1020	Interior Framing: Level 6 MART	20	19	2	5%	-11	08-Jun-15	18-Jun-15	18-May-15	06-Jul-15	15-Jul-15	
GWBM1030	Interior Framing: Level 7 MART	20	19	2	5%	-9	08-Jun-15	18-Jun-15	18-May-15	06-Jul-15	15-Jul-15	
GWBM1040	Interior Framing: Level 8 MART	20	19	29	5%	-9	19-Jun-15	29-Jun-15	20-May-15	17-Jul-15	24-Jul-15	
GWBM1050	Interior Framing: Level 9 MART	20	19	29	5%	-9	19-Jun-15	29-Jun-15	20-May-15	17-Jul-15	24-Jul-15	
GWB Walls												
GWBM1080	GWB Partitions: Level 7 MART	20	20	0	0%	49	09-Sep-15	11-Aug-15		07-Oct-15	08-Sep-15	
GWBM1060	GWB Partitions: Level 8 MART	20	20	0	0%	59	08-Sep-15	24-Aug-15		06-Oct-15	21-Sep-15	
GWBM1090	GWB Partitions: Level 9 MART	20	20	0	0%	29	07-Oct-15	05-Oct-15		04-Nov-15	02-Nov-15	
GWBM1160	GWB Partitions: Level 5 MART	20	20	0	0%	9	06-Nov-15	06-Oct-15		04-Dec-15	02-Nov-15	
GWBM1070	GWB Partitions: Level 6 MART	20	20	0	0%	-24	25-Sep-15	07-Oct-15		23-Oct-15	04-Nov-15	
GWBM1140	GWB Partitions: Level 4 MART	20	20	0	0%	-24	14-Oct-15	14-Oct-15		11-Nov-15	11-Nov-15	
GWB Ceilings												
GWBM1180	GWB Ceilings: Level 4 MART	15	15	0	0%	-92	21-Jan-16	25-Jan-16		11-Feb-16	12-Feb-16	
GWBM1170	GWB Ceilings: Level 5 MART	15	15	0	0%	-67	28-Jan-16	01-Feb-16		18-Feb-16	19-Feb-16	
GWBM1110	GWB Ceilings: Level 6 MART	15	15	0	0%	-52	28-Jan-16	01-Feb-16		18-Feb-16	19-Feb-16	
GWBM1120	3-Form Ceiling System: Level 6 MART	15	15	0	0%	-15	28-Jan-16	01-Feb-16		18-Feb-16	19-Feb-16	
GWBM1150	GWB Ceilings: Level 7 MART	15	15	0	0%	-47	04-Feb-16	08-Feb-16		25-Feb-16	26-Feb-16	
GWBM1100	GWB Ceilings: Level 8 MART	15	15	0	0%	-57	04-Feb-16	16-Mar-16		25-Feb-16	06-Apr-16	
GWBM1130	GWB Ceilings: Level 9 MART	15	15	0	0%	-52	11-Feb-16	23-Mar-16		03-Mar-16	13-Apr-16	
Suspended Acoustical Ceiling												
ACTM1100	ACT Ceilings: Level 4 MART	20	20	0	0%	28	21-Jan-16	25-Jan-16		18-Feb-16	19-Feb-16	
ACTM1050	ACT Ceilings: Level 6 MART	20	20	0	0%	40	28-Jan-16	01-Feb-16		25-Feb-16	26-Feb-16	
ACTM1080	HPL soffits: Level 5 MART	20	20	0	0%	23	28-Jan-16	01-Feb-16		25-Feb-16	26-Feb-16	
ACTM1020	HPL soffits: Level 6 MART	20	20	0	0%	40	28-Jan-16	01-Feb-16		25-Feb-16	26-Feb-16	
ACTM1070	ACT Ceilings: Level 7 MART	20	20	0	0%	35	04-Feb-16	08-Feb-16		03-Mar-16	04-Mar-16	
ACTM1000	HPL soffits: Level 7 MART	20	20	0	0%	35	04-Feb-16	08-Feb-16		03-Mar-16	04-Mar-16	
ACTM1040	ACT Ceilings: Level 8 MART	20	20	0	0%	-14	04-Feb-16	16-Mar-16		03-Mar-16	13-Apr-16	
ACTM1010	HPL soffits: Level 8 MART	20	20	0	0%	-14	04-Feb-16	16-Mar-16		03-Mar-16	13-Apr-16	
ACTM1090	ACT Ceilings: Level 5 MART	20	20	0	0%	-12	28-Jan-16	21-Mar-16		25-Feb-16	15-Apr-16	

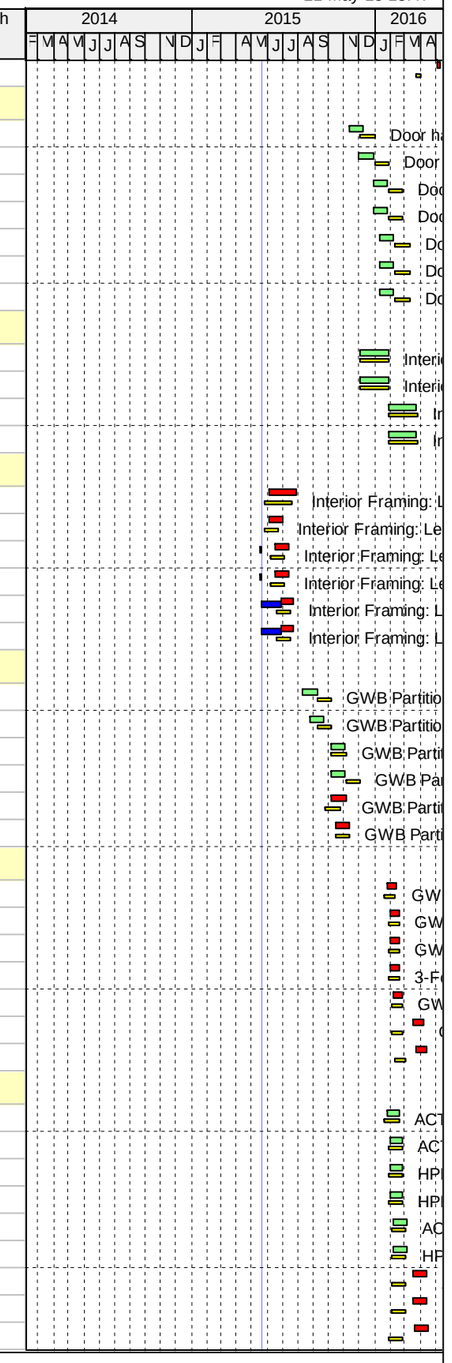

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
ACTM1060	ACT Ceilings: Level 9 MART	20	20	0	0%	3	11-Feb-16	23-Mar-16		10-Mar-16	20-Apr-16	
ACTM1030	HPL soffits: Level 9 MART	20	20	0	0%	3	11-Feb-16	23-Mar-16		10-Mar-16	20-Apr-16	
Finish Carpentry: Casework, Paneling & Trims												
FCM1020	Finish carpentry: Level 6 MART	20	20	0	0%	8	18-Feb-16	22-Feb-16		17-Mar-16	18-Mar-16	
FCM1030	Finish carpentry: Level 7 MART	20	20	0	0%	3	25-Feb-16	29-Feb-16		24-Mar-16	25-Mar-16	
FCM1040	Finish carpentry: Level 8 MART	20	20	0	0%	-24	25-Feb-16	06-Apr-16		24-Mar-16	04-May-16	
FCM1000	Finish carpentry: Level 4 MART	20	20	0	0%	-29	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	
FCM1010	Finish carpentry: Level 5 MART	20	20	0	0%	-29	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	
FCM1050	Finish carpentry: Level 9 MART	20	20	0	0%	-29	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	
FCM1060	Install Column enclosures MART	75	75	0	0%	-51	25-Jan-16	19-Apr-16		06-May-16	01-Aug-16	
Painting												
PNTM1050	Painting: Level 4 MART	20	20	0	0%	-92	11-Feb-16	15-Feb-16		10-Mar-16	11-Mar-16	
PNTM1040	Painting: Level 5 MART	20	20	0	0%	-67	18-Feb-16	22-Feb-16		17-Mar-16	18-Mar-16	
PNTM1010	Painting: Level 6 MART	20	20	0	0%	-52	18-Feb-16	22-Feb-16		17-Mar-16	18-Mar-16	
PNTM1060	Painting: Level 10 MART	20	20	0	0%	-20	11-Feb-16	29-Feb-16		10-Mar-16	25-Mar-16	
PNTM1030	Painting: Level 7 MART	20	20	0	0%	-47	25-Feb-16	29-Feb-16		24-Mar-16	25-Mar-16	
PNTM1070	Painting: Level 3 MART	20	20	0	0%	-92	11-Feb-16	29-Feb-16		10-Mar-16	25-Mar-16	
PNTM1000	Painting: Level 8 MART	20	20	0	0%	-57	25-Feb-16	06-Apr-16		24-Mar-16	04-May-16	
PNTM1020	Painting: Level 9 MART	20	20	0	0%	-52	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	
GFRC												
CON210	GFRC installations	30	30	0	0%	13	28-Jan-16	01-Feb-16		10-Mar-16	11-Mar-16	
Interior Glazing												
GLZM1040	Level 4 IGUs MART	20	20	0	0%	4	11-Feb-16	15-Feb-16		10-Mar-16	11-Mar-16	
GLZM1060	Level 5 IGUs MART	20	20	0	0%	-1	18-Feb-16	22-Feb-16		17-Mar-16	18-Mar-16	
GLZM1010	Glass railings Level 6 MART	20	20	0	0%	8	18-Feb-16	22-Feb-16		17-Mar-16	18-Mar-16	
GLZM1000	Level 6 IGUs MART	20	20	0	0%	-12	17-Mar-16	21-Mar-16		14-Apr-16	15-Apr-16	
GLZM1020	Level 7 IGUs MART	20	20	0	0%	-12	17-Mar-16	21-Mar-16		14-Apr-16	15-Apr-16	
GLZM1030	Level 8 IGUs MART	20	20	0	0%	-24	17-Mar-16	06-Apr-16		14-Apr-16	04-May-16	
GLZM1050	Level 9 IGUs MART	20	20	0	0%	-29	17-Mar-16	13-Apr-16		14-Apr-16	11-May-16	
Resilient Flooring & Carpeting												
RFM1040	Level 5 Resilient Flooring MART	20	20	0	0%	-12	18-Feb-16	22-Feb-16		17-Mar-16	18-Mar-16	
RFM1050	Level 5 FR Expansion Joint MART	10	10	0	0%	-2	18-Feb-16	22-Feb-16		03-Mar-16	04-Mar-16	
RFM1070	Level 4 Resilient Flooring MART	20	20	0	0%	-2	03-Mar-16	07-Mar-16		31-Mar-16	01-Apr-16	
RFM1000	Level 6 Resilient Flooring MART	20	20	0	0%	6	17-Mar-16	21-Mar-16		14-Apr-16	15-Apr-16	
RFM1010	Level 6 FR Expansion Joint MART	10	10	0	0%	6	17-Mar-16	21-Mar-16		31-Mar-16	01-Apr-16	
RFM1020	Level 7 Resilient Flooring MART	20	20	0	0%	6	31-Mar-16	04-Apr-16		28-Apr-16	29-Apr-16	
RFM1030	Level 8 Resilient Flooring MART	20	20	0	0%	-7	13-Apr-16	04-May-16		11-May-16	01-Jun-16	
RFM1060	Level 9 Resilient Flooring MART	20	20	0	0%	-12	13-Apr-16	11-May-16		11-May-16	08-Jun-16	
Ceramic Tile												
TLM1060	Ceramic tile 4 MART	20	20	0	0%	1	11-Feb-16	15-Feb-16		10-Mar-16	11-Mar-16	
TLM1050	Glass wall tile 4 MART	40	40	0	0%	30	11-Feb-16	15-Feb-16		07-Apr-16	08-Apr-16	
TLM1040	Ceramic tile 5 MART	20	20	0	0%	-15	18-Feb-16	22-Feb-16		17-Mar-16	18-Mar-16	
TLM1020	Ceramic tile 6 MART	20	20	0	0%	-24	18-Feb-16	22-Feb-16		17-Mar-16	18-Mar-16	
TLM1000	Ceramic tile 7 MART	20	20	0	0%	-29	25-Feb-16	29-Feb-16		24-Mar-16	25-Mar-16	
TLM1010	Ceramic tile 8 MART	20	20	0	0%	-57	25-Feb-16	06-Apr-16		24-Mar-16	04-May-16	
TLM1030	Ceramic tile 9 MART	20	20	0	0%	-52	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	

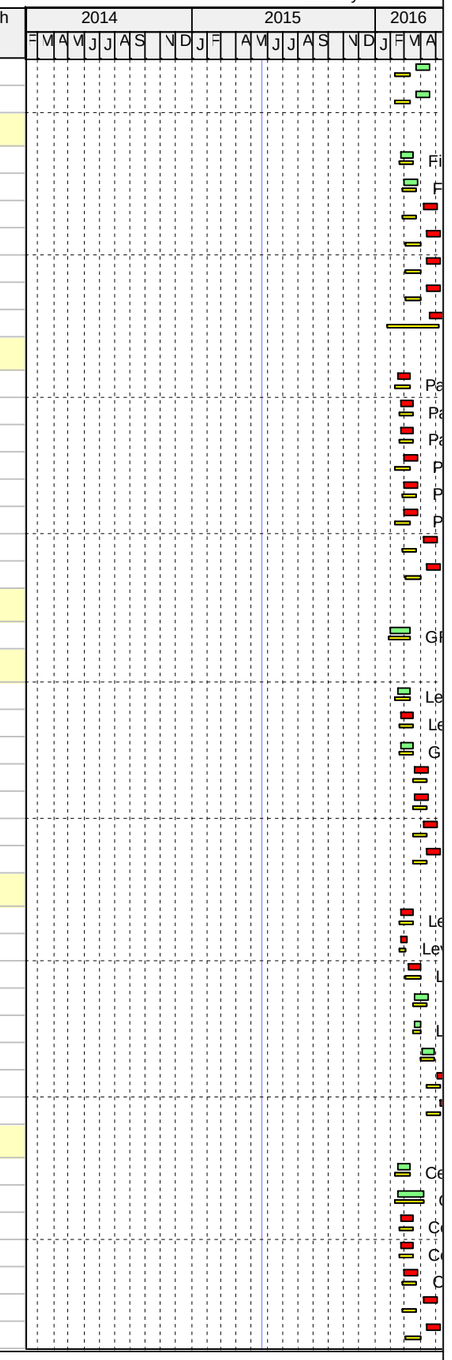

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
Specialties/Accessories												
ACCM1000	Install Div. 10 accessories: Level 4 MART	30	30	0	0%	3	11-Feb-16	15-Feb-16		24-Mar-16	25-Mar-16	
ACCM1010	Install Div. 10 accessories: Level 5 MART	20	20	0	0%	-22	17-Mar-16	21-Mar-16		14-Apr-16	15-Apr-16	
ACCM1020	Install Div. 10 accessories: Level 6 MART	20	20	0	0%	-22	17-Mar-16	21-Mar-16		14-Apr-16	15-Apr-16	
ACCM1030	Install Div. 10 accessories: Level 7 MART	20	20	0	0%	-22	31-Mar-16	04-Apr-16		28-Apr-16	29-Apr-16	
ACCM1040	Install Div. 10 accessories: Level 8 MART	20	20	0	0%	-44	31-Mar-16	04-May-16		28-Apr-16	01-Jun-16	
ACCM1050	Install Div. 10 accessories: Level 9 MART	20	20	0	0%	-49	31-Mar-16	11-May-16		28-Apr-16	08-Jun-16	
Wall Protections												
WPM1000	Wall Protection: Corner Guards & Crash Rail Level 4 MART	10	10	0	0%	-7	10-Mar-16	14-Mar-16		24-Mar-16	25-Mar-16	
WPM1010	Wall Protection: Corner Guards & Crash Rail Level 5 MART	10	10	0	0%	-12	17-Mar-16	21-Mar-16		31-Mar-16	01-Apr-16	
WPM1020	Wall Protection: Corner Guards & Crash Rail Level 6 MART	10	10	0	0%	-12	17-Mar-16	21-Mar-16		31-Mar-16	01-Apr-16	
WPM1030	Wall Protection: Corner Guards & Crash Rail Level 7 MART	10	10	0	0%	-12	31-Mar-16	04-Apr-16		14-Apr-16	15-Apr-16	
WPM1040	Wall Protection: Corner Guards & Crash Rail Level 8 MART	10	10	0	0%	-34	31-Mar-16	04-May-16		14-Apr-16	18-May-16	
WPM1050	Wall Protection: Corner Guards & Crash Rail Level 9 MART	10	10	0	0%	-39	31-Mar-16	11-May-16		14-Apr-16	25-May-16	
Laboratory Equipment												
MEDM1000	Medical Equipment tie-ins 7 MART	60	60	0	0%	42	10-Dec-15	22-Dec-15		03-Mar-16	14-Mar-16	
MEDM1070	Medical Equipment tie-ins 8 MART	60	60	0	0%	52	10-Dec-15	22-Dec-15		03-Mar-16	14-Mar-16	
MEDM1010	Medical Equipment tie-ins 9 MART	60	60	0	0%	12	24-Dec-15	22-Dec-15		17-Mar-16	14-Mar-16	
MEDM1040	Medical Equipment tie-ins 4 MART	30	30	0	0%	42	07-Jan-16	22-Dec-15		18-Feb-16	01-Feb-16	
MEDM1050	Medical Equipment tie-ins 6 MART	60	60	0	0%	12	26-Nov-15	22-Dec-15		18-Feb-16	14-Mar-16	
MEDM1060	Medical Equipment tie-ins 3 MART	30	30	0	0%	20	07-Jan-16	07-Jan-16		18-Feb-16	18-Feb-16	
MEDM1020	Fume hoods: 7 MART	20	20	0	0%	3	25-Feb-16	29-Feb-16		24-Mar-16	25-Mar-16	
MEDM1080	Fume hoods: 8 MART	20	20	0	0%	3	25-Feb-16	29-Feb-16		24-Mar-16	25-Mar-16	
MEDM1100	Glass washers and sterilizer tie-ins 8 MART	10	10	0	0%	-34	25-Feb-16	06-Apr-16		10-Mar-16	20-Apr-16	
MEDM1030	Fume hoods: 9 MART	20	20	0	0%	-29	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	
MEDM1090	Glass washers and sterilizer tie-ins 7 MART	10	10	0	0%	-34	24-Mar-16	20-Apr-16		07-Apr-16	04-May-16	
MEDM1110	Glass washers and sterilizer tie-ins 9 MART	10	10	0	0%	-39	07-Apr-16	11-May-16		21-Apr-16	25-May-16	
Medical Equipment: PETCT1												
EQTIEM1060	Layout PETCT1	10	10	0	0%	3	25-May-15	04-Jun-15		08-Jun-15	18-Jun-15	
EQTIEM1070	Partition framing: PETCT1	20	20	0	0%	3	08-Jun-15	18-Jun-15		06-Jul-15	16-Jul-15	
EQTIEM1080	HVAC Rough: PETCT1	20	20	0	0%	3	06-Jul-15	16-Jul-15		03-Aug-15	13-Aug-15	
EQTIEM1090	Plumbing Rough: PETCT1	20	20	0	0%	3	03-Aug-15	13-Aug-15		31-Aug-15	10-Sep-15	
EQTIEM1100	Electric Rough: PETCT1	20	20	0	0%	3	31-Aug-15	10-Sep-15		28-Sep-15	08-Oct-15	
EQTIEM1110	GWB: PETCT1	10	10	0	0%	3	28-Sep-15	08-Oct-15		12-Oct-15	22-Oct-15	
EQTIEM1120	ACT CelingsPETCT1	10	10	0	0%	3	12-Oct-15	22-Oct-15		26-Oct-15	05-Nov-15	
EQTIEM1130	Finishes:PETCT1	30	30	0	0%	3	26-Oct-15	05-Nov-15		07-Dec-15	17-Dec-15	
EQTIEM1050	Vendor pre-inspection	2	2	0	0%	3	07-Dec-15	17-Dec-15		09-Dec-15	21-Dec-15	
EQTIEM1030	MEP PETCT1-1 tie-ins	60	60	0	0%	3	09-Dec-15	21-Dec-15		02-Mar-16	14-Mar-16	
EQTIEM1140	MEP Finishes PETCT1	10	10	0	0%	3	02-Mar-16	14-Mar-16		16-Mar-16	28-Mar-16	
Environmental Stabilization												
EQTIEM1500	MEP Rough at Freezer Farm	30	30	0	0%	-3	21-Aug-15	06-Oct-15		02-Oct-15	17-Nov-15	
EQTIEM1480	Freezer Farm installation	30	30	0	0%	-28	09-Nov-15	22-Dec-15		18-Dec-15	01-Feb-16	
EQTIEM1510	MEP FInishes at Freezer Farm	10	10	0	0%	-28	21-Dec-15	02-Feb-16		01-Jan-16	15-Feb-16	
EQTIEM1520	Cold Room 7 MART	10	10	0	0%	-28	04-Jan-16	16-Feb-16		15-Jan-16	29-Feb-16	
EQTIEM1530	Cold Room 8 MART	10	10	0	0%	-28	18-Jan-16	01-Mar-16		29-Jan-16	14-Mar-16	
EQTIEM1540	Cold Room 9 MART	10	10	0	0%	-28	01-Feb-16	15-Mar-16		12-Feb-16	28-Mar-16	

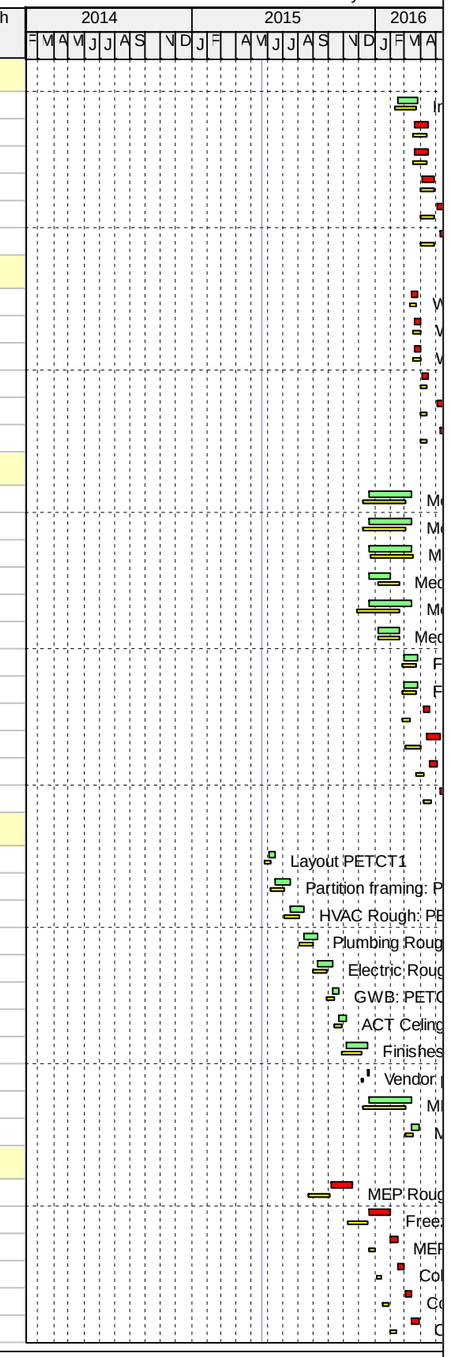

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
Medical Equipment: Cyclotron												
EQTIEM1150	Layout Cyclotron	5	5	0	0%	14	08-Jul-15	08-Jul-15		15-Jul-15	15-Jul-15	
EQTIEM1160	Partition framing: Cyclotron	10	10	0	0%	14	29-Jul-15	15-Jul-15		12-Aug-15	29-Jul-15	
EQTIEM1170	HVAC Rough: Cyclotron	20	20	0	0%	14	12-Aug-15	29-Jul-15		09-Sep-15	26-Aug-15	
EQTIEM1440	Production lab pass-thru	5	5	0	0%	19	12-Aug-15	29-Jul-15		19-Aug-15	05-Aug-15	
EQTIEM1180	Plumbing Rough: Cyclotron	20	20	0	0%	14	26-Aug-15	12-Aug-15		23-Sep-15	09-Sep-15	
EQTIEM1190	Electric Rough: Cyclotron	20	20	0	0%	14	09-Sep-15	26-Aug-15		07-Oct-15	23-Sep-15	
EQTIEM1430	Install hot cells	20	20	0	0%	14	15-Jul-15	26-Aug-15		12-Aug-15	23-Sep-15	
EQTIEM1200	GWB: Cyclotron	10	10	0	0%	14	07-Oct-15	23-Sep-15		21-Oct-15	07-Oct-15	
EQTIEM1210	ACT CelingsCyclotron	10	10	0	0%	14	07-Oct-15	23-Sep-15		21-Oct-15	07-Oct-15	
EQTIEM1220	Finishes:Cyclotron	15	15	0	0%	14	07-Oct-15	23-Sep-15		28-Oct-15	14-Oct-15	
EQTIEM1450	Vendor pre-inspection	2	2	0	0%	14	28-Oct-15	14-Oct-15		30-Oct-15	16-Oct-15	
EQTIEM1420	Cyclotron delivery	0	0	0	0%	-3				30-Oct-15	09-Nov-15	
CON5560	High-density concrete block at Cyclotron	30	30	0	0%	-3	30-Oct-15	10-Nov-15		11-Dec-15	21-Dec-15	
EQTIEM1040	Cyclotron tie-ins	50	50	0	0%	-3	20-Nov-15	01-Dec-15		29-Jan-16	08-Feb-16	
CON5570	Cyclotron Vault door	15	15	0	0%	-3	20-Nov-15	01-Dec-15		11-Dec-15	21-Dec-15	
EQTIEM1230	MEP Finishes Cyclotron	10	10	0	0%	-3	29-Jan-16	09-Feb-16		12-Feb-16	22-Feb-16	
Manufactured Casework												
CASEM1030	Install Manufactured Casework: Level 6 MART	20	20	0	0%	-22	17-Mar-16	21-Mar-16		14-Apr-16	15-Apr-16	
CASEM1040	Install Manufactured Casework: Level 7 MART	20	20	0	0%	-22	30-Mar-16	01-Apr-16		27-Apr-16	29-Apr-16	
CASEM1060	Install Manufactured Casework: Level 8 MART	20	20	0	0%	-24	13-Apr-16	19-Apr-16		10-May-16	17-May-16	
CASEM1070	Install Manufactured Casework: Level 9 MART	20	20	0	0%	-24	26-Apr-16	02-May-16		24-May-16	30-May-16	
CASEM1080	Install Manufactured Casework: Level 5 MART	20	20	0	0%	-24	09-May-16	13-May-16		06-Jun-16	10-Jun-16	
CASEM1090	Install Manufactured Casework: Level 4 MART	20	20	0	0%	-24	20-May-16	27-May-16		17-Jun-16	23-Jun-16	
Laboratory Casework												
CASEM1000	Install Lab Casework: Level 7 MART	20	20	0	0%	-9	24-Mar-16	28-Mar-16		21-Apr-16	22-Apr-16	
CASEM1010	Install Lab Casework: Level 8 MART	20	20	0	0%	-27	06-Apr-16	04-May-16		04-May-16	01-Jun-16	
CASEM1020	Install Lab Casework: Level 9 MART	20	20	0	0%	-27	20-Apr-16	17-May-16		17-May-16	14-Jun-16	
CASEM1050	Install Lab Casework: Level 3 MART	20	20	0	0%	-27	04-May-16	31-May-16		31-May-16	28-Jun-16	
Controlled Environment Rooms												
CON11250	Controlled Environment Rooms 7 MART	30	30	0	0%	16	14-Dec-15	27-Jan-16		22-Jan-16	08-Mar-16	
CON11260	Controlled Environment Rooms 8 MART	30	30	0	0%	16	14-Dec-15	27-Jan-16		22-Jan-16	08-Mar-16	
CON11270	Controlled Environment Rooms 9 MART	30	30	0	0%	16	14-Dec-15	27-Jan-16		22-Jan-16	08-Mar-16	
Radiation Protection												
CON110	Radiation protection installation (MART)	30	30	0	0%	14	14-Oct-15	01-Jan-16		25-Nov-15	12-Feb-16	
Pneumatic Tube Systems												
CON3740	Pneumatic tube system installations	90	90	0	0%	-30	17-Aug-15	27-Aug-15		21-Dec-15	31-Dec-15	
Wet Standpipe System Piping												
FSM1010	Fire suppression branch work and heads Level 7 MART	35	35	0	0%	60	09-Jul-15	11-Jun-15		27-Aug-15	29-Jul-15	
FSM1020	Fire suppression branch work and heads Level 8 MART	38	38	0	0%	68	30-Jul-15	22-Jun-15		22-Sep-15	12-Aug-15	
FSM1030	Fire suppression branch work and heads Level 9 MART	38	38	0	0%	57	20-Aug-15	20-Jul-15		13-Oct-15	09-Sep-15	
FSM1040	Fire suppression branch work and heads Level 10 MART	20	20	0	0%	-3	20-Aug-15	20-Jul-15		17-Sep-15	14-Aug-15	
FSM1000	Fire suppression branch work and heads Level 6 MART	59	59	0	0%	-24	20-Jul-15	30-Jul-15		09-Oct-15	21-Oct-15	
FSM1050	Fire suppression branch work and heads Level 5 MART	56	56	0	0%	-23	03-Sep-15	03-Aug-15		20-Nov-15	19-Oct-15	
FSM1070	Fire suppression branch work and heads Level 3 MART	13	13	0	0%	-26	01-Oct-15	31-Aug-15		20-Oct-15	16-Sep-15	

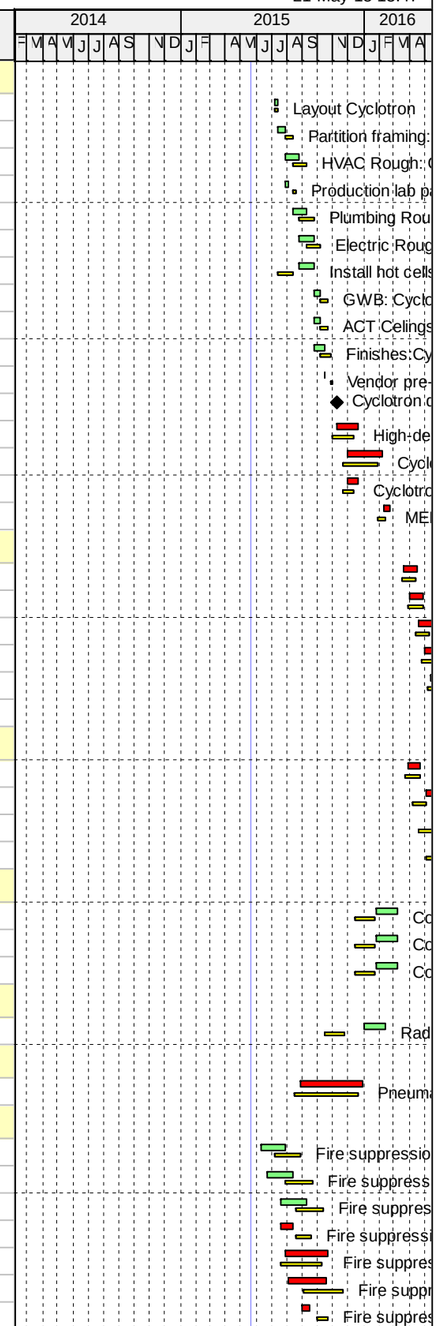

Remaining Level of Effort | Actual Level of Effort | Project Baseline Bar | Primary Baseline | Actual Work | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
FSM1060	Fire suppression branch work and heads Level 4 MART	16	16	0	0%	-26	20-Oct-15	17-Sep-15		11-Nov-15	08-Oct-15	
FSM1080	Fire pumps installation Level 3 MART	15	15	0	0%	61	20-Nov-15	20-Oct-15		11-Dec-15	09-Nov-15	
FSM1090	Fire Suppression System Pressure Test MART	5	5	0	0%	61	11-Dec-15	10-Nov-15		18-Dec-15	16-Nov-15	
Sanitary & Vent												
PMART1010	Sanitary, acid waste, and vent Level 7 MART	22	20	7	10%	56	16-Jul-15	18-Jun-15	11-May-15	17-Aug-15	15-Jul-15	
PMART1030	Sanitary, acid waste, and vent Level 8 MART	18	16	7	10%	24	09-Jul-15	18-Jun-15	11-May-15	04-Aug-15	10-Jul-15	
PMART1070	Sanitary, acid waste, and vent Level 9 MART	18	18	0	0%	-37	30-Jul-15	29-Jun-15		25-Aug-15	22-Jul-15	
PMART1110	Sanitary, and vent Level 10 MART	10	10	0	0%	-37	25-Aug-15	23-Jul-15		08-Sep-15	05-Aug-15	
PMART1120	Sanitary, and vent Roof MART	10	10	0	0%	-37	25-Aug-15	23-Jul-15		08-Sep-15	05-Aug-15	
PMART1000	Sanitary, and vent Level 6 MART	28	25	7	10%	5	20-Jul-15	30-Jul-15	11-May-15	27-Aug-15	03-Sep-15	
PMART1200	Sanitary, and vent Level 4 MART	40	40	0	0%	-39	10-Sep-15	10-Aug-15		05-Nov-15	02-Oct-15	
PMART1130	Sanitary, and vent Level 5 MART	40	40	0	0%	-5	17-Sep-15	17-Aug-15		12-Nov-15	09-Oct-15	
Domestic Piping												
PMART1090	HW/CW distribution Level 8 MART	28	27	7	5%	24	22-Jul-15	22-Jun-15	11-May-15	31-Aug-15	28-Jul-15	
PMART1050	HW/CW distribution Level 7 MART	28	27	7	5%	56	31-Jul-15	24-Jun-15	11-May-15	09-Sep-15	30-Jul-15	
PMART1100	HW/CW distribution Level 9 MART	26	25	7	5%	11	20-Aug-15	20-Jul-15	11-May-15	25-Sep-15	21-Aug-15	
PMART1160	HW/CW distribution Level 10 MART	8	8	0	0%	9	08-Sep-15	30-Jul-15		18-Sep-15	10-Aug-15	
PMART1060	HW/CW distribution Level 6 MART	35	33	7	5%	5	07-Aug-15	10-Aug-15	11-May-15	25-Sep-15	24-Sep-15	
PMART1220	HW/CW distribution Level 4 MART	25	25	0	0%	-39	01-Oct-15	31-Aug-15		05-Nov-15	02-Oct-15	
PMART1190	HW/CW distribution Level 5 MART	30	30	0	0%	-5	08-Oct-15	07-Sep-15		19-Nov-15	16-Oct-15	
Compressed Air & Vacuum, Medical Gas Distribution												
PMART1170	Compressed air/vacuum/medical gas pipe and fittings 10 MART	24	24	0	0%	9	22-Sep-15	13-Aug-15		26-Oct-15	15-Sep-15	
PMART1140	Compressed air/vacuum/medical gas pipe and fittings 6 MART	25	25	0	0%	22	01-Sep-15	24-Aug-15		06-Oct-15	28-Sep-15	
PMART1210	Compressed air/vacuum/medical gas pipe, fittings, & Equipment 7 MART	30	30	0	0%	22	01-Sep-15	24-Aug-15		13-Oct-15	05-Oct-15	
PMART1150	Compressed air/vacuum/medical gas pipe and fittings 8 MART	25	25	0	0%	40	22-Sep-15	14-Sep-15		27-Oct-15	19-Oct-15	
PMART1180	Compressed air/vacuum/medical gas pipe and fittings 9 MART	25	25	0	0%	40	22-Sep-15	14-Sep-15		27-Oct-15	19-Oct-15	
PMART1240	Compressed air/vacuum/medical gas pipe and fittings 4 MART	40	40	0	0%	-39	19-Oct-15	16-Sep-15		14-Dec-15	10-Nov-15	
PMART1250	Compressed air/vacuum/medical gas pipe and fittings 3 MART	20	20	0	0%	-3	30-Oct-15	29-Sep-15		27-Nov-15	26-Oct-15	
PMART1230	Compressed air/vacuum/medical gas pipe and fittings 5 MART	22	22	0	0%	-5	06-Nov-15	06-Oct-15		08-Dec-15	04-Nov-15	
Natural Gas Piping												
PMART1020	Gas distribution Level 7 MART	18	18	0	0%	22	13-Oct-15	05-Oct-15		06-Nov-15	29-Oct-15	
PMART1080	Gas distribution Level 9 MART	20	20	0	0%	40	27-Oct-15	19-Oct-15		24-Nov-15	16-Nov-15	
PMART1040	Gas distribution Level 8 MART	20	20	0	0%	22	06-Nov-15	29-Oct-15		04-Dec-15	26-Nov-15	
Laboratory Gas Alarms												
CON9010	Laboratory gas alarms 6 MART	10	10	0	0%	-14	04-Feb-16	08-Feb-16		18-Feb-16	19-Feb-16	
CON9020	Laboratory gas alarms 7 MART	10	10	0	0%	-19	11-Feb-16	15-Feb-16		25-Feb-16	26-Feb-16	
CON9030	Laboratory gas alarms 8 MART	10	10	0	0%	-46	11-Feb-16	23-Mar-16		25-Feb-16	06-Apr-16	
CON9070	Laboratory gas alarms 4 MART	10	10	0	0%	-45	18-Feb-16	30-Mar-16		03-Mar-16	13-Apr-16	
CON9060	Laboratory gas alarms 5 MART	10	10	0	0%	-51	18-Feb-16	30-Mar-16		03-Mar-16	13-Apr-16	
CON9040	Laboratory gas alarms 9 MART	10	10	0	0%	-51	18-Feb-16	30-Mar-16		03-Mar-16	13-Apr-16	
CON9050	Laboratory gas alarms 10 MART	10	10	0	0%	-51	18-Feb-16	30-Mar-16		03-Mar-16	13-Apr-16	
Chemical Waste Systems												
CWPCON8	Chemical waste piping Level 7 MART	20	20	0	0%	59	06-Aug-15	30-Jun-15		03-Sep-15	27-Jul-15	
CWPCON8	Chemical waste piping Level 8 MART	20	20	0	0%	79	30-Jul-15	30-Jun-15		27-Aug-15	27-Jul-15	
Plumbing Fixtures												

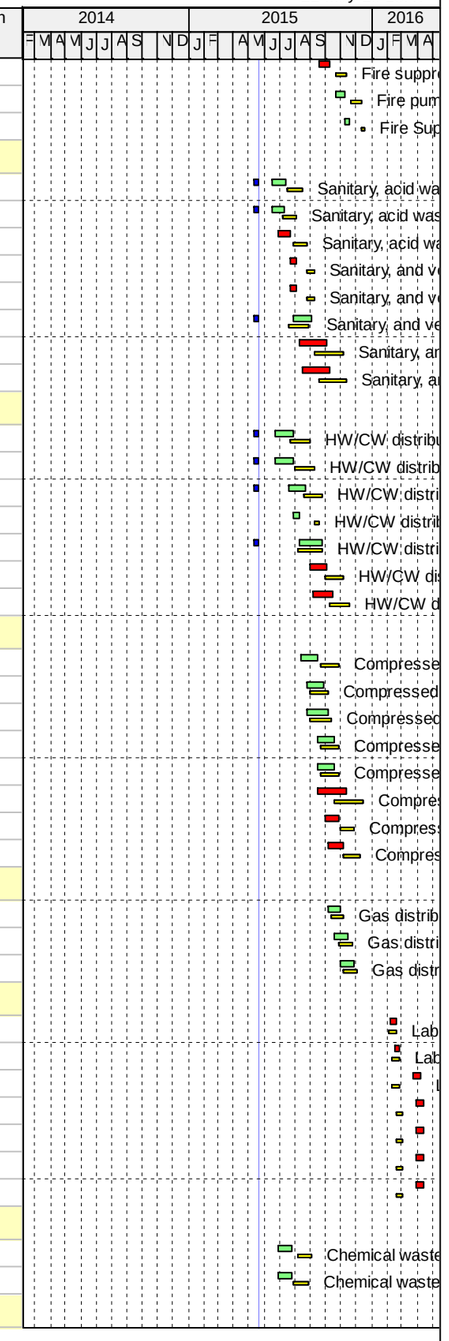

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
PMART1270	Plumbing Fixtures 6 MART	28	28	0	0%	-24	17-Mar-16	21-Mar-16		26-Apr-16	27-Apr-16	
PMART1280	Plumbing Fixtures 7 MART	25	25	0	0%	-29	24-Mar-16	28-Mar-16		28-Apr-16	29-Apr-16	
PMART1290	Plumbing Fixtures 8 MART	30	30	0	0%	-57	24-Mar-16	04-May-16		05-May-16	15-Jun-16	
PMART1330	Plumbing Fixtures 4 MART	12	12	0	0%	-45	06-Apr-16	17-May-16		22-Apr-16	02-Jun-16	
PMART1310	Plumbing Fixtures 5 MART	30	30	0	0%	-57	06-Apr-16	17-May-16		18-May-16	28-Jun-16	
PMART1300	Plumbing Fixtures 9 MART	32	32	0	0%	-57	06-Apr-16	17-May-16		20-May-16	30-Jun-16	
PMART1320	Plumbing Fixtures 10 MART	8	8	0	0%	-57	06-Apr-16	17-May-16		18-Apr-16	27-May-16	
PMART1340	Scrub Sinks 4 MART	12	12	0	0%	-45	06-Apr-16	17-May-16		22-Apr-16	02-Jun-16	
Hydronic Piping												
MECHM1040	HW/CHW/S/R/CD 7 MART	20	20	0	0%	-40	09-Jul-15	11-Jun-15		06-Aug-15	08-Jul-15	
MECHM1100	HW/CHW/S/R/CD 8 MART	20	20	0	0%	-17	30-Jul-15	22-Jun-15		27-Aug-15	17-Jul-15	
MECHM1170	HW/CHW/S/R/CD 9 MART	20	20	0	0%	-17	20-Aug-15	20-Jul-15		17-Sep-15	14-Aug-15	
MECHM1180	HW/CHW/S/R/CD 10 MART	20	20	0	0%	3	20-Aug-15	20-Jul-15		17-Sep-15	14-Aug-15	
MECHM1030	HW/CHW/S/R/CD 6 MART	20	20	0	0%	-30	20-Jul-15	30-Jul-15		17-Aug-15	27-Aug-15	
MECHM1300	HW/CHW/S/R/CD 4 MART	40	40	0	0%	-12	10-Sep-15	10-Aug-15		05-Nov-15	02-Oct-15	
MECHM1330	HW/CHW/S/R/CD 3 MART	40	40	0	0%	23	01-Oct-15	31-Aug-15		26-Nov-15	23-Oct-15	
MECHM1250	HW/CHW/S/R/CD 5 MART	20	20	0	0%	-57	15-Oct-15	14-Sep-15		12-Nov-15	09-Oct-15	
Hydronic Piping insulation												
MECHM1060	HW/CHW/S/R/CD insulation 7 MART	20	20	0	0%	-40	06-Aug-15	09-Jul-15		03-Sep-15	05-Aug-15	
MECHM1120	HW/CHW/S/R/CD insulation 8 MART	20	20	0	0%	-40	20-Aug-15	23-Jul-15		17-Sep-15	19-Aug-15	
MECHM1050	HW/CHW/S/R/CD insulation 6 MART	20	20	0	0%	-30	20-Jul-15	30-Jul-15		17-Aug-15	27-Aug-15	
MECHM1280	HW/CHW/S/R/CD insulation 10 MART	20	20	0	0%	13	17-Sep-15	17-Aug-15		15-Oct-15	11-Sep-15	
MECHM1190	HW/CHW/S/R/CD insulation 9 MART	20	20	0	0%	-40	17-Sep-15	20-Aug-15		15-Oct-15	16-Sep-15	
MECHM1340	HW/CHW/S/R/CD insulation 3 MART	40	40	0	0%	13	15-Oct-15	14-Sep-15		10-Dec-15	06-Nov-15	
MECHM1260	HW/CHW/S/R/CD insulation 5 MART	20	20	0	0%	-57	12-Nov-15	12-Oct-15		10-Dec-15	06-Nov-15	
MECHM1310	HW/CHW/S/R/CD insulation 4 MART	40	40	0	0%	-57	12-Nov-15	12-Oct-15		07-Jan-16	04-Dec-15	
Steam & Condensate Piping												
STMM1050	Steam/Condensate piping 5 MART	20	20	0	0%	19	01-Oct-15	31-Aug-15		29-Oct-15	25-Sep-15	
STMM1060	Steam/Condensate piping 4 MART	40	40	0	0%	-27	01-Oct-15	31-Aug-15		26-Nov-15	23-Oct-15	
STMM1000	Steam/Condensate piping 6 MART	20	19	7	5%	19	29-Oct-15	28-Sep-15	11-May-15	26-Nov-15	22-Oct-15	
STMM1040	Steam/Condensate piping 10 MART	20	20	0	0%	19	29-Oct-15	28-Sep-15		26-Nov-15	23-Oct-15	
STMM1010	Steam/Condensate piping 7 MART	20	19	7	5%	19	12-Nov-15	12-Oct-15	11-May-15	10-Dec-15	05-Nov-15	
STMM1020	Steam/Condensate piping 8 MART	20	19	7	5%	37	12-Nov-15	12-Oct-15	11-May-15	10-Dec-15	05-Nov-15	
STMM1030	Steam/Condensate piping 9 MART	20	19	7	5%	41	26-Nov-15	15-Oct-15	11-May-15	24-Dec-15	10-Nov-15	
HVAC Ductwork												
MECHM1000	Ductwork 6 MART	40	36	34	10%	-92	25-May-15	09-Jun-15	02-Apr-15	14-Jul-15	28-Jul-15	
MECHM1010	Ductwork 7 MART	40	36	13	10%	-92	18-Jun-15	09-Jun-15	01-May-15	13-Aug-15	28-Jul-15	
MECHM1020	Ductwork 8 MART	40	36	13	10%	-92	09-Jul-15	18-Jun-15	01-May-15	03-Sep-15	06-Aug-15	
MECHM1090	Ductwork 9 MART	40	40	0	0%	-92	30-Jul-15	29-Jun-15		24-Sep-15	21-Aug-15	
MECHM1160	Ductwork 5 MART	40	40	0	0%	-92	20-Aug-15	20-Jul-15		15-Oct-15	11-Sep-15	
MECHM1240	Ductwork 4 MART	40	40	0	0%	-92	10-Sep-15	10-Aug-15		05-Nov-15	02-Oct-15	
MECHM1490	Air balancing: MART	40	40	0	0%	-5	17-Feb-16	11-Feb-16		13-Apr-16	06-Apr-16	
Duct Insulation												
DINSM1030	Ductwork insulation 9 MART	20	20	0	0%	1	27-Aug-15	27-Jul-15		24-Sep-15	21-Aug-15	
DINSM1000	Ductwork insulation 6 MART	20	20	0	0%	21	14-Jul-15	29-Jul-15		11-Aug-15	25-Aug-15	
DINSM1010	Ductwork insulation 7 MART	20	20	0	0%	31	13-Aug-15	29-Jul-15		10-Sep-15	25-Aug-15	

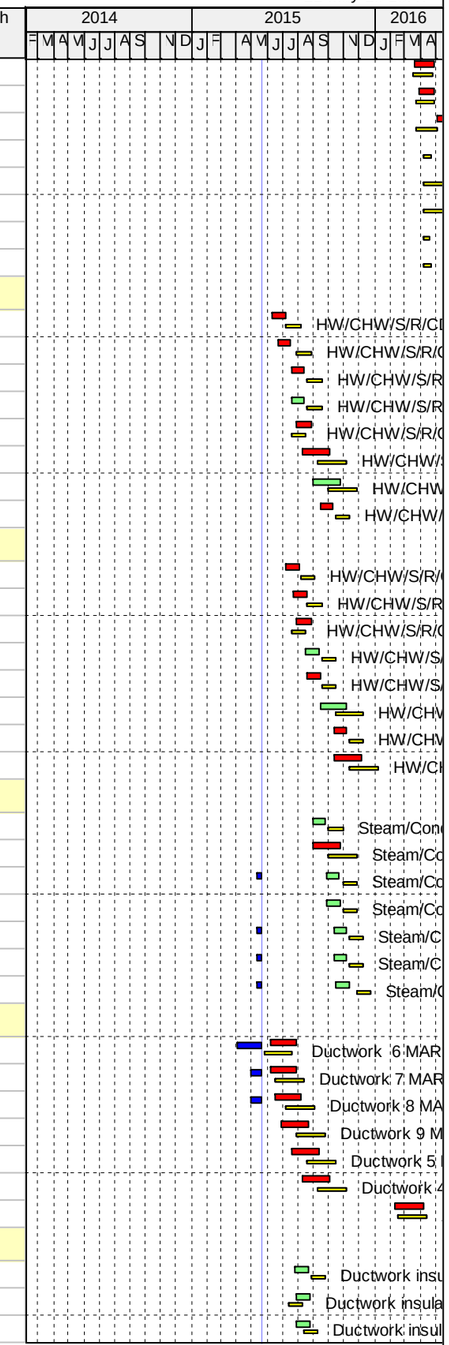

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
DINSM1020	Ductwork insulation 8 MART	20	20	0	0%	-18	03-Sep-15	07-Aug-15		01-Oct-15	03-Sep-15	
DINSM1040	Ductwork insulation 5 MART	20	20	0	0%	-27	15-Oct-15	14-Sep-15		12-Nov-15	09-Oct-15	
DINSM1050	Ductwork insulation 4 MART	30	30	0	0%	-92	05-Nov-15	05-Oct-15		17-Dec-15	13-Nov-15	
HVAC Equipment												
MECHM1320	HWC/HRP Pumps: 10 MART	40	40	0	0%	38	28-Oct-15	07-Sep-15		23-Dec-15	02-Nov-15	
MECHM1400	Chiller installlation: MART	40	40	0	0%	-5	07-Dec-15	17-Dec-15		29-Jan-16	10-Feb-16	
MECHM1360	Chiller Pumps: 3 MART	40	40	0	0%	-5	07-Dec-15	17-Dec-15		29-Jan-16	10-Feb-16	
MECHM1450	HVAC Equipment Roof MART	40	40	0	0%	4	06-Jan-16	18-Dec-15		02-Mar-16	12-Feb-16	
MECHM1460	HVAC Equipment 10 MART	30	30	0	0%	4	06-Jan-16	18-Dec-15		17-Feb-16	29-Jan-16	
HVAC DDC & Secondary Controls												
MECHM1110	HVAC Control wiring 6 MART	20	20	0	0%	57	03-Aug-15	11-Aug-15		31-Aug-15	08-Sep-15	
MECHM1150	HVAC Control wiring 7 MART	20	20	0	0%	57	03-Aug-15	11-Aug-15		31-Aug-15	08-Sep-15	
MECHM1140	HVAC Control wiring 8 MART	20	20	0	0%	-9	14-Aug-15	24-Aug-15		11-Sep-15	21-Sep-15	
MECHM1200	HVAC Control wiring 9 MART	20	20	0	0%	-9	14-Aug-15	24-Aug-15		11-Sep-15	21-Sep-15	
MECHM1350	HVAC Control wiring Roof MART	20	20	0	0%	-44	12-Nov-15	26-Oct-15		10-Dec-15	20-Nov-15	
MECHM1220	HVAC Control wiring 10 MART	20	20	0	0%	-44	12-Nov-15	26-Oct-15		10-Dec-15	20-Nov-15	
MECHM1370	HVAC Control wiring 5 MART	20	20	0	0%	-44	25-Nov-15	06-Nov-15		23-Dec-15	04-Dec-15	
MECHM1390	HVAC Control wiring 4 MART	30	30	0	0%	4	25-Nov-15	06-Nov-15		06-Jan-16	18-Dec-15	
HVAC Grilles												
MECHM1380	Grilles, registers, & diffusers 6 MART	20	20	0	0%	25	18-Feb-16	22-Feb-16		17-Mar-16	18-Mar-16	
MECHM1410	Grilles, registers, & diffusers 7 MART	20	20	0	0%	20	25-Feb-16	29-Feb-16		24-Mar-16	25-Mar-16	
MECHM1420	Grilles, registers, & diffusers 8 MART	20	20	0	0%	-7	25-Feb-16	06-Apr-16		24-Mar-16	04-May-16	
MECHM1480	Grilles, registers, & diffusers 4 MART	40	40	0	0%	-12	03-Mar-16	13-Apr-16		28-Apr-16	08-Jun-16	
MECHM1470	Grilles, registers, & diffusers 5 MART	20	20	0	0%	-12	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	
MECHM1430	Grilles, registers, & diffusers 9 MART	20	20	0	0%	-12	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	
MECHM1440	Grilles, registers, & diffusers 10 MART	20	20	0	0%	-12	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	
Air Terminal Units												
MECHM1070	Air terminal Units 6 MART	20	20	0	0%	71	06-Apr-15	20-May-15		01-May-15	16-Jun-15	
MECHM1080	Air terminal Units 7 MART	20	20	0	0%	51	16-Jul-15	01-Jul-15		13-Aug-15	28-Jul-15	
MECHM1130	Air terminal Units 8 MART	20	20	0	0%	2	06-Aug-15	10-Jul-15		03-Sep-15	06-Aug-15	
MECHM1210	Air terminal Units 9 MART	20	20	0	0%	-11	27-Aug-15	27-Jul-15		24-Sep-15	21-Aug-15	
MECHM1230	Air terminal Units 10 MART	20	20	0	0%	-11	09-Sep-15	07-Aug-15		07-Oct-15	04-Sep-15	
MECHM1270	Air terminal Units 4 MART	40	40	0	0%	-62	10-Sep-15	10-Aug-15		05-Nov-15	02-Oct-15	
MECHM1290	Air terminal Units 5 MART	20	20	0	0%	-11	23-Sep-15	20-Aug-15		20-Oct-15	17-Sep-15	
Conduits, Troughs, Boxes and Fittings												
ELECM1010	Low-voltage conduit 4 MART	30	30	0	0%	-43	08-Jun-15	18-Jun-15		20-Jul-15	30-Jul-15	
ELECM1020	Low-voltage conduit 5 MART	30	30	0	0%	-13	08-Jun-15	18-Jun-15		20-Jul-15	30-Jul-15	
ELECM1080	Low-voltage conduit: 6 MART	30	30	0	0%	-11	22-Jun-15	30-Jun-15		03-Aug-15	11-Aug-15	
ELECM1090	Low-voltage conduit 7 MART	30	30	0	0%	-1	22-Jun-15	30-Jun-15		03-Aug-15	11-Aug-15	
ELECM1130	Low-voltage conduit 3 MART	20	20	0	0%	-43	22-Jun-15	02-Jul-15		20-Jul-15	30-Jul-15	
ELECM1150	Low-voltage conduit: Roof MART	30	30	0	0%	0	03-Jul-15	13-Jul-15		14-Aug-15	24-Aug-15	
ELECM1160	Low-voltage conduit 8 MART	30	30	0	0%	-9	03-Jul-15	13-Jul-15		14-Aug-15	24-Aug-15	
ELECM1170	Low-voltage conduit 9 MART	30	30	0	0%	-9	03-Jul-15	13-Jul-15		14-Aug-15	24-Aug-15	
ELECM1180	Low-voltage conduit 10 MART	30	30	0	0%	0	03-Jul-15	13-Jul-15		14-Aug-15	24-Aug-15	
Panelboards and Switchboards												
ELECM1030	Branch panels 4 MART	20	20	0	0%	-25	08-Jun-15	18-Jun-15		06-Jul-15	16-Jul-15	

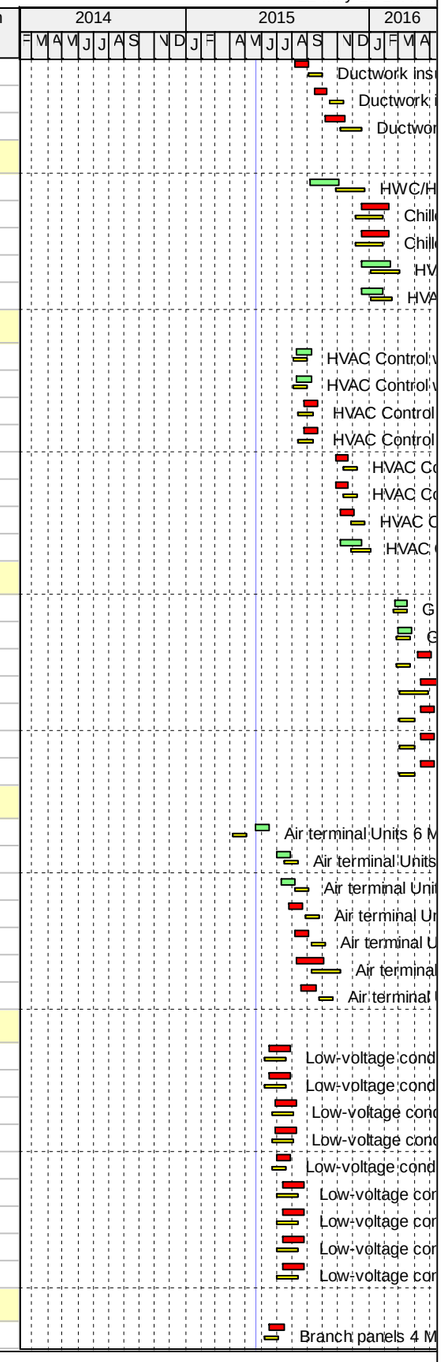

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
ELECM1040	Branch panels: 5 MART	20	20	0	0%	35	08-Jun-15	18-Jun-15		06-Jul-15	16-Jul-15	
ELECM1050	Branch panels 3 MART	10	10	0	0%	32	08-Jun-15	18-Jun-15		22-Jun-15	02-Jul-15	
ELECM1100	Branch panels: 6 MART	10	10	0	0%	27	22-Jun-15	30-Jun-15		06-Jul-15	14-Jul-15	
ELECM1110	Branch panels 7 MART	30	30	0	0%	42	22-Jun-15	30-Jun-15		03-Aug-15	11-Aug-15	
ELECM1190	Branch panels 8 MART	30	30	0	0%	0	03-Jul-15	13-Jul-15		14-Aug-15	24-Aug-15	
ELECM1200	Branch panels 9 MART	30	30	0	0%	20	03-Jul-15	13-Jul-15		14-Aug-15	24-Aug-15	
Branch Wiring: Power & Lighting												
ELECM1070	Branch wiring 7 MART	30	30	0	0%	49	22-Jun-15	30-Jun-15		03-Aug-15	11-Aug-15	
ELECM1060	Branch wiring 5 MART	30	30	0	0%	47	22-Jun-15	02-Jul-15		03-Aug-15	13-Aug-15	
ELECM1120	Branch wiring 3 MART	5	5	0	0%	62	22-Jun-15	02-Jul-15		29-Jun-15	09-Jul-15	
ELECM1140	Branch wiring 8 MART	30	30	0	0%	59	03-Jul-15	13-Jul-15		14-Aug-15	24-Aug-15	
ELECM1210	Branch wiring 6 MART	30	30	0	0%	27	06-Jul-15	14-Jul-15		17-Aug-15	25-Aug-15	
ELECM1000	Branch wiring 4 MART	40	40	0	0%	0	06-Jul-15	16-Jul-15		31-Aug-15	10-Sep-15	
ELECM1240	Branch wiring 10 MART	30	30	0	0%	29	17-Jul-15	27-Jul-15		28-Aug-15	07-Sep-15	
ELECM1230	Branch wiring 9 MART	30	30	0	0%	29	14-Aug-15	24-Aug-15		25-Sep-15	05-Oct-15	
ELECM1220	Branch wiring Roof MART	20	20	0	0%	17	31-Aug-15	10-Sep-15		28-Sep-15	08-Oct-15	
Motor Connections												
ELECM1310	Motor connection 8 MART	10	10	0	0%	-18	17-Sep-15	21-Aug-15		01-Oct-15	03-Sep-15	
ELECM1280	Motor connection 6 MART	10	10	0	0%	21	11-Aug-15	26-Aug-15		25-Aug-15	08-Sep-15	
ELECM1290	Motor connection 7 MART	10	10	0	0%	31	10-Sep-15	26-Aug-15		24-Sep-15	08-Sep-15	
ELECM1350	Motor connection 9 MART	10	10	0	0%	-18	01-Oct-15	04-Sep-15		15-Oct-15	17-Sep-15	
ELECM1380	Motor connection 5 MART	10	10	0	0%	-27	12-Nov-15	12-Oct-15		26-Nov-15	23-Oct-15	
ELECM1420	Motor connection 4 MART	20	20	0	0%	-92	19-Nov-15	19-Oct-15		17-Dec-15	13-Nov-15	
ELECM1430	Motor connection 3 MART	5	5	0	0%	-44	19-Nov-15	19-Oct-15		26-Nov-15	23-Oct-15	
ELECM1450	Motor connection Roof MART	10	10	0	0%	18	12-Nov-15	26-Oct-15		26-Nov-15	06-Nov-15	
ELECM1460	Motor connection 10 MART	10	10	0	0%	-44	12-Nov-15	26-Oct-15		26-Nov-15	06-Nov-15	
ELECM1260	Switchgear installation MART	30	30	0	0%	-7	13-Oct-15	27-Oct-15		23-Nov-15	08-Dec-15	
Cable Trays & Ladder Racks												
CTM1020	COMMS Cable trays 8 MART	20	20	0	0%	52	01-Oct-15	04-Sep-15		29-Oct-15	01-Oct-15	
CTM1000	COMMS Cable trays: 7 MART	20	20	0	0%	31	24-Sep-15	09-Sep-15		22-Oct-15	06-Oct-15	
CTM1030	COMMS Cable trays 9 MART	20	20	0	0%	61	15-Oct-15	18-Sep-15		12-Nov-15	15-Oct-15	
CTM1010	COMMS Cable trays: 6 MART	20	20	0	0%	-9	09-Oct-15	21-Oct-15		06-Nov-15	18-Nov-15	
CTM1040	COMMS Cable trays 5 MART	20	20	0	0%	-27	26-Nov-15	26-Oct-15		24-Dec-15	20-Nov-15	
CTM1050	COMMS Cable trays 4 MART	40	40	0	0%	-92	19-Nov-15	16-Nov-15		14-Jan-16	08-Jan-16	
Wiring Devices												
ELECM1400	Wiring devices 5 MART	20	20	0	0%	9	06-Nov-15	06-Oct-15		04-Dec-15	02-Nov-15	
ELECM1390	Wiring devices 4 MART	20	20	0	0%	13	14-Oct-15	14-Oct-15		11-Nov-15	11-Nov-15	
ELECM1340	Wiring devices 3 MART	20	20	0	0%	13	14-Oct-15	14-Oct-15		11-Nov-15	11-Nov-15	
ELECM1250	Wiring devices 6 MART	20	20	0	0%	7	28-Oct-15	05-Nov-15		25-Nov-15	03-Dec-15	
ELECM1330	Wiring devices 7 MART	20	20	0	0%	-3	28-Oct-15	19-Nov-15		25-Nov-15	17-Dec-15	
ELECM1370	Wiring devices 9 MART	20	20	0	0%	-13	28-Oct-15	02-Dec-15		25-Nov-15	30-Dec-15	
ELECM1320	Wiring devices 8 MART	20	20	0	0%	-13	28-Oct-15	02-Dec-15		25-Nov-15	30-Dec-15	
ELECM1300	Wiring devices 10 MART	20	20	0	0%	-43	06-Nov-15	16-Dec-15		04-Dec-15	13-Jan-16	
ELECM1270	Wiring devices Roof MART	10	10	0	0%	-43	06-Nov-15	30-Dec-15		20-Nov-15	13-Jan-16	
Electrical Light Fixtures												
ELECM1520	Light Fixtures 4 MART	10	10	0	0%	-57	10-Mar-16	14-Mar-16		24-Mar-16	25-Mar-16	

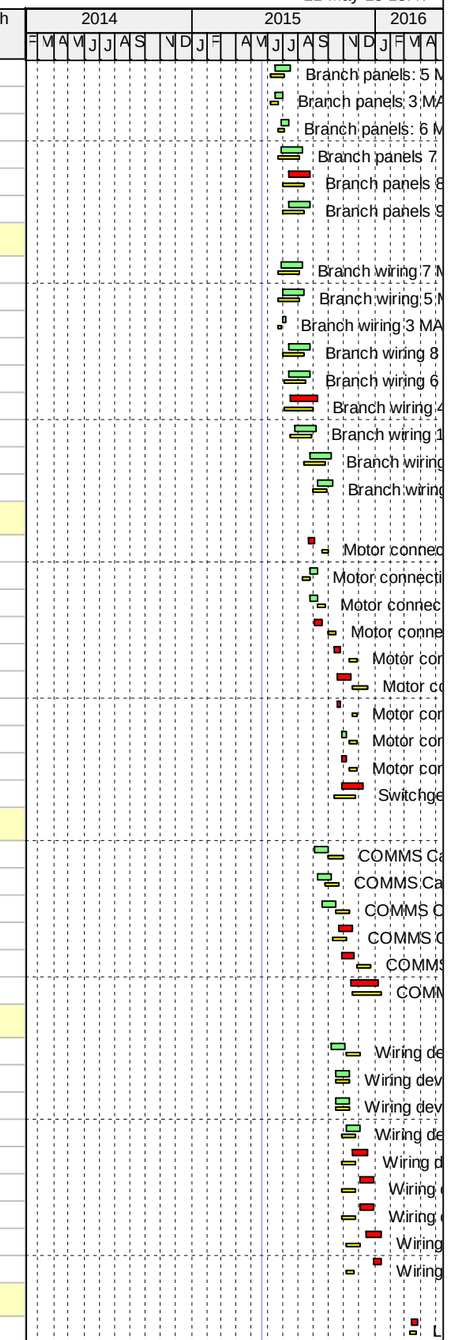

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
ELECM1440	Light Fixtures 6 MART	20	20	0	0%	-52	17-Mar-16	21-Mar-16		14-Apr-16	15-Apr-16	
ELECM1500	Light Fixtures 5 MART	25	25	0	0%	-67	17-Mar-16	21-Mar-16		21-Apr-16	22-Apr-16	
ELECM1600	Exam Room Specialty Lighting 5 MART	20	20	0	0%	-12	17-Mar-16	21-Mar-16		14-Apr-16	15-Apr-16	
ELECM1610	Exam Room Specialty Lighting 6 MART	20	20	0	0%	-12	17-Mar-16	21-Mar-16		14-Apr-16	15-Apr-16	
ELECM1480	Light Fixtures 7 MART	20	20	0	0%	-47	24-Mar-16	28-Mar-16		21-Apr-16	22-Apr-16	
ELECM1530	Light Fixtures 3 MART	15	15	0	0%	-92	10-Mar-16	28-Mar-16		17-Mar-16	15-Apr-16	
ELECM1620	Exam Room Specialty Lighting 7 MART	20	20	0	0%	-17	24-Mar-16	28-Mar-16		21-Apr-16	22-Apr-16	
ELECM1410	Light Fixtures 8 MART	20	20	0	0%	-44	25-Feb-16	06-Apr-16		24-Mar-16	04-May-16	
ELECM1470	Light Fixtures 9 MART	20	20	0	0%	-39	03-Mar-16	13-Apr-16		31-Mar-16	11-May-16	
UPS												
ELECM1360	UPS System, MART	40	40	0	0%	-18	29-Sep-15	29-Oct-15		23-Nov-15	23-Dec-15	
Lighting Control Systems												
ELECM1590	Lighting control systems 4 MART	20	20	0	0%	-92	17-Mar-16	18-Apr-16		31-Mar-16	13-May-16	
ELECM1550	Lighting control systems 3 MART	20	20	0	0%	-92	17-Mar-16	18-Apr-16		24-Mar-16	13-May-16	
ELECM1570	Lighting control systems 5 MART	20	20	0	0%	-92	24-Mar-16	02-May-16		21-Apr-16	27-May-16	
ELECM1490	Lighting control systems 6 MART	20	20	0	0%	-92	07-Apr-16	16-May-16		28-Apr-16	10-Jun-16	
ELECM1510	Lighting control systems 7 MART	20	20	0	0%	-92	07-Apr-16	30-May-16		28-Apr-16	24-Jun-16	
ELECM1540	Lighting control systems 8 MART	20	20	0	0%	-92	07-Apr-16	13-Jun-16		28-Apr-16	08-Jul-16	
ELECM1560	Lighting control systems 9 MART	20	20	0	0%	-92	07-Apr-16	27-Jun-16		28-Apr-16	22-Jul-16	
ELECM1580	Lighting control system programming, MART	20	20	0	0%	-92	07-Apr-16	11-Jul-16		06-May-16	05-Aug-16	
Fire Detection and Alarm System												
FAM1080	Fire Alarm wiring 3 MART	30	30	0	0%	-43	20-Jul-15	30-Jul-15		17-Aug-15	10-Sep-15	
FAM1060	Fire Alarm wiring 4 MART	40	40	0	0%	-43	20-Jul-15	13-Aug-15		14-Sep-15	08-Oct-15	
FAM1070	Fire Alarm wiring 5 MART	30	30	0	0%	-43	20-Jul-15	10-Sep-15		17-Aug-15	22-Oct-15	
FAM1000	Fire Alarm wiring 6 MART	30	30	0	0%	-43	03-Aug-15	24-Sep-15		31-Aug-15	05-Nov-15	
FAM1010	Fire Alarm wiring 7 MART	30	30	0	0%	-43	03-Aug-15	08-Oct-15		31-Aug-15	19-Nov-15	
FAM1020	Fire Alarm wiring 8 MART	30	30	0	0%	-43	14-Aug-15	21-Oct-15		11-Sep-15	02-Dec-15	
FAM1030	Fire Alarm wiring 9 MART	30	30	0	0%	-13	14-Aug-15	21-Oct-15		11-Sep-15	02-Dec-15	
FAM1050	Fire Alarm wiring 10 MART	30	30	0	0%	-43	11-Sep-15	04-Nov-15		09-Oct-15	16-Dec-15	
FAM1040	Fire Alarm wiring Roof MART	30	30	0	0%	-43	11-Sep-15	18-Nov-15		25-Sep-15	30-Dec-15	
FAM1090	FACPs MART (MS2)	30	30	0	0%	-55	23-Dec-15	01-Feb-16		03-Feb-16	14-Mar-16	
FAM1100	FA Programming (MS2) MART	42	42	0	0%	-55	20-Jan-16	29-Feb-16		18-Mar-16	27-Apr-16	
Work by Owner												
SECM1020	Security/Access wiring 4 MART	5	5	0	0%	-67	14-Jan-16	11-Jan-16		21-Jan-16	15-Jan-16	
COMMSM1(	COMMS wiring 4 MART	10	10	0	0%	-92	14-Jan-16	11-Jan-16		21-Jan-16	22-Jan-16	
SECM1010	Security/Access wiring 3 MART	5	5	0	0%	-67	14-Jan-16	11-Jan-16		21-Jan-16	15-Jan-16	
AVM1000	AV wiring 4 MART	5	5	0	0%	-29	14-Jan-16	11-Jan-16		21-Jan-16	15-Jan-16	
SECM1030	Security/Access wiring 5 MART	5	5	0	0%	-67	21-Jan-16	18-Jan-16		28-Jan-16	22-Jan-16	
SECM1040	Security/Access wiring 6 MART	5	5	0	0%	-24	21-Jan-16	18-Jan-16		28-Jan-16	22-Jan-16	
COMMSM1(	COMMS wiring 5 MART	10	10	0	0%	-67	21-Jan-16	18-Jan-16		28-Jan-16	29-Jan-16	
COMMSM1(	COMMS wiring 6 MART	10	10	0	0%	-52	21-Jan-16	18-Jan-16		28-Jan-16	29-Jan-16	
AVM1010	AV wiring 5 MART	5	5	0	0%	-29	21-Jan-16	18-Jan-16		28-Jan-16	22-Jan-16	
AVM1020	AV wiring 6 MART	5	5	0	0%	-29	21-Jan-16	18-Jan-16		28-Jan-16	22-Jan-16	
COMMSM1(	COMMS wiring 7 MART	10	10	0	0%	-47	28-Jan-16	25-Jan-16		04-Feb-16	05-Feb-16	
SECM1050	Security/Access wiring 7 MART	5	5	0	0%	-57	28-Jan-16	02-Mar-16		04-Feb-16	09-Mar-16	
SECM1060	Security/Access wiring 8 MART	5	5	0	0%	-57	28-Jan-16	02-Mar-16		04-Feb-16	09-Mar-16	

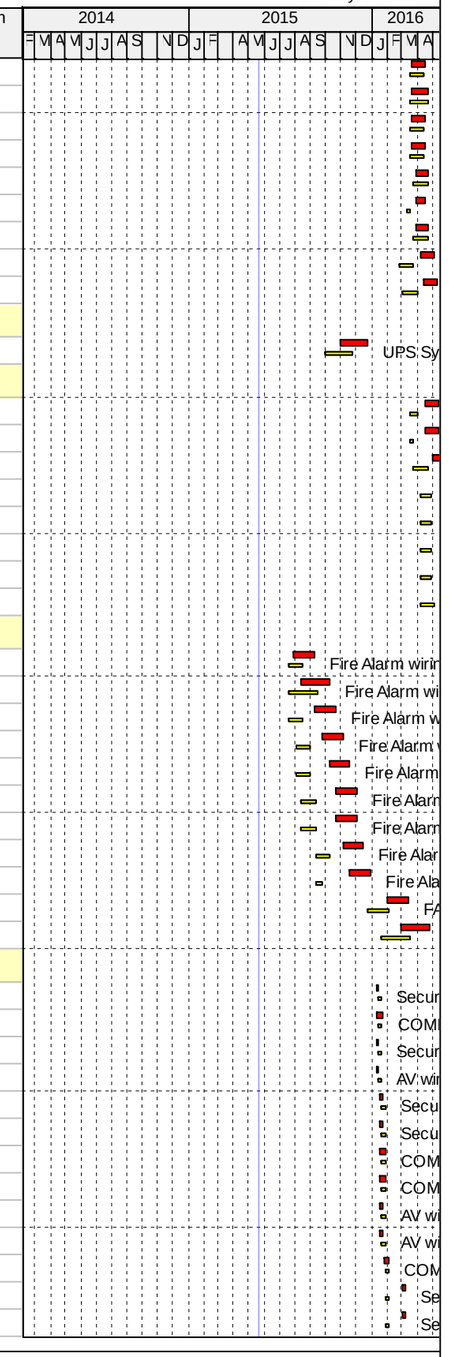

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
COMMSM1(	COMMS wiring 8 MART	10	10	0	0%	-57	28-Jan-16	02-Mar-16		04-Feb-16	16-Mar-16	
AVM1030	AV wiring 7 MART	5	5	0	0%	-57	28-Jan-16	02-Mar-16		04-Feb-16	09-Mar-16	
AVM1040	AV wiring 8 MART	5	5	0	0%	-19	28-Jan-16	02-Mar-16		04-Feb-16	09-Mar-16	
COMMSM1(	COMMS wiring 9 MART	10	10	0	0%	-52	04-Feb-16	09-Mar-16		11-Feb-16	23-Mar-16	
AVM1050	AV wiring 9 MART	5	5	0	0%	-19	04-Feb-16	09-Mar-16		11-Feb-16	16-Mar-16	
SECM1080	Security/Access wiring Roof MART	5	5	0	0%	6	11-Feb-16	16-Mar-16		18-Feb-16	23-Mar-16	
SECM1070	Security/Access wiring 9 MART	5	5	0	0%	-19	11-Feb-16	16-Mar-16		18-Feb-16	23-Mar-16	
SECM1000	Security/Access wiring 10 MART	5	5	0	0%	-19	11-Feb-16	16-Mar-16		18-Feb-16	23-Mar-16	
COMMSM1(	COMMS wiring Roof MART	10	10	0	0%	-24	11-Feb-16	23-Mar-16		18-Feb-16	06-Apr-16	
COMMSM1(	COMMS wiring 10 MART	10	10	0	0%	-24	11-Feb-16	23-Mar-16		18-Feb-16	06-Apr-16	
Bed Tower												
General Requirements												
CON6400	C&S Concrete Deck & Fireproofing: Bed Tower 4	5	5	0	0%	-78	15-Jun-15	15-Jun-15		22-Jun-15	22-Jun-15	
Concrete												
CON6390	Concrete: Bed Tower Level 4	10	10	0	0%	53	14-Dec-15	13-Jan-16		25-Dec-15	26-Jan-16	
CON6300	Level 5 Circular stair infill	10	10	0	0%	-12	14-Dec-15	13-Jan-16		25-Dec-15	26-Jan-16	
CON11020	Concrete infill: Bed Tower Level 5 at shelving	10	10	0	0%	63	14-Dec-15	13-Jan-16		25-Dec-15	26-Jan-16	
CON11600	Concrete: Bed Tower Level 5	10	10	0	0%	-12	14-Dec-15	13-Jan-16		25-Dec-15	26-Jan-16	
CON11610	Concrete: Bed Tower Level 6	10	10	0	0%	76	28-Dec-15	27-Jan-16		08-Jan-16	09-Feb-16	
CON11620	Concrete: Bed Tower Level 7	10	10	0	0%	76	11-Jan-16	10-Feb-16		22-Jan-16	23-Feb-16	
CON11630	Concrete: Bed Tower Level 8	10	10	0	0%	76	25-Jan-16	24-Feb-16		05-Feb-16	08-Mar-16	
CON11640	Concrete: Bed Tower Level 9	10	10	0	0%	76	08-Feb-16	09-Mar-16		19-Feb-16	22-Mar-16	
Masonry												
CON5580	CMU Partitions: Bed Tower Level 1	20	20	0	0%	107	23-Jul-15	29-Jul-15		20-Aug-15	25-Aug-15	
CON5590	CMU Partitions: Bed Tower Level 2	20	20	0	0%	107	05-Aug-15	11-Aug-15		02-Sep-15	08-Sep-15	
CON5600	CMU Partitions: Bed Tower Level 3	20	20	0	0%	107	05-Aug-15	11-Aug-15		02-Sep-15	08-Sep-15	
Structural Steel												
CON10460	Misc. structural framing Bed Tower Level 4	20	20	0	0%	15	19-Jun-15	29-Jul-15		16-Jul-15	25-Aug-15	
CON10470	Misc. structural framing Bed Tower Level 5	30	30	0	0%	38	19-Jun-15	29-Jul-15		30-Jul-15	08-Sep-15	
CON10490	Guide-rail support for operable partitions Bed Tower Level 4	10	10	0	0%	68	15-Oct-15	17-Sep-15		29-Oct-15	01-Oct-15	
CON11450	Guide-rail support for operable partitions Bed Tower Level 5	10	10	0	0%	30	17-Sep-15	08-Oct-15		01-Oct-15	22-Oct-15	
CON5221	Strutural Steel/PBW/Decking/ & Concrete at Circular Stair Opening ((BT)	10	10	0	0%	-12	05-Oct-15	04-Nov-15		16-Oct-15	17-Nov-15	
Miscellaneous Metal												
MMETBT10	Millwork Steel Supports Level 5	30	30	0	0%	-71	23-Oct-15	10-Dec-15		04-Dec-15	21-Jan-16	
MMETBT10	Millwork Steel Supports Level 4	30	30	0	0%	-81	17-Nov-15	24-Dec-15		29-Dec-15	04-Feb-16	
MMETBT10	Millwork Steel Supports Level 6	30	30	0	0%	-8	09-Dec-15	04-Feb-16		20-Jan-16	17-Mar-16	
MMETBT10	Millwork Steel Supports Level 7	30	30	0	0%	18	17-Dec-15	04-Feb-16		28-Jan-16	17-Mar-16	
MMETBT10	Millwork Steel Supports Level 8	30	30	0	0%	18	07-Jan-16	25-Feb-16		18-Feb-16	07-Apr-16	
MMETBT10	Millwork Steel Supports Level 9	30	30	0	0%	5	12-Jan-16	15-Mar-16		23-Feb-16	26-Apr-16	
Steel Stairs												
CON10630	Circular stairs: Bed Tower Level 5	40	40	0	0%	-12	19-Oct-15	18-Nov-15		11-Dec-15	12-Jan-16	
Metal Composite Panels												
CON6700	Ornamental metal & stair railings: Bed Tower Level 6	20	20	0	0%	33	02-Mar-16	09-Mar-16		29-Mar-16	05-Apr-16	
Carpentry												
CON420	Partition Layout (Bed Tower) (ST 25 CONSTRAINS ES)	60	60	0	0%	-81	25-Jun-15	25-Jun-15		17-Sep-15	17-Sep-15	

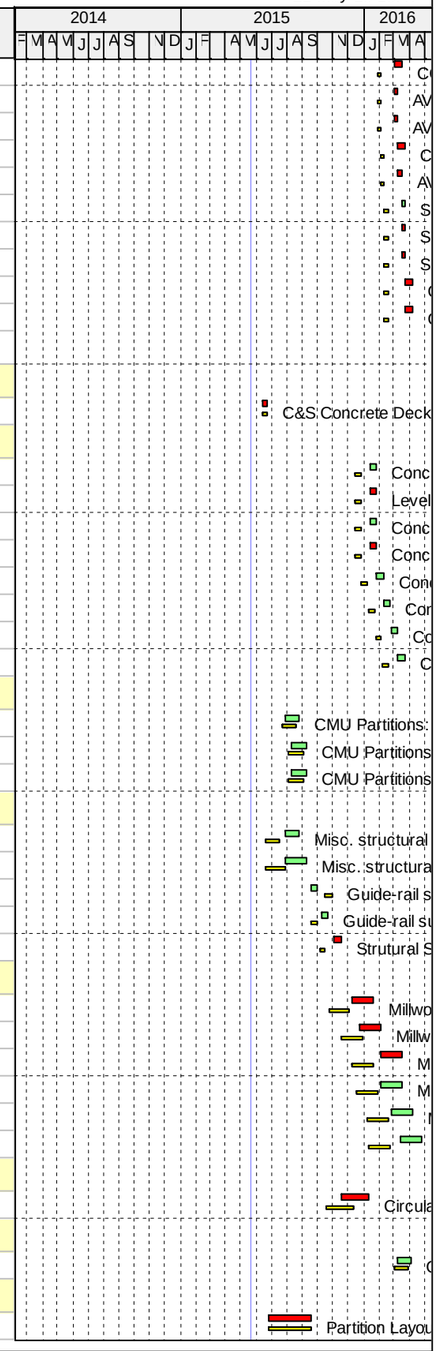

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
CON440	Install radiation shielding	5	5	0	0%	-27	20-Jan-16	02-Mar-16		27-Jan-16	09-Mar-16	
Hollow Metal Doors												
HCMBT1040	HCM doors & Frames: Bed Tower Level 1	2	2	0	0%	26	26-Oct-15	15-Jan-16		28-Oct-15	19-Jan-16	
HCMBT1010	HCM doors & Frames: Bed Tower Level 2	5	5	0	0%	22	05-Nov-15	21-Jan-16		12-Nov-15	28-Jan-16	
HCMBT1000	HCM doors & Frames: Bed Tower Level 3	20	20	0	0%	22	12-Nov-15	28-Jan-16		10-Dec-15	25-Feb-16	
HCMBT1020	HCM doors & Frames: Bed Tower Level 4	20	20	0	0%	17	26-Jan-16	04-Feb-16		23-Feb-16	03-Mar-16	
HCMBT1030	HCM doors & Frames: Bed Tower Level 5	20	20	0	0%	17	23-Feb-16	03-Mar-16		22-Mar-16	31-Mar-16	
HCMBT1090	HCM doors & Frames: Bed Tower Level 10	2	2	0	0%	55	23-Feb-16	03-Mar-16		25-Feb-16	07-Mar-16	
HCMBT1050	HCM doors & Frames: Bed Tower Level 6	20	20	0	0%	31	02-Mar-16	13-Apr-16		30-Mar-16	11-May-16	
HCMBT1060	HCM doors & Frames: Bed Tower Level 7	20	20	0	0%	31	22-Mar-16	13-Apr-16		19-Apr-16	11-May-16	
HCMBT1070	HCM doors & Frames: Bed Tower Level 8	20	20	0	0%	31	19-Apr-16	11-May-16		17-May-16	08-Jun-16	
HCMBT1080	HCM doors & Frames: Bed Tower Level 9	20	20	0	0%	32	19-Apr-16	07-Jun-16		17-May-16	05-Jul-16	
PLAM Doors												
PLAMBT10	PLAM doors: Bed Tower Level 1	20	20	0	0%	-8	06-Jan-16	06-Apr-16		03-Feb-16	04-May-16	
PLAMBT10	PLAM doors: Bed Tower Level 2	20	20	0	0%	12	06-Jan-16	06-Apr-16		03-Feb-16	04-May-16	
PLAMBT10	PLAM doors: Bed Tower Level 3	20	20	0	0%	-8	04-Feb-16	05-May-16		02-Mar-16	01-Jun-16	
PLAMBT10	PLAM doors: Bed Tower Level 4	20	20	0	0%	-8	15-Mar-16	05-May-16		12-Apr-16	01-Jun-16	
PLAMBT10	PLAM doors: Bed Tower Level 5	20	20	0	0%	-8	15-Mar-16	05-May-16		12-Apr-16	01-Jun-16	
PLAMBT10	PLAM doors: Bed Tower Level 6	20	20	0	0%	-5	20-Apr-16	02-Jun-16		18-May-16	29-Jun-16	
PLAMBT10	PLAM doors: Bed Tower Level 7	20	20	0	0%	-5	20-Apr-16	02-Jun-16		18-May-16	29-Jun-16	
PLAMBT10	PLAM doors: Bed Tower Level 8	20	20	0	0%	-40	19-May-16	18-Aug-16		16-Jun-16	15-Sep-16	
PLAMBT10	PLAM doors: Bed Tower Level 9	20	20	0	0%	0	19-May-16	18-Aug-16		16-Jun-16	15-Sep-16	
Specialty Doors & Frames												
CON11070	Install Operable Partition Bed Tower Level 4	20	20	0	0%	-12	14-Dec-15	08-Feb-16		08-Jan-16	04-Mar-16	
CON11060	Install WON door assemblies Bed Tower Level 5	30	30	0	0%	5	11-Jan-16	07-Mar-16		19-Feb-16	15-Apr-16	
CON11080	Install Operable Partition Bed Tower Level 5	30	30	0	0%	-12	11-Jan-16	07-Mar-16		19-Feb-16	15-Apr-16	
Door Hardware												
HWRBT1000	Door hardware: Bed Tower Level 1	2	2	0	0%	-8	03-Feb-16	04-May-16		05-Feb-16	06-May-16	
HWRBT1010	Door hardware: Bed Tower Level 2	20	20	0	0%	-8	03-Feb-16	04-May-16		02-Mar-16	01-Jun-16	
HWRBT1030	Door hardware: Bed Tower Level 3	20	20	0	0%	-8	04-Feb-16	05-May-16		02-Mar-16	01-Jun-16	
HWRBT1040	Door hardware: Bed Tower Level 4	20	20	0	0%	-8	15-Mar-16	05-May-16		12-Apr-16	01-Jun-16	
HWRBT1020	Door hardware: Bed Tower Level 5	20	20	0	0%	-8	22-Mar-16	05-May-16		19-Apr-16	01-Jun-16	
HWRBT1050	Door hardware: Bed Tower Level 6	20	20	0	0%	15	20-Apr-16	02-Jun-16		18-May-16	29-Jun-16	
HWRBT1060	Door hardware: Bed Tower Level 7	20	20	0	0%	15	18-May-16	30-Jun-16		15-Jun-16	27-Jul-16	
HWRBT1070	Door hardware: Bed Tower Level 8	20	20	0	0%	-40	16-Jun-16	15-Sep-16		14-Jul-16	13-Oct-16	
HWRBT1080	Door hardware: Bed Tower Level 9	20	20	0	0%	-40	14-Jul-16	13-Oct-16		11-Aug-16	10-Nov-16	
Aluminum Storefront												
SFBT1000	Interior Storefront installations (rated) 5	40	40	0	0%	2	12-Feb-16	24-Mar-16		08-Apr-16	19-May-16	
SFBT1010	Interior Storefront installations (non-rated) 5	40	40	0	0%	2	12-Feb-16	24-Mar-16		08-Apr-16	19-May-16	
SFBT1020	Interior Storefront installations (rated) 6	40	40	0	0%	16	20-Apr-16	01-Jun-16		15-Jun-16	27-Jul-16	
SFBT1030	Interior Storefront installations (non-rated) 6	40	40	0	0%	16	18-May-16	29-Jun-16		13-Jul-16	24-Aug-16	
Light-gauge Metal Framing												
GWBBT1000	Interior Framing: Bed Tower Level 1	10	10	0	0%	-31	25-Jun-15	25-Jun-15		09-Jul-15	09-Jul-15	
GWBBT1010	Interior Framing: Bed Tower Level 2	10	10	0	0%	-31	25-Jun-15	25-Jun-15		09-Jul-15	09-Jul-15	
GWBBT1020	Interior Framing: Bed Tower Level 3	20	20	0	0%	-31	25-Jun-15	25-Jun-15		23-Jul-15	23-Jul-15	
GWBBT1030	Interior Framing: Bed Tower Level 4	20	20	0	0%	-31	08-Jul-15	08-Jul-15		05-Aug-15	05-Aug-15	

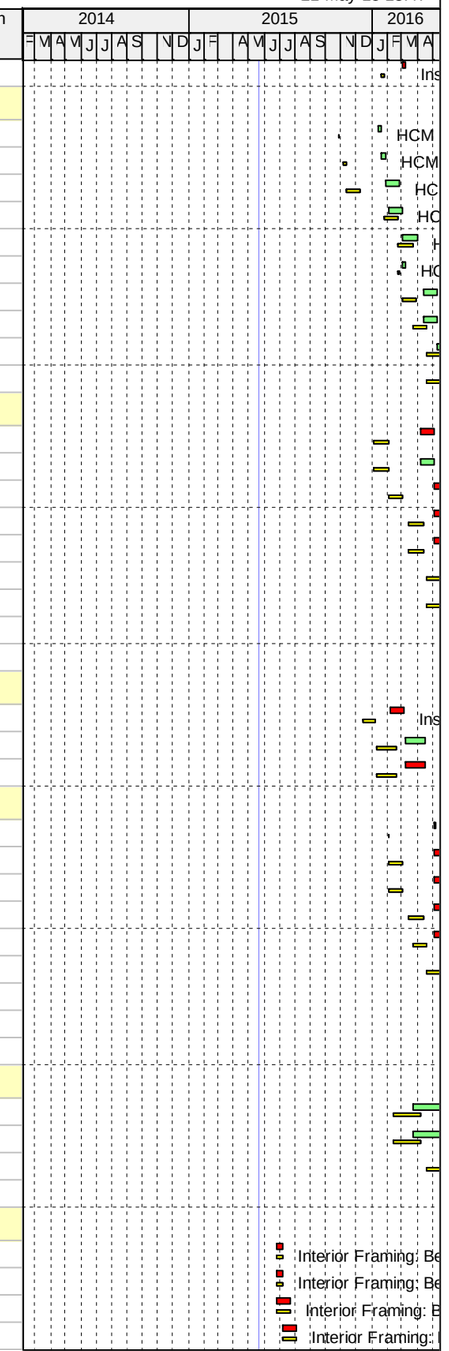

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
GWBBT1040	Interior Framing: Bed Tower Level 5	20	20	0	0%	-31	08-Jul-15	08-Jul-15		05-Aug-15	05-Aug-15	
GWBBT1050	Interior Framing: Bed Tower Level 6	20	20	0	0%	-9	22-Jul-15	22-Jul-15		19-Aug-15	19-Aug-15	
GWBBT1060	Interior Framing: Bed Tower Level 7	20	20	0	0%	-9	22-Jul-15	22-Jul-15		19-Aug-15	19-Aug-15	
GWBBT1070	Interior Framing: Bed Tower Level 8	20	20	0	0%	2	05-Aug-15	05-Aug-15		02-Sep-15	02-Sep-15	
GWBBT1080	Interior Framing: Bed Tower Level 9	20	20	0	0%	12	05-Aug-15	05-Aug-15		02-Sep-15	02-Sep-15	
GWB Walls												
GWBBT1110	GWB Partitions: Bed Tower Level 3	20	20	0	0%	-26	28-Sep-15	19-Nov-15		26-Oct-15	17-Dec-15	
GWBBT1090	GWB Partitions: Bed Tower Level 1	20	20	0	0%	-47	28-Sep-15	18-Dec-15		26-Oct-15	15-Jan-16	
GWBBT1100	GWB Partitions: Bed Tower Level 2	20	20	0	0%	-56	08-Oct-15	24-Dec-15		05-Nov-15	21-Jan-16	
GWBBT1130	GWB Partitions: Bed Tower Level 5	20	20	0	0%	-72	04-Dec-15	25-Dec-15		01-Jan-16	22-Jan-16	
GWBBT1120	GWB Partitions: Bed Tower Level 4	20	20	0	0%	-81	29-Dec-15	07-Jan-16		26-Jan-16	04-Feb-16	
GWBBT1220	GWB Partitions: Bed Tower Level 8	30	30	0	0%	15	07-Jan-16	01-Mar-16		18-Feb-16	12-Apr-16	
GWBBT1190	GWB Partitions: Bed Tower Level 6	30	30	0	0%	-27	20-Jan-16	02-Mar-16		02-Mar-16	13-Apr-16	
GWBBT1200	GWB Partitions: Bed Tower Level 7	30	30	0	0%	6	20-Jan-16	02-Mar-16		02-Mar-16	13-Apr-16	
GWBBT1230	GWB Partitions: Bed Tower Level 9	30	30	0	0%	-25	23-Feb-16	26-Apr-16		05-Apr-16	07-Jun-16	
Acoustical Wall & Ceiling Panels												
AWPBT1000	Acoustical wall panels: Bed Tower Level 4	20	20	0	0%	27	02-Feb-16	17-Mar-16		01-Mar-16	13-Apr-16	
AWPBT1010	Acoustical wall panels: Bed Tower Level 5	20	20	0	0%	27	02-Feb-16	17-Mar-16		01-Mar-16	13-Apr-16	
AWPBT1020	Acoustical wall panels: Bed Tower Level 6	20	20	0	0%	36	20-Apr-16	01-Jun-16		18-May-16	29-Jun-16	
AWPBT1030	Acoustical wall panels: Bed Tower Level 7	20	20	0	0%	27	20-Apr-16	14-Jun-16		18-May-16	12-Jul-16	
AWPBT1040	Acoustical wall panels: Bed Tower Level 8	20	20	0	0%	0	19-May-16	18-Aug-16		16-Jun-16	15-Sep-16	
AWPBT1050	Acoustical wall panels: Bed Tower Level 9	20	20	0	0%	0	24-May-16	18-Aug-16		21-Jun-16	15-Sep-16	
GWB Ceilings												
GWBBT1180	GWB Ceilings: Bed Tower Level 5	20	20	0	0%	-50	01-Dec-15	14-Jan-16		29-Dec-15	11-Feb-16	
GWBBT1170	GWB Ceilings: Bed Tower Level 4	20	20	0	0%	-33	05-Jan-16	18-Feb-16		02-Feb-16	16-Mar-16	
GWBBT1210	GWB Ceilings: Bed Tower Level 6	30	30	0	0%	-20	27-Jan-16	09-Mar-16		09-Mar-16	20-Apr-16	
GWBBT1150	GWB Ceilings: Bed Tower Level 3	20	20	0	0%	-47	10-Dec-15	10-Mar-16		06-Jan-16	06-Apr-16	
GWBBT1140	GWB Ceilings: Bed Tower Level 1	5	5	0	0%	-33	17-Dec-15	17-Mar-16		23-Dec-15	23-Mar-16	
GWBBT1240	GWB Ceilings: Bed Tower Level 7	30	30	0	0%	-8	27-Jan-16	22-Mar-16		09-Mar-16	03-May-16	
GWBBT1160	GWB Ceilings: Bed Tower Level 2	5	5	0	0%	-35	24-Dec-15	24-Mar-16		30-Dec-15	30-Mar-16	
GWBBT1250	GWB Ceilings: Bed Tower Level 9	30	30	0	0%	5	01-Mar-16	03-May-16		12-Apr-16	14-Jun-16	
GWBBT1260	GWB Ceilings: Bed Tower Level 8	30	30	0	0%	-40	25-Feb-16	26-May-16		07-Apr-16	07-Jul-16	
Suspended Acoustical Ceiling												
ACTBT1000	HPL soffits: Bed Tower Level 5	20	20	0	0%	-16	04-Dec-15	25-Dec-15		01-Jan-16	22-Jan-16	
ACTBT1050	ACT Ceilings: Bed Tower Level 5	20	20	0	0%	-30	04-Dec-15	14-Jan-16		01-Jan-16	11-Feb-16	
ACTBT1030	ACT Ceilings: Bed Tower Level 4	20	20	0	0%	-32	05-Jan-16	18-Feb-16		02-Feb-16	16-Mar-16	
ACTBT1060	HPL soffits: Bed Tower Level 6	20	20	0	0%	-29	20-Jan-16	02-Mar-16		17-Feb-16	30-Mar-16	
ACTBT1070	HPL soffits: Bed Tower Level 7	20	20	0	0%	1	20-Jan-16	02-Mar-16		17-Feb-16	30-Mar-16	
ACTBT1010	ACT Ceilings: Bed Tower Level 3	5	5	0	0%	-27	03-Dec-15	03-Mar-16		09-Dec-15	09-Mar-16	
ACTBT1020	ACT Ceilings: Bed Tower Level 2	10	10	0	0%	-27	05-Jan-16	24-Mar-16		19-Jan-16	06-Apr-16	
ACTBT1080	ACT Ceilings: Bed Tower Level 6	40	40	0	0%	-29	17-Feb-16	30-Mar-16		13-Apr-16	25-May-16	
ACTBT1100	ACT Ceilings: Bed Tower Level 7	40	40	0	0%	1	17-Feb-16	30-Mar-16		13-Apr-16	25-May-16	
ACTBT1040	HPL soffits: Bed Tower Level 8	20	20	0	0%	-27	19-Jan-16	07-Apr-16		16-Feb-16	04-May-16	
ACTBT1090	HPL soffits: Bed Tower Level 9	20	20	0	0%	-27	23-Feb-16	05-May-16		22-Mar-16	01-Jun-16	
ACTBT1120	ACT Ceilings: Bed Tower Level 8	40	40	0	0%	-22	25-Feb-16	26-May-16		21-Apr-16	21-Jul-16	
ACTBT1110	ACT Ceilings: Bed Tower Level 9	40	40	0	0%	-27	22-Mar-16	02-Jun-16		17-May-16	27-Jul-16	

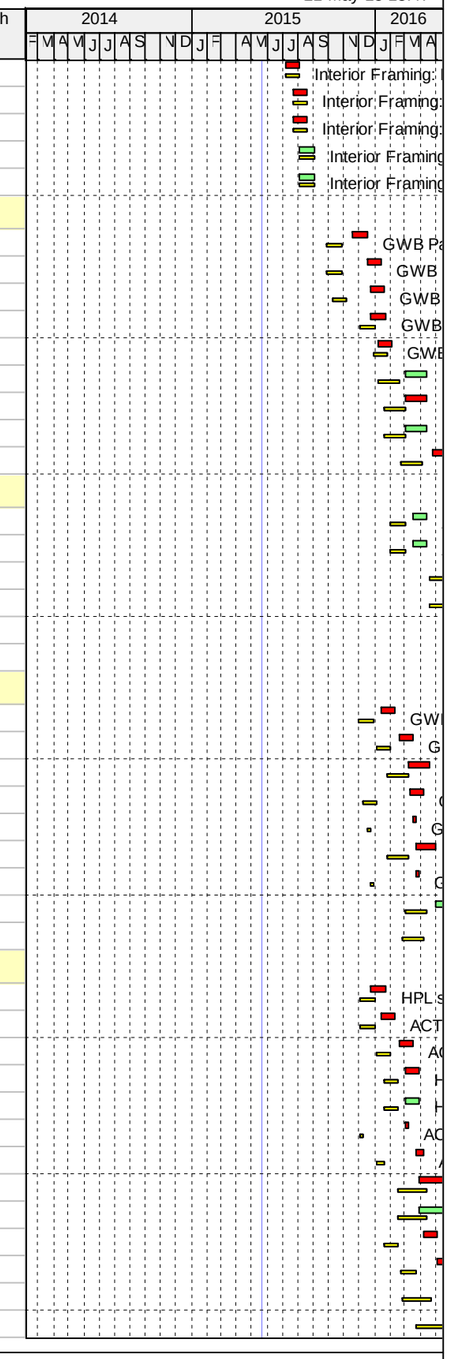

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
Finish Carpentry: Casework, Paneling & Trims												
FCBT1000	Install Column enclosures Bed Tower	75	75	0	0%	-51	25-Jan-16	19-Apr-16		06-May-16	01-Aug-16	
FCBT1010	Finish Carpentry: Bed Tower Level 3	20	20	0	0%	-8	04-Feb-16	05-May-16		02-Mar-16	01-Jun-16	
FCBT1020	Finish Carpentry: Bed Tower Level 4	20	20	0	0%	-8	15-Mar-16	05-May-16		12-Apr-16	01-Jun-16	
FCBT1030	Finish Carpentry: Bed Tower Level 5	20	20	0	0%	-8	15-Mar-16	05-May-16		12-Apr-16	01-Jun-16	
FCBT1040	Finish Carpentry: Bed Tower Level 6	20	20	0	0%	36	20-Apr-16	01-Jun-16		18-May-16	29-Jun-16	
FCBT1050	Finish Carpentry: Bed Tower Level 7	20	20	0	0%	27	20-Apr-16	14-Jun-16		18-May-16	12-Jul-16	
FCBT1060	Finish Carpentry: Bed Tower Level 8	20	20	0	0%	-20	19-May-16	18-Aug-16		16-Jun-16	15-Sep-16	
FCBT1070	Finish Carpentry: Bed Tower Level 9	20	20	0	0%	-20	16-Jun-16	15-Sep-16		14-Jul-16	13-Oct-16	
Painting												
PNTBT1040	Painting: Bed Tower Level 5	30	30	0	0%	-50	01-Jan-16	11-Feb-16		12-Feb-16	24-Mar-16	
PNTBT1030	Painting: Bed Tower Level 4	30	30	0	0%	-33	02-Feb-16	17-Mar-16		15-Mar-16	27-Apr-16	
PNTBT1000	Painting: Bed Tower Level 1	10	10	0	0%	-33	23-Dec-15	23-Mar-16		06-Jan-16	06-Apr-16	
PNTBT1010	Painting: Bed Tower Level 2	10	10	0	0%	-35	30-Dec-15	30-Mar-16		13-Jan-16	13-Apr-16	
PNTBT1020	Painting: Bed Tower Level 3	20	20	0	0%	-38	07-Jan-16	07-Apr-16		03-Feb-16	04-May-16	
PNTBT1050	Painting: Bed Tower Level 6	30	30	0	0%	-20	09-Mar-16	20-Apr-16		20-Apr-16	01-Jun-16	
PNTBT1060	Painting: Bed Tower Level 7	30	30	0	0%	-8	09-Mar-16	03-May-16		20-Apr-16	14-Jun-16	
PNTBT1070	Painting: Bed Tower Level 9	30	30	0	0%	17	12-Apr-16	14-Jun-16		24-May-16	26-Jul-16	
PNTBT1080	Painting: Bed Tower Level 8	30	30	0	0%	-40	07-Apr-16	07-Jul-16		19-May-16	18-Aug-16	
GFRC												
CON220	GFRC installations	60	60	0	0%	12	01-Jan-16	11-Feb-16		25-Mar-16	05-May-16	
Wall Coverings												
CON10380	Wall coverings: Bed Tower Level 6	30	30	0	0%	18	20-Apr-16	01-Jun-16		01-Jun-16	13-Jul-16	
CON10390	Wall coverings: Bed Tower Level 7	30	30	0	0%	18	03-May-16	14-Jun-16		14-Jun-16	26-Jul-16	
CON10400	Wall coverings: Bed Tower Level 8	30	30	0	0%	10	17-May-16	07-Jul-16		27-Jun-16	18-Aug-16	
CON10410	Wall coverings: Bed Tower Level 9	30	30	0	0%	10	30-May-16	20-Jul-16		11-Jul-16	31-Aug-16	
Interior Glazing												
IGUBT1000	IGUs: Bed Tower Level 4	30	30	0	0%	47	26-Jan-16	04-Feb-16		08-Mar-16	17-Mar-16	
IGUBT1010	IGUs: Bed Tower Level 5	30	30	0	0%	47	26-Jan-16	04-Feb-16		08-Mar-16	17-Mar-16	
IGUBT1020	IGUs: Bed Tower Level 6	30	30	0	0%	41	02-Mar-16	13-Apr-16		13-Apr-16	25-May-16	
IGUBT1030	IGUs: Bed Tower Level 7	30	30	0	0%	41	02-Mar-16	13-Apr-16		13-Apr-16	25-May-16	
IGUBT1040	IGUs: Bed Tower Level 8	30	30	0	0%	51	15-Mar-16	26-Apr-16		26-Apr-16	07-Jun-16	
IGUBT1050	IGUs: Bed Tower Level 9	30	30	0	0%	22	05-Apr-16	07-Jun-16		17-May-16	19-Jul-16	
Carpet												
CARPBT10(	Carpeting: Bed Tower Level 4	20	20	0	0%	-5	15-Mar-16	02-May-16		12-Apr-16	27-May-16	
CARPBT10:	Carpeting: Bed Tower Level 5	20	20	0	0%	-5	15-Mar-16	02-May-16		12-Apr-16	27-May-16	
CARPBT10:	Carpeting: Bed Tower Level 6	20	20	0	0%	36	20-Apr-16	01-Jun-16		18-May-16	29-Jun-16	
CARPBT10:	Carpeting: Bed Tower Level 7	20	20	0	0%	27	20-Apr-16	14-Jun-16		18-May-16	12-Jul-16	
CARPBT10-	Carpeting: Bed Tower Level 8	20	20	0	0%	0	19-May-16	18-Aug-16		16-Jun-16	15-Sep-16	
CARPBT10!	Carpeting: Bed Tower Level 9	20	20	0	0%	0	24-May-16	18-Aug-16		21-Jun-16	15-Sep-16	
Resilient Flooring & Carpeting												
RFBT1020	Resilient flooring Bed Tower Level 1	5	5	0	0%	-8	25-Jan-16	06-Apr-16		29-Jan-16	13-Apr-16	
RFBT1010	Resilient flooring: Bed Tower Level 2	10	10	0	0%	-13	25-Jan-16	13-Apr-16		05-Feb-16	27-Apr-16	
RFBT1000	Resilient flooring: Bed Tower Level 3	20	20	0	0%	-18	08-Feb-16	05-May-16		04-Mar-16	01-Jun-16	
RFBT1030	Resilient flooring Bed Tower Level 4	20	20	0	0%	-18	15-Mar-16	05-May-16		12-Apr-16	01-Jun-16	

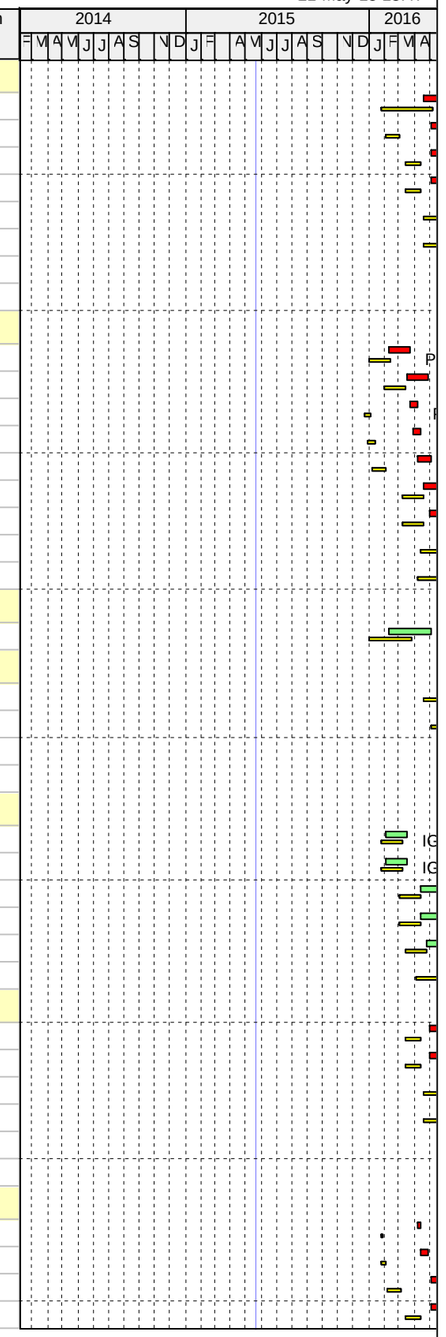

Remaining Level of Effort
Actual Level of Effort
Project Baseline Bar
Primary Baseline
Actual Work
Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
RFBT1040	Resilient flooring Bed Tower Level 5	20	20	0	0%	-18	29-Mar-16	19-May-16		26-Apr-16	15-Jun-16	
RFBT1050	FR Expansion Joint Bed Tower Level 5	10	10	0	0%	27	29-Mar-16	19-May-16		12-Apr-16	01-Jun-16	
RFBT1060	Resilient flooring Bed Tower Level 6	20	20	0	0%	27	20-Apr-16	02-Jun-16		18-May-16	29-Jun-16	
RFBT1070	FR Expansion Joint Bed Tower Level 6	10	10	0	0%	27	20-Apr-16	02-Jun-16		04-May-16	15-Jun-16	
RFBT1080	Resilient flooring: Bed Tower Level 7	20	20	0	0%	27	04-May-16	16-Jun-16		01-Jun-16	13-Jul-16	
RFBT1090	Resilient flooring: Bed Tower Level 8	20	20	0	0%	-9	19-May-16	18-Aug-16		16-Jun-16	15-Sep-16	
RFBT1100	Resilient flooring: Bed Tower Level 9	20	20	0	0%	-9	01-Jun-16	31-Aug-16		29-Jun-16	28-Sep-16	
Ceramic Tile												
TLBT1000	Ceramic Tile: Bed Tower Level 4	20	20	0	0%	-23	02-Feb-16	17-Mar-16		01-Mar-16	13-Apr-16	
TLBT1010	Ceramic Tile: Bed Tower Level 5	20	20	0	0%	-23	02-Feb-16	17-Mar-16		01-Mar-16	13-Apr-16	
TLBT1020	Ceramic Tile: Bed Tower Level 6	20	20	0	0%	-10	09-Mar-16	20-Apr-16		06-Apr-16	18-May-16	
TLBT1030	Ceramic Tile: Bed Tower Level 7	20	20	0	0%	21	09-Mar-16	03-May-16		06-Apr-16	31-May-16	
TLBT1040	Ceramic Tile: Bed Tower Level 8	20	20	0	0%	20	07-Apr-16	07-Jul-16		05-May-16	04-Aug-16	
TLBT1050	Ceramic Tile: Bed Tower Level 9	20	20	0	0%	20	12-Apr-16	07-Jul-16		10-May-16	04-Aug-16	
Epoxy Flooring												
CON4790	Epoxy flooring Bed Tower Level 6	20	20	0	0%	28	20-Apr-16	01-Jun-16		18-May-16	29-Jun-16	
CON4800	Epoxy flooring: Bed Tower Level 7	20	20	0	0%	28	03-May-16	14-Jun-16		31-May-16	12-Jul-16	
CON4810	Epoxy flooring: Bed Tower Level 8	20	20	0	0%	-10	19-May-16	18-Aug-16		16-Jun-16	15-Sep-16	
CON4820	Epoxy flooring: Bed Tower Level 9	20	20	0	0%	-10	01-Jun-16	31-Aug-16		29-Jun-16	28-Sep-16	
Specialties/Accessories												
ACCBT1010	Install Div. 10 accessories: Bed Tower Level 1	2	2	0	0%	0	06-Jan-16	06-Apr-16		08-Jan-16	08-Apr-16	
ACCBT1020	Install Div. 10 accessories: Bed Tower Level 2	2	2	0	0%	-3	13-Jan-16	13-Apr-16		15-Jan-16	15-Apr-16	
ACCBT1100	Install patient room head-walls Bed Tower Level 7	20	20	0	0%	37	09-Mar-16	03-May-16		06-Apr-16	31-May-16	
ACCBT1000	Install Div. 10 accessories: Bed Tower Level 3	2	2	0	0%	-17	04-Feb-16	05-May-16		05-Feb-16	06-May-16	
ACCBT1030	Install Div. 10 accessories: Bed Tower Level 4	10	10	0	0%	-17	15-Mar-16	18-May-16		29-Mar-16	01-Jun-16	
ACCBT1040	Install Div. 10 accessories: Bed Tower Level 5	10	10	0	0%	-17	28-Mar-16	31-May-16		11-Apr-16	14-Jun-16	
ACCBT1060	Install Div. 10 accessories: Bed Tower Level 6	10	10	0	0%	46	20-Apr-16	01-Jun-16		04-May-16	15-Jun-16	
ACCBT1050	Install High Density Shelving: Bed Tower Level 5	20	20	0	0%	-32	12-Feb-16	08-Jun-16		11-Mar-16	05-Jul-16	
ACCBT1130	Install Bio-safety Cabinets Bed Tower Level 7	5	5	0	0%	47	20-Apr-16	14-Jun-16		27-Apr-16	21-Jun-16	
ACCBT1070	Install Div. 10 accessories: Bed Tower Level 7	10	10	0	0%	46	04-May-16	15-Jun-16		18-May-16	29-Jun-16	
ACCBT1160	Install Bio-safety Cabinets Bed Tower Level 3	5	5	0	0%	47	27-Apr-16	21-Jun-16		04-May-16	28-Jun-16	
ACCBT1110	Install patient room head-walls Bed Tower Level 8	20	20	0	0%	10	07-Apr-16	07-Jul-16		05-May-16	04-Aug-16	
ACCBT1120	Install patient room head-walls Bed Tower Level 9	20	20	0	0%	10	05-May-16	04-Aug-16		02-Jun-16	01-Sep-16	
ACCBT1080	Install Div. 10 accessories: Bed Tower Level 8	10	10	0	0%	10	19-May-16	18-Aug-16		02-Jun-16	01-Sep-16	
ACCBT1090	Install Div. 10 accessories: Bed Tower Level 9	10	10	0	0%	10	24-May-16	18-Aug-16		07-Jun-16	01-Sep-16	
ACCBT1140	Install Bio-safety Cabinets Bed Tower Level 8	5	5	0	0%	10	19-May-16	18-Aug-16		26-May-16	25-Aug-16	
ACCBT1150	Install Bio-safety Cabinets Bed Tower Level 9	5	5	0	0%	10	26-May-16	25-Aug-16		02-Jun-16	01-Sep-16	
Wall Protections												
WPBT1010	Wall Protection: Corner Guards & Crash Rail Bed Tower Level 2	10	10	0	0%	-28	17-Feb-16	18-May-16		02-Mar-16	01-Jun-16	
WPBT1000	Wall Protection: Corner Guards & Crash Rail Bed Tower Level 1	10	10	0	0%	-28	17-Feb-16	18-May-16		02-Mar-16	01-Jun-16	
WPBT1020	Wall Protection: Corner Guards & Crash Rail Bed Tower Level 3	10	10	0	0%	-28	02-Mar-16	01-Jun-16		16-Mar-16	15-Jun-16	
WPBT1030	Wall Protection: Corner Guards & Crash Rail Bed Tower Level 4	10	10	0	0%	-28	15-Mar-16	01-Jun-16		29-Mar-16	15-Jun-16	
WPBT1040	Wall Protection: Corner Guards & Crash Rail Bed Tower Level 5	10	10	0	0%	-28	29-Mar-16	15-Jun-16		12-Apr-16	29-Jun-16	
WPBT1050	Wall Protection: Corner Guards & Crash Rail Bed Tower Level 6	10	10	0	0%	36	01-Jun-16	13-Jul-16		15-Jun-16	27-Jul-16	
WPBT1060	Wall Protection: Corner Guards & Crash Rail Bed Tower Level 7	10	10	0	0%	36	01-Jun-16	13-Jul-16		15-Jun-16	27-Jul-16	
WPBT1070	Wall Protection: Corner Guards & Crash Rail Bed Tower Level 8	10	10	0	0%	10	01-Jun-16	18-Aug-16		15-Jun-16	01-Sep-16	

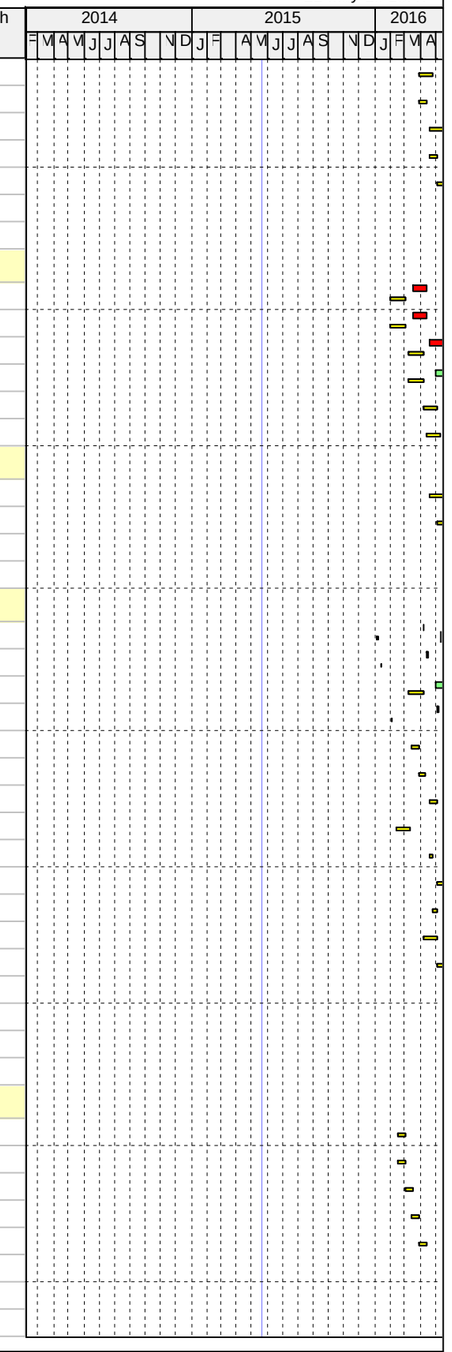

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
WPBT1080	Wall Protection: Corner Guards & Crash Rail Bed Tower Level 9	10	10	0	0%	-6	22-Jun-16	09-Sep-16		06-Jul-16	23-Sep-16	
Laboratory Equipment												
EQUIPBTC(	Freezer Farm Bed Tower Level 3	40	40	0	0%	20	07-Jan-16	07-Jan-16		03-Mar-16	03-Mar-16	
Medical Equipment: MRI3T												
EQTIEM1240	Layout MRI3T	10	10	0	0%	-21	08-Jul-15	08-Jul-15		22-Jul-15	22-Jul-15	
EQTIEM1250	Partition framing: MRI3T	20	20	0	0%	-21	22-Jul-15	22-Jul-15		19-Aug-15	19-Aug-15	
EQTIEM1260	HVAC Rough: MRI3T	25	25	0	0%	-21	19-Aug-15	19-Aug-15		23-Sep-15	23-Sep-15	
EQTIEM1270	Plumbing Rough: MRI3T	20	20	0	0%	-21	02-Sep-15	02-Sep-15		30-Sep-15	30-Sep-15	
EQTIEM1280	Electric Rough: MRI3T	20	20	0	0%	-21	16-Sep-15	16-Sep-15		14-Oct-15	14-Oct-15	
CON7590	MRI3T shielding installation	20	20	0	0%	-21	14-Oct-15	14-Oct-15		11-Nov-15	11-Nov-15	
EQTIEM1290	GWB: MRI3T	10	10	0	0%	-21	11-Nov-15	11-Nov-15		25-Nov-15	25-Nov-15	
EQTIEM1310	Finishes:MRI3T	20	20	0	0%	-21	11-Nov-15	11-Nov-15		09-Dec-15	09-Dec-15	
EQTIEM1300	ACT Celings MRI3T	10	10	0	0%	-21	25-Nov-15	25-Nov-15		09-Dec-15	09-Dec-15	
EQTIEM1460	Vendor pre-inspection	2	2	0	0%	-21	09-Dec-15	09-Dec-15		11-Dec-15	11-Dec-15	
EQTIEM1010	MRI 3T tie-ins	60	60	0	0%	-21	11-Dec-15	11-Dec-15		22-Jan-16	04-Mar-16	
EQTIEM1320	MEP Finishes MRI3T	10	10	0	0%	-21	22-Jan-16	04-Mar-16		05-Feb-16	18-Mar-16	
Medical Equipment: MRI 1.5T												
EQTIEM1330	Layout MRI1.5T	10	10	0	0%	-26	08-Jul-15	08-Jul-15		22-Jul-15	22-Jul-15	
EQTIEM1340	Partition framing: MRI1.5T	20	20	0	0%	-26	08-Jul-15	08-Jul-15		05-Aug-15	05-Aug-15	
EQTIEM1350	HVAC Rough: MRI1.5T	25	25	0	0%	-26	05-Aug-15	05-Aug-15		09-Sep-15	09-Sep-15	
EQTIEM1360	Plumbing Rough: MRI1.5T	25	25	0	0%	-26	19-Aug-15	19-Aug-15		23-Sep-15	23-Sep-15	
EQTIEM1370	Electric Rough: MRI1.5T	25	25	0	0%	-26	02-Sep-15	02-Sep-15		07-Oct-15	07-Oct-15	
CON11650	MRI 1.5T shielding installation	20	20	0	0%	-26	07-Oct-15	07-Oct-15		04-Nov-15	04-Nov-15	
EQTIEM1380	GWB: MRI1.5T	10	10	0	0%	-26	21-Oct-15	21-Oct-15		04-Nov-15	04-Nov-15	
EQTIEM1390	ACT Celings MRI1.5T	10	10	0	0%	-26	04-Nov-15	04-Nov-15		18-Nov-15	18-Nov-15	
EQTIEM1400	Finishes: MRI1.5T	20	20	0	0%	-26	18-Nov-15	18-Nov-15		16-Dec-15	16-Dec-15	
EQTIEM1470	Vendor pre-inspection	2	2	0	0%	-26	16-Dec-15	16-Dec-15		18-Dec-15	18-Dec-15	
EQTIEM1020	MEP MRI 1.5T tie-ins	60	60	0	0%	-26	18-Dec-15	18-Dec-15		29-Jan-16	11-Mar-16	
EQTIEM1410	MEP Finishes MRI1.5T	10	10	0	0%	-26	29-Jan-16	11-Mar-16		12-Feb-16	25-Mar-16	
Furnishings												
FCBT1080	Install headwalls Bed Tower Level 6	40	40	0	0%	-29	02-Mar-16	25-May-16		27-Apr-16	20-Jul-16	
FCBT1090	Install headwalls Bed Tower Level 7	40	40	0	0%	-19	13-Apr-16	22-Jun-16		08-Jun-16	17-Aug-16	
EQUIPBTC(	Patient Lift Bed Tower 6	30	30	0	0%	-29	27-Apr-16	22-Jun-16		08-Jun-16	03-Aug-16	
FCBT1100	Install headwalls Bed Tower Level 8	40	40	0	0%	-19	11-May-16	20-Jul-16		06-Jul-16	14-Sep-16	
EQUIPBTC(	Patient Lift Bed Tower 7	30	30	0	0%	-29	08-Jun-16	03-Aug-16		20-Jul-16	14-Sep-16	
FCBT1110	Install headwalls Bed Tower Level 9	40	40	0	0%	-19	17-May-16	17-Aug-16		12-Jul-16	12-Oct-16	
EQUIPBTC(	Patient Lift Bed Tower 8	20	20	0	0%	-29	20-Jul-16	14-Sep-16		17-Aug-16	12-Oct-16	
EQUIPBTC(	Patient Lift Bed Tower 9	20	20	0	0%	-29	03-Aug-16	28-Sep-16		31-Aug-16	26-Oct-16	
Manufactured Casework												
CASEBT101	Install Manufactured Casework: Bed Tower Level 1	30	30	0	0%	-13	25-Jan-16	06-Apr-16		04-Mar-16	18-May-16	
CASEBT103	Install Manufactured Casework: Bed Tower Level 2	30	30	0	0%	-18	25-Jan-16	13-Apr-16		04-Mar-16	25-May-16	
CASEBT104	Install Manufactured Casework: Bed Tower Level 3	30	30	0	0%	-18	15-Feb-16	05-May-16		25-Mar-16	15-Jun-16	
CASEBT100	Install Manufactured Casework: Bed Tower Level 4	30	30	0	0%	-18	15-Mar-16	05-May-16		26-Apr-16	15-Jun-16	
CASEBT102	Install Manufactured Casework: Bed Tower Level 5	30	30	0	0%	-18	15-Mar-16	05-May-16		26-Apr-16	15-Jun-16	
CASEBT105	Install Manufactured Casework: Bed Tower Level 6	30	30	0	0%	-14	20-Apr-16	01-Jun-16		01-Jun-16	13-Jul-16	
CASEBT106	Install Manufactured Casework: Bed Tower Level 7	30	30	0	0%	-14	11-May-16	22-Jun-16		22-Jun-16	03-Aug-16	

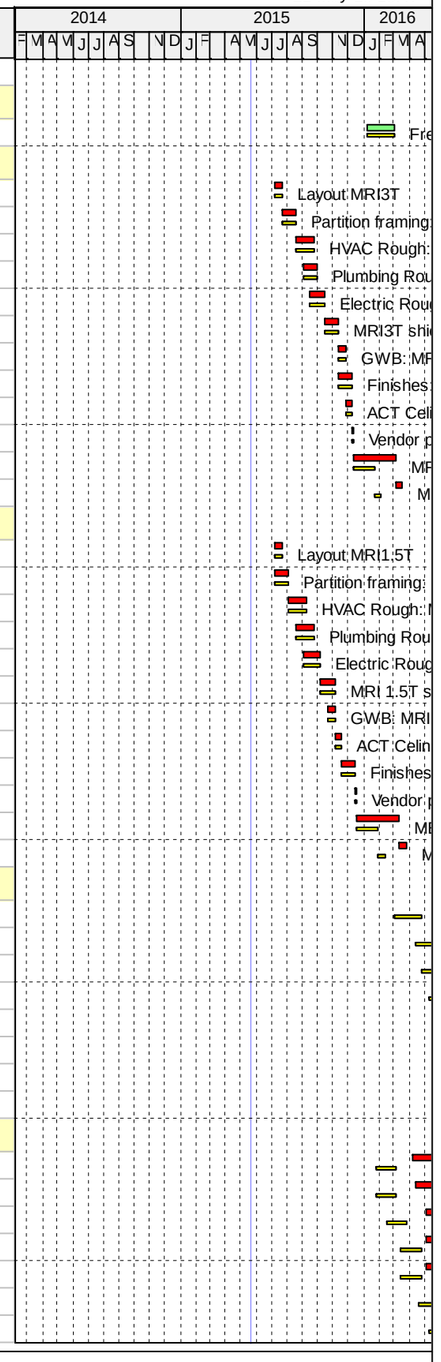

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
CASEBT107	Install Manufactured Casework: Bed Tower Level 8	30	30	0	0%	-25	01-Jun-16	18-Aug-16		14-Jul-16	30-Sep-16	
CASEBT108	Install Manufactured Casework: Bed Tower Level 9	30	30	0	0%	-26	22-Jun-16	09-Sep-16		03-Aug-16	21-Oct-16	
Radiation Protection												
CON120	Radiation protection installation	30	30	0	0%	-23	17-Nov-15	24-Dec-15		29-Dec-15	04-Feb-16	
Wet Standpipe System Piping												
FSBT1020	Fire suppression branch work and heads Level 3	42	42	0	0%	-13	30-Jul-15	03-Sep-15		28-Sep-15	02-Nov-15	
FSBT1030	Fire suppression branch work and heads Level 4	53	53	0	0%	-54	15-Oct-15	17-Sep-15		29-Dec-15	01-Dec-15	
FSBT1040	Fire suppression branch work and heads Level 5	56	56	0	0%	-72	17-Sep-15	08-Oct-15		04-Dec-15	25-Dec-15	
FSBT1010	Fire suppression branch work and heads Level 2	9	9	0	0%	-19	20-Aug-15	05-Nov-15		02-Sep-15	18-Nov-15	
FSBT1000	Fire suppression branch work and heads Level 1	26	26	0	0%	-50	06-Aug-15	12-Nov-15		11-Sep-15	18-Dec-15	
FSBT1080	Fire pumps installation Bed Tower Level 3	30	30	0	0%	29	23-Oct-15	13-Nov-15		04-Dec-15	25-Dec-15	
FSBT1060	Fire suppression branch work and heads Level 6	59	59	0	0%	-57	29-Oct-15	10-Dec-15		20-Jan-16	02-Mar-16	
FSBT1050	Fire suppression branch work and heads Level 10	36	36	0	0%	-7	05-Nov-15	25-Dec-15		25-Dec-15	15-Feb-16	
FSBT1070	Fire suppression branch work and heads Level 7	44	44	0	0%	-57	19-Nov-15	31-Dec-15		20-Jan-16	02-Mar-16	
FSBT1090	Fire suppression branch work and heads Level 8	20	20	0	0%	-4	19-Nov-15	21-Jan-16		17-Dec-15	18-Feb-16	
FSBT1110	Fire suppression branch work and heads Level 9	53	53	0	0%	-48	10-Dec-15	11-Feb-16		23-Feb-16	26-Apr-16	
FSBT1100	Fire Suppression System Pressure Test: Bed Tower (MS2)	10	10	0	0%	-7	25-Dec-15	15-Feb-16		08-Jan-16	29-Feb-16	
FSBT1120	Fire Suppression System Pressure Test: Bed Tower (MS2A)	10	10	0	0%	-28	23-Feb-16	26-Apr-16		08-Mar-16	10-May-16	
Clean-Agent Fire Suppression												
FSCBT1150	Clean-agent Fire suppression branch work and heads Level 3	60	60	0	0%	-20	19-Nov-15	24-Dec-15		11-Feb-16	17-Mar-16	
Sanitary & Vent												
PBT1040	Sanitary, storm, and vent Level 4	28	28	0	0%	-16	20-Aug-15	13-Aug-15		29-Sep-15	22-Sep-15	
PBT1070	Sanitary, storm, and vent Level 5	30	30	0	0%	-31	20-Aug-15	03-Sep-15		01-Oct-15	15-Oct-15	
PBT1160	Sanitary, storm, and vent Level 6	45	45	0	0%	-5	24-Sep-15	05-Nov-15		26-Nov-15	07-Jan-16	
PBT1000	Sanitary, and vent Level 1	5	5	0	0%	-66	06-Aug-15	12-Nov-15		13-Aug-15	19-Nov-15	
PBT1010	Sanitary, and vent Level 2	20	20	0	0%	-71	03-Sep-15	19-Nov-15		01-Oct-15	17-Dec-15	
PBT1020	Sanitary, and vent Level 3	25	25	0	0%	-71	03-Sep-15	19-Nov-15		08-Oct-15	24-Dec-15	
PBT1200	Sanitary, storm, and vent Level 7	28	28	0	0%	10	15-Oct-15	26-Nov-15		24-Nov-15	05-Jan-16	
PBT1230	Sanitary, storm, and vent Level 8	42	42	0	0%	7	15-Oct-15	17-Dec-15		14-Dec-15	15-Feb-16	
PBT1280	Sanitary, storm and vent Level 9	38	38	0	0%	-27	05-Nov-15	07-Jan-16		29-Dec-15	01-Mar-16	
Domestic Piping												
PBT1100	HW/CW distribution Level 5	25	25	0	0%	-31	10-Sep-15	24-Sep-15		15-Oct-15	29-Oct-15	
PBT1050	HW/CW distribution Level 3	8	8	0	0%	-71	24-Aug-15	09-Nov-15		03-Sep-15	19-Nov-15	
PBT1060	HW/CWdistribution Level 4	25	25	0	0%	-71	03-Sep-15	19-Nov-15		08-Oct-15	24-Dec-15	
PBT1190	HW/CW distribution Level 6	30	30	0	0%	-5	15-Oct-15	26-Nov-15		26-Nov-15	07-Jan-16	
PBT1220	HW/CW distribution Level 7	18	18	0	0%	10	15-Oct-15	26-Nov-15		10-Nov-15	22-Dec-15	
PBT1030	HW/CW distribution Level 2	5	5	0	0%	-56	01-Oct-15	17-Dec-15		08-Oct-15	24-Dec-15	
PBT1270	HW/CW distribution Level 8	38	38	0	0%	7	10-Nov-15	07-Jan-16		01-Jan-16	01-Mar-16	
PBT1300	HW/CW distribution Level 9	33	33	0	0%	-27	26-Nov-15	28-Jan-16		12-Jan-16	15-Mar-16	
Compressed Air & Vacuum, Medical Gas Distribution												
PBT1120	Compressed air/vacuum/medical gas pipe and fittings 4	31	31	0	0%	-29	24-Sep-15	24-Dec-15		06-Nov-15	05-Feb-16	
PBT1180	Compressed air/vacuum/medical gas pipe and fittings 5	5	5	0	0%	-50	01-Oct-15	07-Jan-16		08-Oct-15	14-Jan-16	
PBT1170	Compressed air/vacuum/medical gas pipe and fittings 3	22	22	0	0%	-29	15-Oct-15	14-Jan-16		16-Nov-15	15-Feb-16	
PBT1240	Compressed air/vacuum/medical gas pipe and fittings 6	30	30	0	0%	-40	05-Nov-15	04-Feb-16		17-Dec-15	17-Mar-16	
PBT1330	Compressed air/vacuum/medical gas pipe and fittings 9	33	33	0	0%	-27	17-Dec-15	18-Feb-16		02-Feb-16	05-Apr-16	
PBT1290	Compressed air/vacuum/medical gas pipe and fittings 7	18	18	0	0%	-40	26-Nov-15	25-Feb-16		22-Dec-15	22-Mar-16	

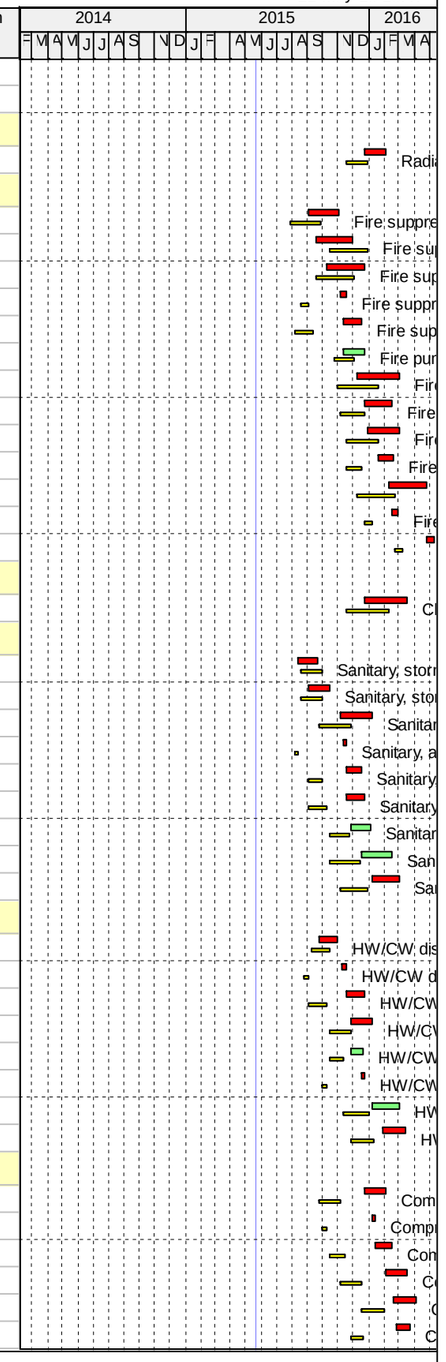

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
PBT1310	Compressed air/vacuum/medical gas pipe and fittings 8	38	38	0	0%	-40	04-Jan-16	04-Apr-16		25-Feb-16	26-May-16	
Natural Gas Piping												
PBT1080	Gas distribution Level 3	8	8	0	0%	59	28-Aug-15	02-Oct-15		09-Sep-15	14-Oct-15	
PBT1090	Gas distribution Level 4	5	5	0	0%	45	23-Nov-15	26-Oct-15		30-Nov-15	02-Nov-15	
PBT1150	Gas distribution Level 5	5	5	0	0%	-13	27-Oct-15	17-Nov-15		03-Nov-15	24-Nov-15	
PBT1210	Gas distribution Level 6	5	5	0	0%	10	09-Dec-15	20-Jan-16		16-Dec-15	27-Jan-16	
PBT1250	Gas distribution Level 7	5	5	0	0%	23	21-Dec-15	01-Feb-16		28-Dec-15	08-Feb-16	
PBT1260	Gas distribution Level 8	5	5	0	0%	33	28-Dec-15	08-Feb-16		04-Jan-16	15-Feb-16	
PBT1320	Gas distribution Level 9	5	5	0	0%	38	04-Jan-16	25-Feb-16		11-Jan-16	03-Mar-16	
Laboratory Gas Alarms												
CON9100	Laboratory gas alarms 5	20	20	0	0%	-27	01-Jan-16	11-Feb-16		29-Jan-16	10-Mar-16	
CON9090	Laboratory gas alarms 4	20	20	0	0%	-32	05-Jan-16	18-Feb-16		02-Feb-16	16-Mar-16	
CON9080	Laboratory gas alarms 3	20	20	0	0%	-47	10-Dec-15	10-Mar-16		06-Jan-16	06-Apr-16	
CON9110	Laboratory gas alarms 6	20	20	0	0%	19	16-Mar-16	27-Apr-16		13-Apr-16	25-May-16	
CON9120	Laboratory gas alarms 7	20	20	0	0%	19	16-Mar-16	27-Apr-16		13-Apr-16	25-May-16	
CON9130	Laboratory gas alarms 8	20	20	0	0%	-22	24-Mar-16	23-Jun-16		21-Apr-16	21-Jul-16	
CON9140	Laboratory gas alarms 9	20	20	0	0%	-27	19-Apr-16	30-Jun-16		17-May-16	27-Jul-16	
Plumbing Fixtures												
PBT1360	Plumbing Fixtures 2	5	5	0	0%	-35	06-Jan-16	06-Apr-16		13-Jan-16	13-Apr-16	
PBT1340	Plumbing Fixtures 3	12	12	0	0%	-38	19-Jan-16	19-Apr-16		03-Feb-16	04-May-16	
PBT1350	Plumbing Fixtures 4	23	23	0	0%	-38	15-Mar-16	05-May-16		15-Apr-16	06-Jun-16	
PBT1370	Plumbing Fixtures 5	20	20	0	0%	-38	15-Mar-16	05-May-16		12-Apr-16	01-Jun-16	
PBT1380	Plumbing Fixtures 10	5	5	0	0%	-38	05-Apr-16	26-May-16		12-Apr-16	01-Jun-16	
PBT1390	Plumbing Fixtures 6	40	40	0	0%	-21	20-Apr-16	02-Jun-16		15-Jun-16	27-Jul-16	
PBT1400	Plumbing Fixtures 7	23	23	0	0%	-21	20-Apr-16	28-Jul-16		23-May-16	29-Aug-16	
PBT1410	Plumbing Fixtures 8	41	41	0	0%	-24	19-May-16	18-Aug-16		15-Jul-16	14-Oct-16	
PBT1420	Plumbing Fixtures 9	44	44	0	0%	-24	19-May-16	18-Aug-16		20-Jul-16	19-Oct-16	
Hydronic Piping												
MECHBT11	Level 4 HW/CHW/S/R/CD	20	20	0	0%	-31	15-Oct-15	17-Sep-15		12-Nov-15	15-Oct-15	
MECHBT12	Level 5 HW/CHW/S/R/CD	20	20	0	0%	0	17-Sep-15	08-Oct-15		15-Oct-15	05-Nov-15	
MECHBT12	Level 1 HW/CHW/S/R/CD	20	20	0	0%	-20	06-Aug-15	12-Nov-15		03-Sep-15	10-Dec-15	
MECHBT12	Level 2 HW/CHW/S/R/CD	20	20	0	0%	-25	03-Sep-15	19-Nov-15		01-Oct-15	17-Dec-15	
MECHBT11	Level 3 HW/CHW/S/R/CD	20	20	0	0%	-25	22-Oct-15	03-Dec-15		19-Nov-15	31-Dec-15	
MECHBT13	Level 6 HW/CHW/S/R/CD	20	20	0	0%	12	29-Oct-15	10-Dec-15		26-Nov-15	07-Jan-16	
MECHBT13	Level 7 HW/CHW/S/R/CD	20	20	0	0%	23	19-Nov-15	31-Dec-15		17-Dec-15	28-Jan-16	
MECHBT14	Level 8 HW/CHW/S/R/CD	20	20	0	0%	23	19-Nov-15	21-Jan-16		17-Dec-15	18-Feb-16	
MECHBT14	Level 9 HW/CHW/S/R/CD	20	20	0	0%	-15	10-Dec-15	11-Feb-16		07-Jan-16	10-Mar-16	
Hydronic Piping insulation												
MECHBT11	Level 4 HW/CHW/S/R/CD insulation	20	20	0	0%	-31	15-Oct-15	17-Sep-15		12-Nov-15	15-Oct-15	
MECHBT12	Level 5 HW/CHW/S/R/CD insulation	20	20	0	0%	0	17-Sep-15	08-Oct-15		15-Oct-15	05-Nov-15	
MECHBT11	Level 3 HW/CHW/S/R/CD insulation	20	20	0	0%	3	22-Oct-15	03-Dec-15		19-Nov-15	31-Dec-15	
MECHBT12	Level 1 HW/CHW/S/R/CD insulation	20	20	0	0%	17	03-Sep-15	10-Dec-15		01-Oct-15	07-Jan-16	
MECHBT13	Level 6 HW/CHW/S/R/CD insulation	20	20	0	0%	12	29-Oct-15	10-Dec-15		26-Nov-15	07-Jan-16	
MECHBT12	Level 2 HW/CHW/S/R/CD insulation	20	20	0	0%	15	03-Sep-15	17-Dec-15		01-Oct-15	14-Jan-16	
MECHBT13	Level 7 HW/CHW/S/R/CD insulation	20	20	0	0%	23	19-Nov-15	31-Dec-15		17-Dec-15	28-Jan-16	
MECHBT14	Level 8 HW/CHW/S/R/CD insulation	20	20	0	0%	23	19-Nov-15	21-Jan-16		17-Dec-15	18-Feb-16	

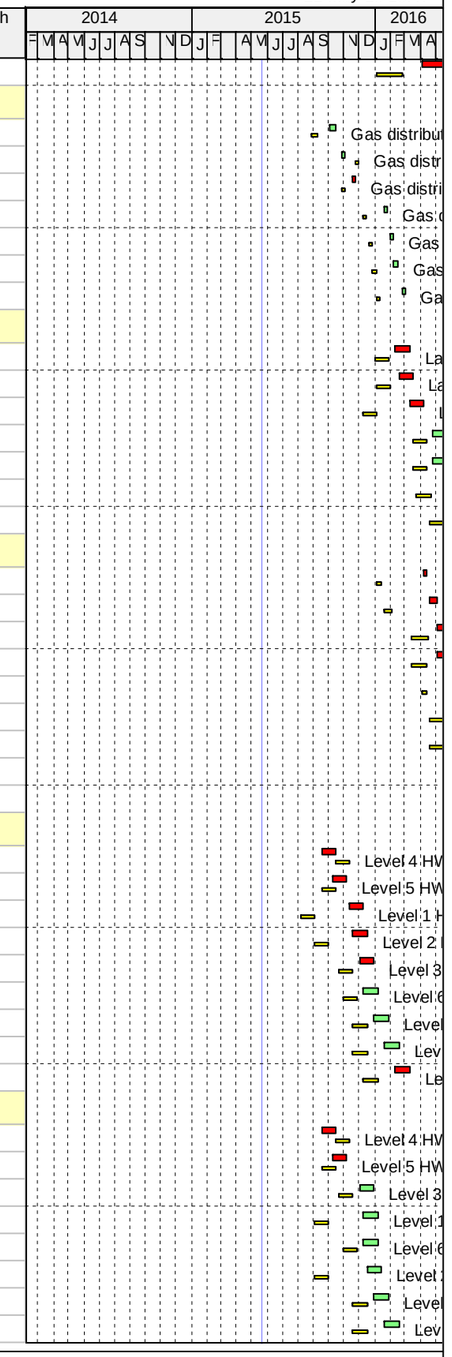

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
MECHBT14	Level 9 HW/CHW/S/R/CD insulation	20	20	0	0%	-15	10-Dec-15	11-Feb-16		07-Jan-16	10-Mar-16	
Steam & Condensate Piping												
STMBT1000	Level 1 Steam/Condensate piping	20	20	0	0%	-81	06-Aug-15	12-Nov-15		03-Sep-15	10-Dec-15	
STMBT1010	Level 2 Steam/Condensate piping	20	20	0	0%	-81	06-Aug-15	12-Nov-15		03-Sep-15	10-Dec-15	
STMBT1020	Level 3 Steam/Condensate piping	20	20	0	0%	-81	20-Aug-15	26-Nov-15		17-Sep-15	24-Dec-15	
STMBT1030	Level 4 Steam/Condensate piping	20	20	0	0%	-81	20-Aug-15	26-Nov-15		17-Sep-15	24-Dec-15	
STMBT1040	Level 5 Steam/Condensate piping	20	20	0	0%	-71	03-Sep-15	10-Dec-15		01-Oct-15	07-Jan-16	
STMBT1080	Level 8 Steam/Condensate piping	20	20	0	0%	-2	15-Oct-15	17-Dec-15		12-Nov-15	14-Jan-16	
STMBT1090	Level 9 Steam/Condensate piping	20	20	0	0%	-2	15-Oct-15	17-Dec-15		12-Nov-15	14-Jan-16	
STMBT1060	Level 6 Steam/Condensate piping	20	20	0	0%	-40	24-Sep-15	07-Jan-16		22-Oct-15	04-Feb-16	
STMBT1070	Level 7 Steam/Condensate piping	20	20	0	0%	-25	24-Sep-15	07-Jan-16		22-Oct-15	04-Feb-16	
HVAC Ductwork												
MECHBT10	Level 4 Ductwork	40	40	0	0%	-81	20-Aug-15	23-Jul-15		15-Oct-15	17-Sep-15	
MECHBT10	Level 5 Ductwork	40	40	0	0%	-81	23-Jul-15	13-Aug-15		17-Sep-15	08-Oct-15	
MECHBT10	Level 3 Ductwork	60	60	0	0%	-81	30-Jul-15	03-Sep-15		22-Oct-15	26-Nov-15	
MECHBT10	Level 2 Ductwork	40	40	0	0%	-81	09-Jul-15	24-Sep-15		03-Sep-15	19-Nov-15	
MECHBT10	Level 1 Ductwork	20	20	0	0%	-81	09-Jul-15	15-Oct-15		06-Aug-15	12-Nov-15	
MECHBT11	Level 6 Ductwork	40	40	0	0%	-57	03-Sep-15	15-Oct-15		29-Oct-15	10-Dec-15	
MECHBT12	Level 7 Ductwork	40	40	0	0%	-57	24-Sep-15	05-Nov-15		19-Nov-15	31-Dec-15	
MECHBT13	Level 8 Ductwork	40	40	0	0%	-48	24-Sep-15	26-Nov-15		19-Nov-15	21-Jan-16	
MECHBT13	Level 9 Ductwork	40	40	0	0%	-48	15-Oct-15	17-Dec-15		10-Dec-15	11-Feb-16	
MECHBT13	Air balancing: Bed Tower	209	209	0	0%	34	10-Dec-15	31-Dec-15		09-Sep-16	18-Oct-16	
Duct Insulation												
DINSBT1020	Level 4 Ductwork insulation	20	20	0	0%	-54	15-Oct-15	17-Sep-15		12-Nov-15	15-Oct-15	
DINSBT1040	Level 5 Ductwork insulation	20	20	0	0%	-72	17-Sep-15	08-Oct-15		15-Oct-15	05-Nov-15	
DINSBT1010	Level 2 Ductwork insulation	20	20	0	0%	-19	20-Aug-15	05-Nov-15		17-Sep-15	03-Dec-15	
DINSBT1000	Level 1 Ductwork insulation	20	20	0	0%	-50	06-Aug-15	12-Nov-15		03-Sep-15	10-Dec-15	
DINSBT1030	Level 3 Ductwork insulation	20	20	0	0%	-20	22-Oct-15	26-Nov-15		19-Nov-15	24-Dec-15	
DINSBT1060	Level 6 Ductwork insulation	20	20	0	0%	-57	29-Oct-15	10-Dec-15		26-Nov-15	07-Jan-16	
DINSBT1070	Level 7 Ductwork insulation	20	20	0	0%	-57	19-Nov-15	31-Dec-15		17-Dec-15	28-Jan-16	
DINSBT1080	Level 8 Ductwork insulation	20	20	0	0%	-4	19-Nov-15	21-Jan-16		17-Dec-15	18-Feb-16	
DINSBT1090	Level 9 Ductwork insulation	20	20	0	0%	-48	10-Dec-15	11-Feb-16		07-Jan-16	10-Mar-16	
HVAC Equipment												
MECHBT12	Chiller installation	60	60	0	0%	0	26-Nov-15	26-Nov-15		18-Feb-16	18-Feb-16	
MECHBT13	Level 10 HVAC Equipment	60	60	0	0%	-17	09-Dec-15	21-Dec-15		02-Mar-16	14-Mar-16	
MECHBT13	Level 3 HVAC Equipment	60	60	0	0%	-25	10-Dec-15	31-Dec-15		03-Mar-16	24-Mar-16	
HVAC DDC & Secondary Controls												
MECHBT11	HVAC control wiring 2	20	20	0	0%	-7	06-Aug-15	17-Aug-15		03-Sep-15	14-Sep-15	
MECHBT10	HVAC control wiring 3	40	40	0	0%	-17	20-Aug-15	31-Aug-15		15-Oct-15	26-Oct-15	
MECHBT10	HVAC control wiring 4	40	40	0	0%	20	03-Sep-15	03-Sep-15		29-Oct-15	29-Oct-15	
MECHBT11	HVAC control wiring 1	10	10	0	0%	-17	03-Sep-15	28-Sep-15		17-Sep-15	12-Oct-15	
MECHBT10	HVAC control wiring 10	40	40	0	0%	0	01-Oct-15	01-Oct-15		26-Nov-15	26-Nov-15	
MECHBT11	HVAC control wiring 6	40	40	0	0%	-7	30-Sep-15	12-Oct-15		25-Nov-15	07-Dec-15	
MECHBT10	HVAC control wiring 7	40	40	0	0%	-9	14-Oct-15	14-Oct-15		09-Dec-15	09-Dec-15	
MECHBT11	HVAC control wiring 5	40	40	0	0%	-17	17-Sep-15	26-Oct-15		12-Nov-15	21-Dec-15	
MECHBT12	HVAC control wiring 8	40	40	0	0%	13	28-Oct-15	28-Oct-15		23-Dec-15	23-Dec-15	

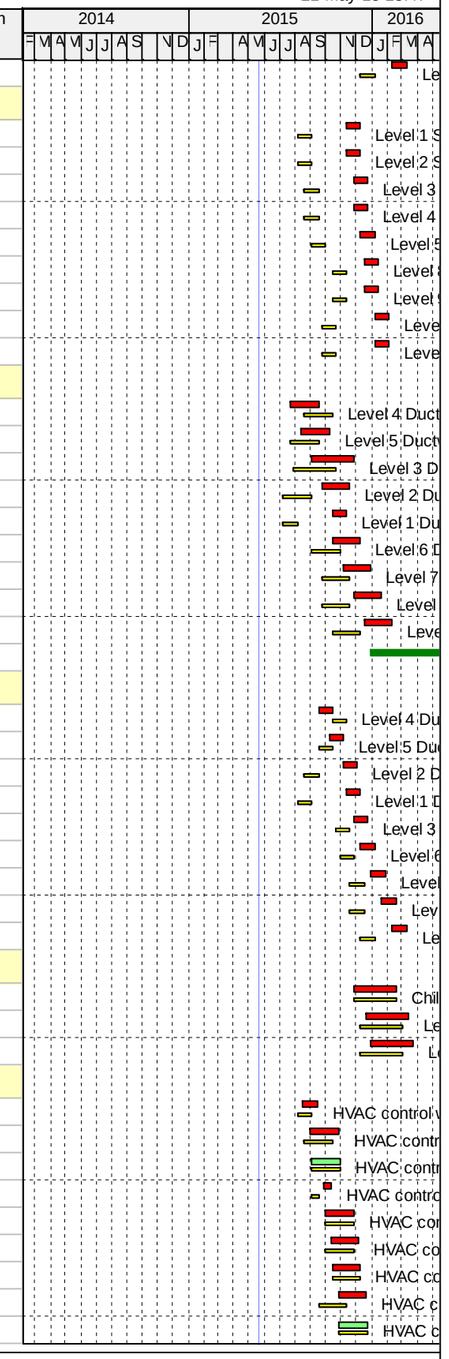

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
MECHBT10	HVAC control wiring 9	40	40	0	0%	13	28-Oct-15	28-Oct-15		23-Dec-15	23-Dec-15	
DDCCON8(	DDC System installation BT	100	100	0	0%	-18	07-Dec-15	17-Dec-15		14-Apr-16	05-May-16	
HVAC Grilles												
MECHBT14	Grilles, registers, & diffusers 1	10	10	0	0%	-27	25-Apr-16	01-Jun-16		06-May-16	14-Jun-16	
MECHBT14	Grilles, registers, & diffusers 5	20	20	0	0%	-27	25-Apr-16	01-Jun-16		20-May-16	28-Jun-16	
MECHBT14	Grilles, registers, & diffusers 2	10	10	0	0%	-27	25-Apr-16	01-Jun-16		06-May-16	14-Jun-16	
MECHBT14	Grilles, registers, & diffusers 3	40	40	0	0%	-27	25-Apr-16	01-Jun-16		17-Jun-16	26-Jul-16	
MECHBT14	Grilles, registers, & diffusers 4	20	20	0	0%	-27	25-Apr-16	01-Jun-16		20-May-16	28-Jun-16	
MECHBT14	Grilles, registers, & diffusers 10	20	20	0	0%	-27	25-Apr-16	01-Jun-16		20-May-16	28-Jun-16	
MECHBT15	Grilles, registers, & diffusers 6	20	20	0	0%	34	23-May-16	29-Jun-16		17-Jun-16	26-Jul-16	
MECHBT15	Grilles, registers, & diffusers 7	20	20	0	0%	34	20-Jun-16	27-Jul-16		15-Jul-16	23-Aug-16	
MECHBT15	Grilles, registers, & diffusers 8	20	20	0	0%	34	18-Jul-16	24-Aug-16		12-Aug-16	20-Sep-16	
MECHBT15	Grilles, registers, & diffusers 9	20	20	0	0%	34	15-Aug-16	21-Sep-16		09-Sep-16	18-Oct-16	
Conduits, Troughs, Boxes and Fittings												
ELECBT1260	Low voltage conduits 2	20	20	0	0%	-31	09-Jul-15	09-Jul-15		06-Aug-15	06-Aug-15	
ELECBT1290	Low voltage conduits 1	20	20	0	0%	-31	09-Jul-15	09-Jul-15		06-Aug-15	06-Aug-15	
ELECBT1050	Low voltage conduits 3	30	30	0	0%	-31	23-Jul-15	23-Jul-15		03-Sep-15	03-Sep-15	
ELECBT1090	Low voltage conduits 4	30	30	0	0%	-31	23-Jul-15	23-Jul-15		03-Sep-15	03-Sep-15	
ELECBT1100	Low voltage conduits 5	30	30	0	0%	-31	23-Jul-15	23-Jul-15		03-Sep-15	03-Sep-15	
ELECBT1110	Low voltage conduits 6	40	40	0	0%	1	05-Aug-15	05-Aug-15		30-Sep-15	30-Sep-15	
ELECBT1140	Low voltage conduits 7	40	40	0	0%	-9	19-Aug-15	19-Aug-15		14-Oct-15	14-Oct-15	
ELECBT1270	Low voltage conduits 8	40	40	0	0%	2	02-Sep-15	02-Sep-15		28-Oct-15	28-Oct-15	
ELECBT1280	Low voltage conduits 9	40	40	0	0%	2	02-Sep-15	02-Sep-15		28-Oct-15	28-Oct-15	
ELECBT1200	Low voltage conduits Roof	20	20	0	0%	19	16-Sep-15	16-Sep-15		14-Oct-15	14-Oct-15	
ELECBT1160	Low voltage conduits 10	20	20	0	0%	2	16-Sep-15	16-Sep-15		14-Oct-15	14-Oct-15	
Panelboards and Switchboards												
ELECBT1000	Branch panels 2	10	10	0	0%	-11	09-Jul-15	09-Jul-15		23-Jul-15	23-Jul-15	
ELECBT1080	Branch panels 3	20	20	0	0%	-16	09-Jul-15	09-Jul-15		06-Aug-15	06-Aug-15	
ELECBT1010	Branch panels 4	30	30	0	0%	-16	23-Jul-15	23-Jul-15		03-Sep-15	03-Sep-15	
ELECBT1020	Branch panels 5	20	20	0	0%	-16	23-Jul-15	23-Jul-15		20-Aug-15	20-Aug-15	
ELECBT1060	Branch panels 6	20	20	0	0%	1	05-Aug-15	05-Aug-15		02-Sep-15	02-Sep-15	
ELECBT1070	Branch panels 7	20	20	0	0%	6	19-Aug-15	19-Aug-15		16-Sep-15	16-Sep-15	
ELECBT1210	Branch panels 8	20	20	0	0%	16	19-Aug-15	19-Aug-15		16-Sep-15	16-Sep-15	
ELECBT1220	Branch panels 9	20	20	0	0%	21	02-Sep-15	02-Sep-15		30-Sep-15	30-Sep-15	
ELECBT1320	Switchgear installation	30	30	0	0%	-7	13-Oct-15	27-Oct-15		23-Nov-15	08-Dec-15	
Branch Wiring: Power & Lighting												
ELECBT1040	Branch wiring 1	10	10	0	0%	-11	23-Jul-15	23-Jul-15		06-Aug-15	06-Aug-15	
ELECBT1030	Branch wiring 2	10	10	0	0%	-11	06-Aug-15	06-Aug-15		20-Aug-15	20-Aug-15	
ELECBT1230	Branch wiring 3	20	20	0	0%	-11	06-Aug-15	06-Aug-15		03-Sep-15	03-Sep-15	
ELECBT1170	Branch wiring 4	30	30	0	0%	-11	06-Aug-15	06-Aug-15		17-Sep-15	17-Sep-15	
ELECBT1120	Branch wiring 5	30	30	0	0%	-16	13-Aug-15	13-Aug-15		24-Sep-15	24-Sep-15	
ELECBT1130	Branch wiring 10	20	20	0	0%	10	20-Aug-15	20-Aug-15		17-Sep-15	17-Sep-15	
ELECBT1150	Branch wiring 6	30	30	0	0%	1	26-Aug-15	26-Aug-15		07-Oct-15	07-Oct-15	
ELECBT1300	Branch wiring 7	30	30	0	0%	1	07-Oct-15	07-Oct-15		18-Nov-15	18-Nov-15	
ELECBT1310	Branch wiring 8	30	30	0	0%	1	07-Oct-15	07-Oct-15		18-Nov-15	18-Nov-15	
ELECBT1350	Branch wiring Roof	20	20	0	0%	1	28-Oct-15	28-Oct-15		25-Nov-15	25-Nov-15	

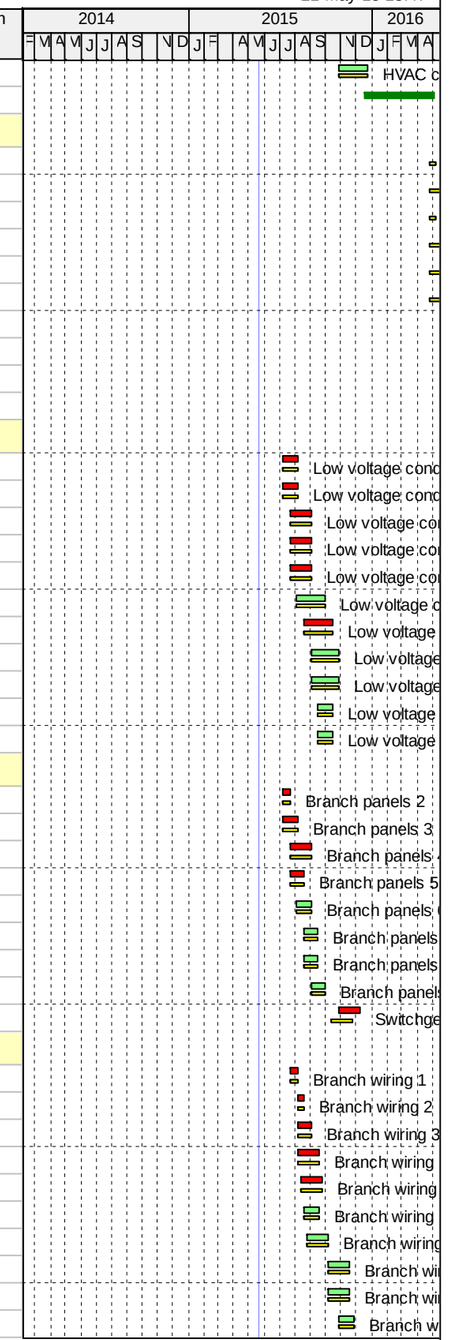

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
ELECBT1360	Branch wiring 9	30	30	0	0%	1	28-Oct-15	28-Oct-15		09-Dec-15	09-Dec-15	
Motor Connections												
ELECBT1340	Motor connection 2	10	10	0	0%	-17	06-Aug-15	17-Aug-15		20-Aug-15	31-Aug-15	
ELECBT1250	Motor connection 3	20	20	0	0%	-17	20-Aug-15	31-Aug-15		17-Sep-15	28-Sep-15	
ELECBT1180	Motor connection 4	10	10	0	0%	0	03-Sep-15	03-Sep-15		17-Sep-15	17-Sep-15	
ELECBT1330	Motor connection 5	5	5	0	0%	0	17-Sep-15	17-Sep-15		24-Sep-15	24-Sep-15	
ELECBT1190	Motor connection 7	5	5	0	0%	0	24-Sep-15	24-Sep-15		01-Oct-15	01-Oct-15	
ELECBT1240	Motor connection 10	10	10	0	0%	0	01-Oct-15	01-Oct-15		15-Oct-15	15-Oct-15	
CTBT1060	Motor Connection Roof	20	20	0	0%	1	28-Oct-15	28-Oct-15		25-Nov-15	25-Nov-15	
Cable Trays & Ladder Racks												
CTBT1000	COMMS Cable Trays 1	10	10	0	0%	-50	11-Sep-15	18-Dec-15		25-Sep-15	01-Jan-16	
CTBT1010	COMMS Cable Trays 2	10	10	0	0%	-50	24-Sep-15	31-Dec-15		08-Oct-15	14-Jan-16	
CTBT1040	COMMS Cable Trays 5	20	20	0	0%	-50	01-Dec-15	14-Jan-16		29-Dec-15	10-Feb-16	
CTBT1020	COMMS Cable Trays 3	40	40	0	0%	-50	08-Oct-15	14-Jan-16		02-Dec-15	09-Mar-16	
CTBT1030	COMMS Cable Trays 4	20	20	0	0%	-50	01-Dec-15	14-Jan-16		29-Dec-15	10-Feb-16	
CTBT1050	COMMS Cable Trays 10	20	20	0	0%	3	01-Dec-15	18-Jan-16		29-Dec-15	15-Feb-16	
CTBT1090	COMMS Cable Trays 8	20	20	0	0%	-13	23-Dec-15	03-Feb-16		20-Jan-16	02-Mar-16	
CTBT1070	COMMS Cable Trays 6	20	20	0	0%	-57	23-Dec-15	03-Feb-16		20-Jan-16	02-Mar-16	
CTBT1080	COMMS Cable Trays 7	20	20	0	0%	-57	23-Dec-15	03-Feb-16		20-Jan-16	02-Mar-16	
CTBT1100	COMMS Cable Trays 9	20	20	0	0%	-43	26-Jan-16	29-Mar-16		23-Feb-16	26-Apr-16	
Wiring Devices												
ELECBT1400	Wiring devices 5	20	20	0	0%	-81	29-Dec-15	07-Jan-16		26-Jan-16	04-Feb-16	
ELECBT1390	Wiring devices 4	20	20	0	0%	-81	29-Dec-15	07-Jan-16		26-Jan-16	04-Feb-16	
ELECBT1430	Wiring devices 10	10	10	0	0%	-31	29-Dec-15	04-Feb-16		12-Jan-16	18-Feb-16	
ELECBT1370	Wiring devices 3	20	20	0	0%	-81	29-Oct-15	04-Feb-16		26-Nov-15	03-Mar-16	
ELECBT1440	Wiring devices Roof	5	5	0	0%	-31	29-Dec-15	04-Feb-16		05-Jan-16	11-Feb-16	
ELECBT1420	Wiring devices 2	5	5	0	0%	-81	29-Oct-15	18-Feb-16		05-Nov-15	25-Feb-16	
ELECBT1410	Wiring devices 1	5	5	0	0%	-81	19-Oct-15	25-Feb-16		26-Oct-15	03-Mar-16	
ELECBT1490	Wiring devices 6	20	20	0	0%	14	03-Feb-16	16-Mar-16		02-Mar-16	13-Apr-16	
ELECBT1550	Wiring devices 7	20	20	0	0%	14	03-Feb-16	16-Mar-16		02-Mar-16	13-Apr-16	
ELECBT1580	Wiring devices 8	20	20	0	0%	14	17-Feb-16	16-Mar-16		16-Mar-16	13-Apr-16	
ELECBT1570	Wiring devices 9	20	20	0	0%	-25	05-Apr-16	10-May-16		03-May-16	07-Jun-16	
Electrical Light Fixtures												
ELECBT1530	Light Fixtures 5	20	20	0	0%	-50	01-Jan-16	11-Feb-16		29-Jan-16	10-Mar-16	
ELECBT1460	Light Fixtures 1	5	5	0	0%	2	21-Mar-16	30-Mar-16		25-Mar-16	06-Apr-16	
ELECBT1470	Light Fixtures 2	5	5	0	0%	2	21-Mar-16	31-Mar-16		25-Mar-16	06-Apr-16	
ELECBT1450	Light Fixtures 3	10	10	0	0%	-13	21-Mar-16	21-Apr-16		01-Apr-16	04-May-16	
ELECBT1480	Light Fixtures 4	20	20	0	0%	-13	21-Mar-16	21-Apr-16		15-Apr-16	18-May-16	
ELECBT1560	Light Fixtures 6	20	20	0	0%	26	16-Mar-16	27-Apr-16		13-Apr-16	25-May-16	
ELECBT1610	Light Fixtures 7	20	20	0	0%	37	16-Mar-16	03-May-16		13-Apr-16	31-May-16	
ELECBT1620	Light Fixtures 9	20	20	0	0%	20	19-Apr-16	30-Jun-16		17-May-16	27-Jul-16	
ELECBT1640	Light Fixtures 8	20	20	0	0%	-10	21-Apr-16	21-Jul-16		19-May-16	18-Aug-16	
UPS												
ELECBT1380	UPS System: Level 3	30	30	0	0%	-8	13-Oct-15	29-Oct-15		23-Nov-15	09-Dec-15	
Lighting Control Systems												
ELECBT1590	Lighting control systems 5 (SS, perf. Z5A first)	25	25	0	0%	-50	01-Jan-16	11-Feb-16		05-Feb-16	17-Mar-16	

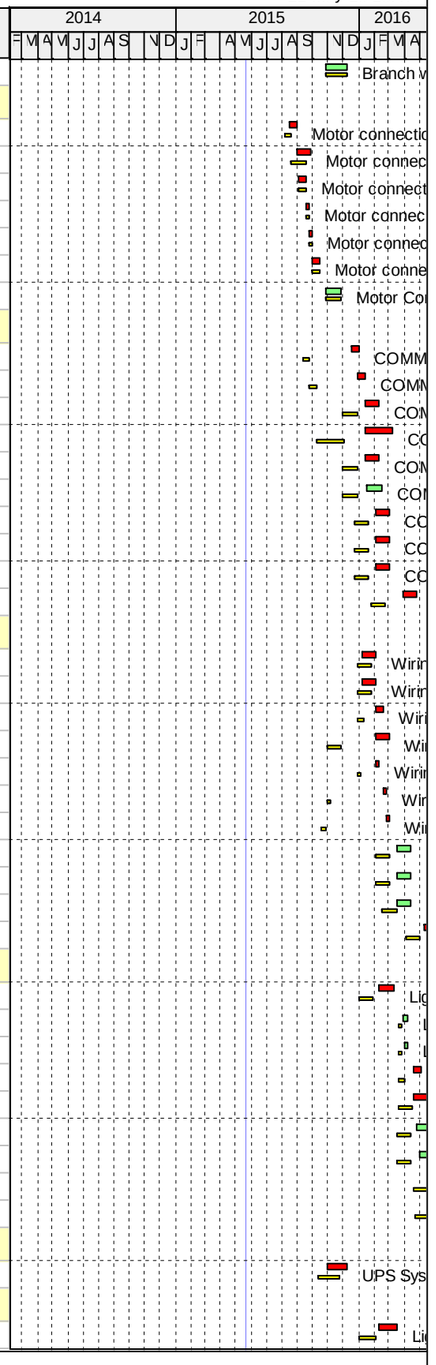

Remaining Level of Effort
Actual Level of Effort
Project Baseline Bar
Primary Baseline
Actual Work
Remaining Work

EW HOWELL

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
ELECBT1670	Lighting control system programming, Bed Tower	165	165	0	0%	-10	01-Jan-16	11-Feb-16		22-Jul-16	29-Sep-16	
ELECBT1500	Lighting control systems 1	5	5	0	0%	-12	28-Mar-16	11-May-16		01-Apr-16	17-May-16	
ELECBT1510	Lighting control systems 2	5	5	0	0%	-12	28-Mar-16	11-May-16		01-Apr-16	17-May-16	
ELECBT1520	Lighting control systems 3	10	10	0	0%	-12	04-Apr-16	18-May-16		15-Apr-16	31-May-16	
ELECBT1540	Lighting control systems 4	15	15	0	0%	-13	18-Apr-16	19-May-16		06-May-16	08-Jun-16	
ELECBT1600	Lighting control systems 6	15	15	0	0%	16	09-May-16	09-Jun-16		27-May-16	29-Jun-16	
ELECBT1630	Lighting control systems 7	15	15	0	0%	16	30-May-16	30-Jun-16		17-Jun-16	20-Jul-16	
ELECBT1650	Lighting control systems 8	15	15	0	0%	-10	10-Jun-16	18-Aug-16		01-Jul-16	08-Sep-16	
ELECBT1660	Lighting control systems 9	15	15	0	0%	-10	01-Jul-16	08-Sep-16		22-Jul-16	29-Sep-16	
	Fire Detection and Alarm System											
FABT1030	Fire alarm wiring 4	30	30	0	0%	-31	03-Sep-15	03-Sep-15		01-Oct-15	15-Oct-15	
FABT1040	Fire alarm wiring 5	30	30	0	0%	-31	17-Sep-15	03-Sep-15		15-Oct-15	15-Oct-15	
FABT1050	Fire alarm wiring 10	30	30	0	0%	9	14-Oct-15	14-Oct-15		11-Nov-15	25-Nov-15	
FABT1020	Fire alarm wiring 3	30	30	0	0%	-31	20-Aug-15	15-Oct-15		17-Sep-15	26-Nov-15	
FABT1060	Fire alarm wiring Roof	30	30	0	0%	9	28-Oct-15	28-Oct-15		25-Nov-15	09-Dec-15	
FABT1000	Fire alarm wiring 2	30	30	0	0%	-31	06-Aug-15	29-Oct-15		03-Sep-15	10-Dec-15	
FABT1010	Fire alarm wiring 1	30	30	0	0%	-21	06-Aug-15	19-Nov-15		03-Sep-15	31-Dec-15	
FABT1070	Fire alarm wiring 6	40	40	0	0%	18	28-Oct-15	03-Dec-15		23-Dec-15	28-Jan-16	
FABT1080	Fire alarm wiring 7	40	40	0	0%	18	25-Nov-15	17-Dec-15		20-Jan-16	11-Feb-16	
FABT1090	Fire alarm wiring 8	40	40	0	0%	18	23-Dec-15	31-Dec-15		17-Feb-16	25-Feb-16	
FABT1100	Fire alarm wiring 9	40	40	0	0%	18	06-Jan-16	14-Jan-16		02-Mar-16	10-Mar-16	
FABT1130	Fire Command Center 5 (MS2)	40	40	0	0%	-31	12-Jan-16	11-Feb-16		08-Mar-16	07-Apr-16	
FABT1120	FACPs (MS2)	60	60	0	0%	-81	29-Dec-15	25-Feb-16		22-Mar-16	19-May-16	
FABT1140	FA Programming Bed Tower (MS2)	30	30	0	0%	-81	09-Feb-16	21-Apr-16		22-Mar-16	02-Jun-16	
FABT1110	FACPs (MS2A)	40	40	0	0%	-25	03-May-16	07-Jun-16		28-Jun-16	02-Aug-16	
FABT1150	FA Programming Bed Tower (MS2A)	40	40	0	0%	-8	28-Jun-16	02-Aug-16		23-Aug-16	27-Sep-16	
	Work by Owner											
COMMBT1(	COMM wiring 5	5	5	0	0%	-50	22-Dec-15	04-Feb-16		29-Dec-15	10-Feb-16	
COMMBT1(	COMM wiring 4	5	5	0	0%	-33	29-Dec-15	11-Feb-16		05-Jan-16	17-Feb-16	
COMMBT11	COMM wiring Roof	5	5	0	0%	3	29-Dec-15	15-Feb-16		05-Jan-16	22-Feb-16	
COMMBT1(	COMM wiring 10	5	5	0	0%	3	29-Dec-15	15-Feb-16		05-Jan-16	22-Feb-16	
COMMBT1(	COMM wiring 6	5	5	0	0%	-20	20-Jan-16	02-Mar-16		27-Jan-16	09-Mar-16	
COMMBT1(	COMM wiring 3	5	5	0	0%	-47	03-Dec-15	03-Mar-16		09-Dec-15	09-Mar-16	
COMMBT1(	COMM wiring 7	5	5	0	0%	-19	20-Jan-16	09-Mar-16		27-Jan-16	16-Mar-16	
COMMBT1(	COMM wiring 1	5	5	0	0%	-35	10-Dec-15	10-Mar-16		16-Dec-15	16-Mar-16	
AVBT1020	AV wiring 3	5	5	0	0%	3	03-Dec-15	10-Mar-16		09-Dec-15	16-Mar-16	
COMMBT1(	COMM wiring 8	5	5	0	0%	-19	27-Jan-16	16-Mar-16		03-Feb-16	23-Mar-16	
COMMBT1(	COMM wiring 2	5	5	0	0%	-35	17-Dec-15	17-Mar-16		23-Dec-15	23-Mar-16	
AVBT1010	AV wiring 2	5	5	0	0%	183	10-Dec-15	17-Mar-16		16-Dec-15	23-Mar-16	
AVBT1030	AV wiring 4	5	5	0	0%	3	29-Dec-15	17-Mar-16		05-Jan-16	23-Mar-16	
AVBT1040	AV wiring 5	5	5	0	0%	3	29-Dec-15	17-Mar-16		05-Jan-16	23-Mar-16	
AVBT1000	AV wiring 1	5	5	0	0%	183	10-Dec-15	17-Mar-16		16-Dec-15	23-Mar-16	
AVBT1050	AV wiring 6	5	5	0	0%	3	20-Jan-16	24-Mar-16		27-Jan-16	30-Mar-16	
AVBT1060	AV wiring 7	5	5	0	0%	3	27-Jan-16	31-Mar-16		03-Feb-16	06-Apr-16	
AVBT1070	AV wiring 8	5	5	0	0%	3	03-Feb-16	07-Apr-16		10-Feb-16	13-Apr-16	
COMMBT1(	COMM wiring 9	5	5	0	0%	-43	23-Feb-16	26-Apr-16		01-Mar-16	03-May-16	

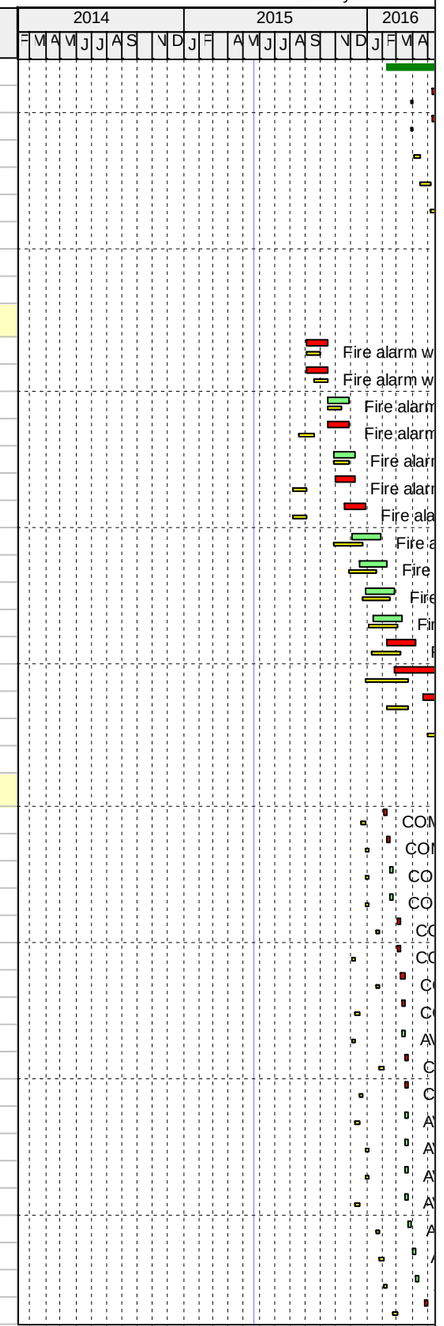

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
AVBT1080	AV wiring 9	5	5	0	0%	-5	23-Feb-16	26-Apr-16		01-Mar-16	03-May-16	
Auditorium												
Ornamental Handrails and Railings												
AUD1310	Hand-rails: Auditorium	20	20	0	0%	-7	25-Jan-16	14-Mar-16		22-Feb-16	11-Apr-16	
Carpentry												
AUD1000	Ramps, Platforms, Auditorium	30	30	0	0%	-15	11-May-15	01-Jun-15		22-Jun-15	13-Jul-15	
AUD1320	Plywood grounds and blocking, walls and ceilings, Auditorium	30	30	0	0%	-45	08-Jun-15	29-Jun-15		20-Jul-15	10-Aug-15	
AUD1340	Ceiling Suspended Panel Framework, Auditorium	30	30	0	0%	-55	06-Jul-15	27-Jul-15		17-Aug-15	07-Sep-15	
PLAM Doors												
AUD1360	PLAM doors: Auditorium	20	20	0	0%	-27	14-Apr-16	11-Apr-16		12-May-16	09-May-16	
Light-gauge Metal Framing												
GWBAUD1(	Interior Framing: Auditorium	20	20	0	0%	-55	11-May-15	01-Jun-15		08-Jun-15	29-Jun-15	
GWB Walls												
GWBAUD1(	GWB Partitions: Auditorium	20	20	0	0%	-55	17-Aug-15	07-Sep-15		14-Sep-15	05-Oct-15	
Acoustical Wall & Ceiling Panels												
AUD1130	Acoustical Wall Panels: Auditorium	30	30	0	0%	-7	14-Dec-15	01-Feb-16		25-Jan-16	14-Mar-16	
AUD1330	Acoustical Ceiling Panels: Auditorium	30	30	0	0%	-30	14-Dec-15	01-Feb-16		25-Jan-16	14-Mar-16	
Finish Carpentry: Casework, Paneling & Trims												
AUD1230	Auditorium wood wall paneling	60	60	0	0%	-55	19-Oct-15	09-Nov-15		14-Dec-15	01-Feb-16	
Painting												
AUD1110	Painting: Auditorium	25	25	0	0%	-55	14-Sep-15	05-Oct-15		19-Oct-15	09-Nov-15	
AUD1140	Performance Flooring	20	20	0	0%	-27	17-Mar-16	14-Mar-16		14-Apr-16	11-Apr-16	
Resilient Flooring & Carpeting												
AUD1270	Resilient Flooring Auditorium	30	30	0	0%	-27	17-Mar-16	14-Mar-16		28-Apr-16	22-Apr-16	
Ceramic Tile												
AUD1240	Ceramic tile Auditorium baths	20	20	0	0%	-2	18-Jan-16	08-Feb-16		15-Feb-16	07-Mar-16	
Terrazzo Flooring												
AUD1210	Terrazzo Flooring: Auditorium	30	30	0	0%	43	19-Oct-15	09-Nov-15		30-Nov-15	21-Dec-15	
Wood Flooring												
AUD1170	Wood Flooring: Auditorium	30	30	0	0%	43	30-Nov-15	21-Dec-15		11-Jan-16	01-Feb-16	
Specialties/Accessories												
AUD1290	Install Div. 10 accessories: Auditorium	20	20	0	0%	-7	22-Feb-16	14-Mar-16		21-Mar-16	11-Apr-16	
AUD1190	Seating	20	20	0	0%	-30	18-Apr-16	06-Jun-16		16-May-16	04-Jul-16	
Wet Standpipe System Piping												
FSAUD1060	Fire suppression branch work and heads Auditorium	20	20	0	0%	-55	08-Jun-15	29-Jun-15		06-Jul-15	27-Jul-15	
Plumbing Fixtures												
PAUD1280	Plumbing Fixtures Auditorium	15	15	0	0%	-48	06-Apr-16	17-May-16		27-Apr-16	07-Jun-16	
General Requirements for Mechanical Work												
MECHAUD1	Air-balancing, Auditorium	5	5	0	0%	-7	04-Jan-16	22-Feb-16		11-Jan-16	29-Feb-16	
HVAC Ductwork												
MECHAUD1	Ductwork Auditorium	20	20	0	0%	-55	11-May-15	01-Jun-15		08-Jun-15	29-Jun-15	
Duct Insulation												
AUD1050	Ductwork Insulation Auditorium	20	20	0	0%	-55	11-May-15	29-Jun-15		08-Jun-15	27-Jul-15	

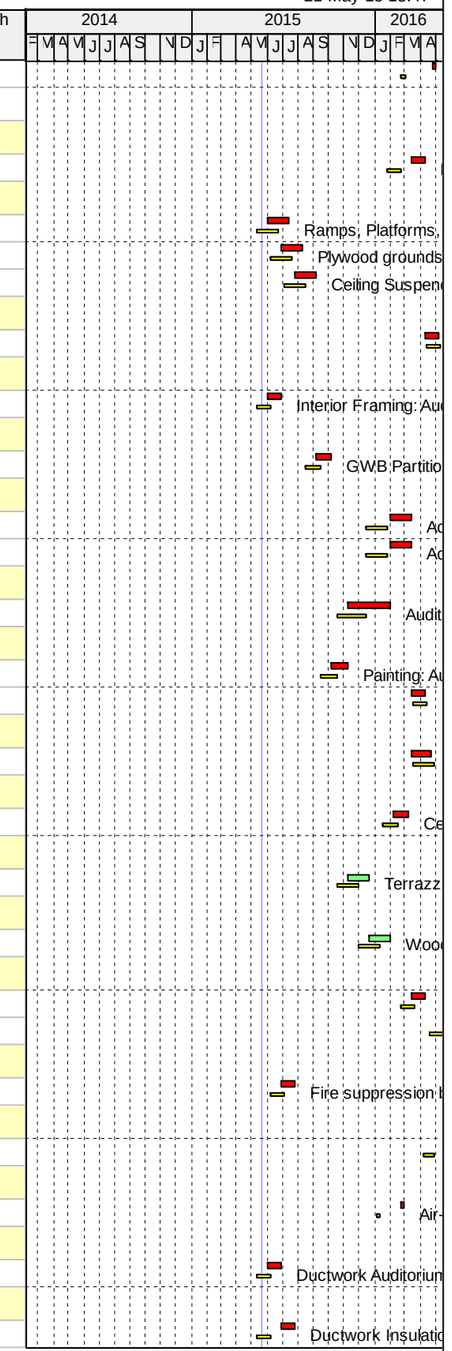

Remaining Level of Effort | Actual Level of Effort | Project Baseline Bar | Primary Baseline | Actual Work | Remaining Work

EW HOWELL

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
HVAC DDC & Secondary Controls												
MECHAUD1	HVAC Control wiring 5 Auditorium	30	30	0	0%	-44	25-Nov-15	06-Nov-15		23-Dec-15	18-Dec-15	
HVAC Grilles												
MECHAUD1	Supply/Return grilles Auditorium	20	20	0	0%	-7	14-Dec-15	01-Feb-16		11-Jan-16	29-Feb-16	
Conduits, Troughs, Boxes and Fittings												
ELECAUD1	Low-voltage conduit Auditorium	20	20	0	0%	27	08-Jun-15	18-Jun-15		06-Jul-15	16-Jul-15	
Panelboards and Switchboards												
ELECAUD1	Branch panels Auditorium	10	10	0	0%	-45	08-Jun-15	29-Jun-15		22-Jun-15	13-Jul-15	
Branch Wiring: Power & Lighting												
ELECAUD1	Branch wiring Auditorium	30	30	0	0%	-55	06-Jul-15	27-Jul-15		17-Aug-15	07-Sep-15	
Motor Connections												
ELECAUD1	Motor connection Auditorium	20	20	0	0%	18	26-Nov-15	09-Nov-15		24-Dec-15	04-Dec-15	
Cable Trays & Ladder Racks												
AUD1160	COMMS Cable trays Auditorium	5	5	0	0%	18	24-Dec-15	07-Dec-15		31-Dec-15	11-Dec-15	
Wiring Devices												
ELECAUD1	Wiring devices Auditorium	20	20	0	0%	-55	23-Dec-15	04-Jan-16		20-Jan-16	01-Feb-16	
Electrical Light Fixtures												
ELECAUD1	Light Fixtures (up) Auditorium	30	30	0	0%	45	17-Aug-15	07-Sep-15		28-Sep-15	19-Oct-15	
ELECAUD1	Light Fixtures (down) Auditorium	30	30	0	0%	-30	25-Jan-16	14-Mar-16		07-Mar-16	25-Apr-16	
Lighting Control Systems												
ELECAUD1	Lighting control systems Auditorium	30	30	0	0%	-30	07-Mar-16	25-Apr-16		18-Apr-16	06-Jun-16	
Fire Detection and Alarm System												
ELECAUD1	Fire Alarm wiring Auditorium	40	40	0	0%	27	06-Jul-15	16-Jul-15		31-Aug-15	10-Sep-15	
Work by Owner												
AUD1150	Security/Access wiring Auditorium	20	20	0	0%	-27	21-Jan-16	18-Jan-16		18-Feb-16	12-Feb-16	
AUD1180	COMMS wiring Auditorium	20	20	0	0%	-27	18-Feb-16	15-Feb-16		17-Mar-16	11-Mar-16	
Canopy												
Concrete												
CON7260	Canopy footings & anchor bolts	20	20	0	0%	-12	28-Dec-15	27-Jan-16		22-Jan-16	23-Feb-16	
Structural Steel												
CON5211	Install canopy steel	25	25	0	0%	-12	25-Jan-16	24-Feb-16		26-Feb-16	29-Mar-16	
Metal Composite Panels												
CON7200	Metal composite panels and trims, Canopy	30	30	0	0%	-2	14-Mar-16	13-Apr-16		22-Apr-16	24-May-16	
PVC Roofing												
CON10640	Canopy roof membrane	10	10	0	0%	-12	29-Feb-16	30-Mar-16		11-Mar-16	12-Apr-16	
Interior Glazing												
CON5920	Fritted glass assemblies, Canopy	30	30	0	0%	-2	14-Mar-16	13-Apr-16		22-Apr-16	24-May-16	
Branch Wiring: Power & Lighting												
CON10650	Branch wiring Canopy	20	20	0	0%	-12	14-Mar-16	13-Apr-16		08-Apr-16	10-May-16	
Electrical Light Fixtures												
CON10660	Light Fixtures Canopy	20	20	0	0%	-12	11-Apr-16	11-May-16		06-May-16	07-Jun-16	
Generator Building												

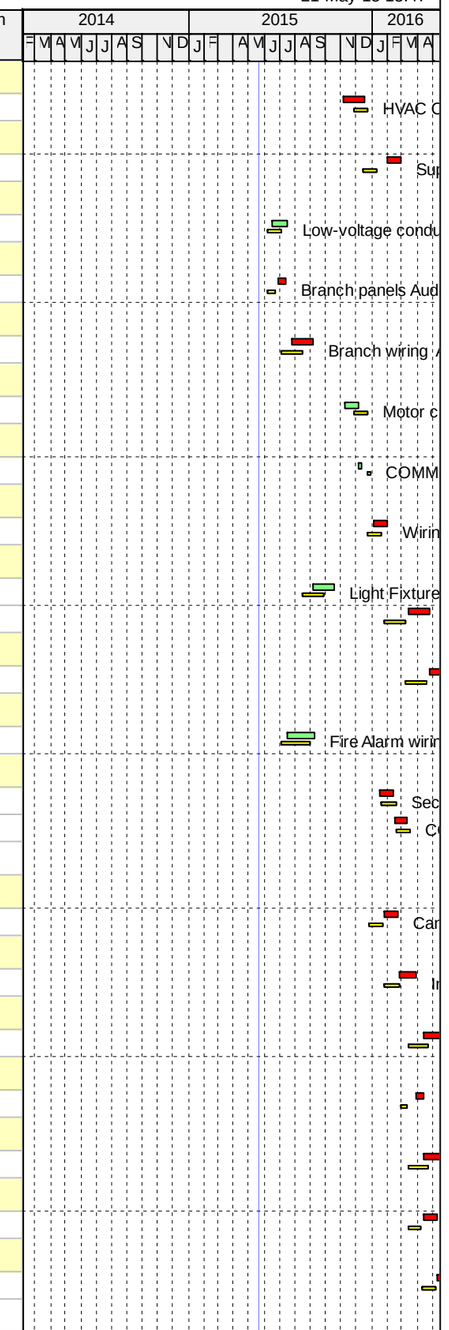

Remaining Level of Effort | Project Baseline Bar | Actual Work
Actual Level of Effort | Primary Baseline | Remaining Work

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
General Construction												
GEN1040	Generator room electrical connection	10	10	0	0%	-17	14-Aug-15	23-Sep-15		27-Aug-15	06-Oct-15	
GEN1130	Roof penetrations for exhaust stacks	3	3	0	0%	-2	15-Oct-15	11-Nov-15		20-Oct-15	13-Nov-15	
GEN1140	Exhaust Stacks	10	10	0	0%	-2	20-Oct-15	16-Nov-15		22-Oct-15	27-Nov-15	
GEN1150	Seal penetrations	2	2	0	0%	-2	22-Oct-15	30-Nov-15		26-Oct-15	01-Dec-15	
Concrete												
GEN1020	Generator mat	1	1	0	0%	9	20-Aug-15	11-Aug-15		21-Aug-15	12-Aug-15	
GEN1030	Generator housekeeping pad	5	5	0	0%	9	03-Sep-15	25-Aug-15		10-Sep-15	01-Sep-15	
Structural Steel												
GEN1070	Install generator louver supports	10	10	0	0%	-2	17-Sep-15	14-Oct-15		01-Oct-15	27-Oct-15	
HVAC Grilles												
GEN1110	Install Generator House Louvers	10	10	0	0%	-2	01-Oct-15	28-Oct-15		15-Oct-15	10-Nov-15	
Packaged Generators												
GEN1000	Install generator conduits (FBO)	10	3	7	70%	9	06-Aug-15	06-Aug-15	11-May-15	20-Aug-15	11-Aug-15	
GEN1010	Generator cable, I	8	8	0	0%	16	20-Aug-15	11-Aug-15		01-Sep-15	21-Aug-15	
GEN1050	Mount Mechanical Generator	5	5	0	0%	-17	10-Sep-15	07-Oct-15		17-Sep-15	13-Oct-15	
GEN1060	Mount Electrical Generator	5	5	0	0%	-17	10-Sep-15	07-Oct-15		17-Sep-15	13-Oct-15	
GEN1080	Install parelleling gear	10	10	14	5%	-17	17-Sep-15	14-Oct-15	30-Apr-15	01-Oct-15	27-Oct-15	
GEN1090	Generator cable, II	2	2	0	0%	-9	17-Sep-15	14-Oct-15		21-Sep-15	15-Oct-15	
GEN1100	Generator terminations	5	5	0	0%	-17	01-Oct-15	27-Oct-15		08-Oct-15	03-Nov-15	
GEN1120	FBO fuel oil	0	0	0	0%	-17				08-Oct-15	03-Nov-15	
Zone 5A (exist.)												
General Construction												
Z5A1090	ICRA protections	20	20	0	0%	-50	26-Jan-16	03-Mar-16		23-Feb-16	31-Mar-16	
Selective Demolition												
Z5A1190	Selective general demolition	10	10	0	0%	-47	07-Mar-16	13-Apr-16		18-Mar-16	26-Apr-16	
Abatement												
Z5A1100	ACM removals: Level 2	5	5	0	0%	-50	26-Jan-16	03-Mar-16		02-Feb-16	10-Mar-16	
Z5A1110	ACM removals: Level 3	5	5	0	0%	-50	02-Feb-16	10-Mar-16		09-Feb-16	17-Mar-16	
Z5A1140	ACM removals: Level 4	5	5	0	0%	-47	15-Feb-16	23-Mar-16		22-Feb-16	30-Mar-16	
Z5A1160	ACM removals: Level 5	5	5	0	0%	-47	29-Feb-16	06-Apr-16		04-Mar-16	12-Apr-16	
Light-gauge Metal Framing												
Z5A1130	GWB Enclosures: Level 2	15	15	0	0%	-50	24-Mar-16	02-May-16		14-Apr-16	23-May-16	
Z5A1310	GWB Enclosures: Level 4	15	15	0	0%	-33	12-Apr-16	19-May-16		03-May-16	09-Jun-16	
Z5A1270	GWB Enclosures: Level 3	15	15	0	0%	-50	14-Apr-16	23-May-16		05-May-16	13-Jun-16	
Z5A1320	GWB Enclosures: Level 5	15	15	0	0%	-38	26-Apr-16	02-Jun-16		17-May-16	23-Jun-16	
Suspended Acoustical Ceiling												
Z5A1280	ACT Ceilings Level 1	10	10	0	0%	-45	25-Apr-16	01-Jun-16		06-May-16	14-Jun-16	
Z5A1330	ACT Ceilings Level 2	10	10	0	0%	-45	25-Apr-16	01-Jun-16		06-May-16	14-Jun-16	
Z5A1340	ACT Ceilings Level 3	10	10	0	0%	-23	03-May-16	09-Jun-16		17-May-16	23-Jun-16	
Z5A1360	ACT Ceilings: Level 4	15	15	0	0%	-43	30-May-16	06-Jul-16		20-Jun-16	27-Jul-16	
Z5A1390	ACT Ceilings: Level 5	10	10	0	0%	-43	30-May-16	06-Jul-16		13-Jun-16	20-Jul-16	
Painting												
Z5A1350	Painting: Level 2	15	15	0	0%	-45	25-Apr-16	01-Jun-16		13-May-16	21-Jun-16	

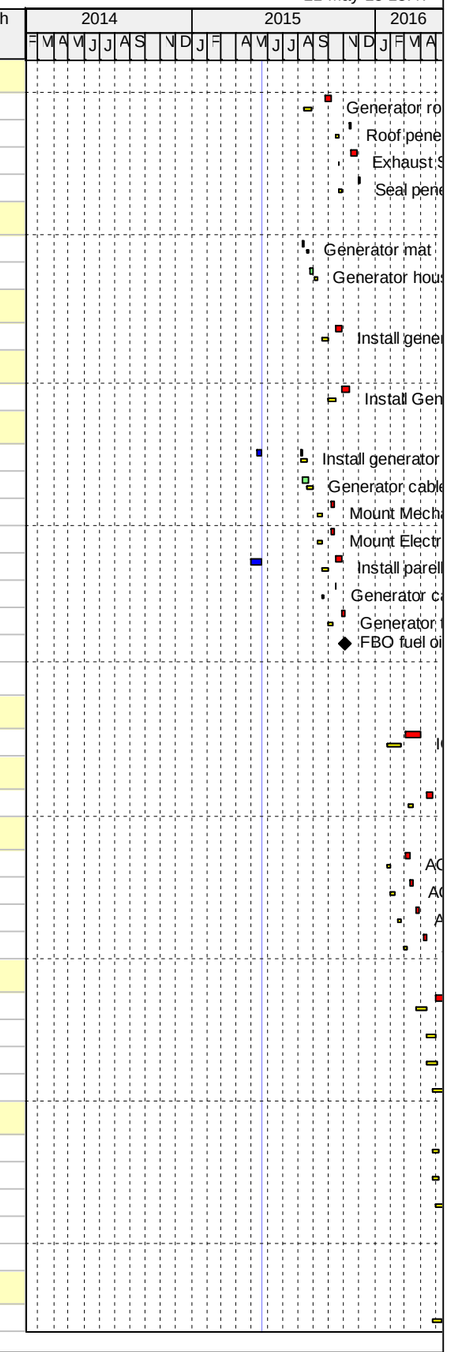

Remaining Level of Effort
Actual Level of Effort
Project Baseline Bar
Primary Baseline
Actual Work
Remaining Work

EW HOWELL

TASK filter: All Activities

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
Z5A1370	Painting: Level 3	15	15	0	0%	-50	05-May-16	13-Jun-16		26-May-16	04-Jul-16	
Z5A1400	Painting: Level 4	15	15	0	0%	-50	26-May-16	04-Jul-16		16-Jun-16	25-Jul-16	
Z5A1410	Painting: Level 5	15	15	0	0%	-50	02-Jun-16	11-Jul-16		23-Jun-16	01-Aug-16	
Resilient Flooring & Carpeting												
Z5A1380	Resilient flooring Level 2	23	23	0	0%	-45	16-May-16	22-Jun-16		15-Jun-16	22-Jul-16	
Pneumatic Tube Systems												
Z5A1290	Pneumatic tubes: Level 3	10	10	0	0%	-23	19-Apr-16	26-May-16		03-May-16	09-Jun-16	
Z5A1300	Pneumatic tubes: Level 4	10	10	0	0%	-43	16-May-16	22-Jun-16		30-May-16	06-Jul-16	
Wet Standpipe System Piping												
Z5A1170	Selective sprinkler demolition: Level 3	5	5	0	0%	-23	09-Feb-16	17-Mar-16		16-Feb-16	24-Mar-16	
Z5A1210	Selective sprinkler demolition: Level 4	5	5	0	0%	-28	22-Feb-16	30-Mar-16		29-Feb-16	06-Apr-16	
Z5A1240	Selective sprinkler demolition: Level 5	5	5	0	0%	-37	07-Mar-16	13-Apr-16		11-Mar-16	19-Apr-16	
Z5A1180	Selective sprinkler demolition: Level 1	5	5	0	0%	-45	07-Mar-16	13-Apr-16		11-Mar-16	19-Apr-16	
Z5A1220	Sprinkler: Level 3	30	30	0	0%	-23	08-Mar-16	14-Apr-16		19-Apr-16	26-May-16	
Z5A1230	Sprinkler: Level 1	30	30	0	0%	-45	14-Mar-16	20-Apr-16		22-Apr-16	31-May-16	
Z5A1250	Sprinkler: Level 4	40	40	0	0%	-43	21-Mar-16	27-Apr-16		16-May-16	22-Jun-16	
Z5A1260	Sprinkler: Level 5	30	30	0	0%	-47	28-Mar-16	04-May-16		06-May-16	14-Jun-16	
HVAC Ductwork												
Z5A1010	HVAC ductwork demolition: Level 3	10	10	0	0%	-50	09-Feb-16	17-Mar-16		23-Feb-16	31-Mar-16	
Z5A1040	HVAC ductwork demolition: Level 4	10	10	0	0%	-43	22-Feb-16	30-Mar-16		07-Mar-16	13-Apr-16	
Z5A1030	HVAC ductwork reinstalled Level 3	10	10	0	0%	-50	23-Feb-16	31-Mar-16		08-Mar-16	14-Apr-16	
Z5A1070	HVAC ductwork demolition: Level 5	5	5	0	0%	-47	07-Mar-16	13-Apr-16		11-Mar-16	19-Apr-16	
Z5A1060	HVAC ductwork reinstalled Level 4	10	10	0	0%	-43	07-Mar-16	13-Apr-16		21-Mar-16	27-Apr-16	
Z5A1080	HVAC ductwork reinstalled Level 5	10	10	0	0%	-47	14-Mar-16	20-Apr-16		25-Mar-16	03-May-16	
Branch Wiring: Power & Lighting												
Z5A1000	Electrical demolition: Level 1-3	10	10	0	0%	-35	02-Feb-16	10-Mar-16		16-Feb-16	24-Mar-16	
Z5A1020	Electrical demolition: Level 4	10	10	0	0%	-23	16-Feb-16	24-Mar-16		01-Mar-16	07-Apr-16	
Z5A1050	Electrical demolition: Level 5	10	10	0	0%	-23	01-Mar-16	07-Apr-16		15-Mar-16	21-Apr-16	
Z5A1120	Electrical rewiring Level 1-3	12	12	0	0%	-50	08-Mar-16	14-Apr-16		24-Mar-16	02-May-16	
Z5A1150	Electrical rewiring Level 4	15	15	0	0%	-38	22-Mar-16	28-Apr-16		12-Apr-16	19-May-16	
Z5A1200	Electrical rewiring Level 5	15	15	0	0%	-38	05-Apr-16	12-May-16		26-Apr-16	02-Jun-16	
General												
Concrete												
CON6520	Bollard footings	5	5	0	0%	19	28-Dec-15	27-Jan-16		01-Jan-16	02-Feb-16	
Overhead Coiling Doors												
CON5213	Overhead Coiling Door Installation	40	40	0	0%	-27	21-Mar-16	04-May-16		13-May-16	28-Jun-16	
Alerton Systems												
CON8650	Alertron System installation	60	60	0	0%	31	04-Jan-16	25-Nov-15		25-Mar-16	17-Feb-16	
Exterior Improvements												
CON6510	Crash Bollards	20	20	0	0%	19	28-Mar-16	27-Apr-16		22-Apr-16	24-May-16	
CON6500	Concrete walks	30	30	0	0%	19	25-Apr-16	25-May-16		03-Jun-16	05-Jul-16	
CON7010	Landscaping	60	60	0	0%	19	06-Jun-16	06-Jul-16		26-Aug-16	27-Sep-16	
CON6490	Paving	30	30	0	0%	19	29-Aug-16	28-Sep-16		07-Oct-16	08-Nov-16	
Close-out												

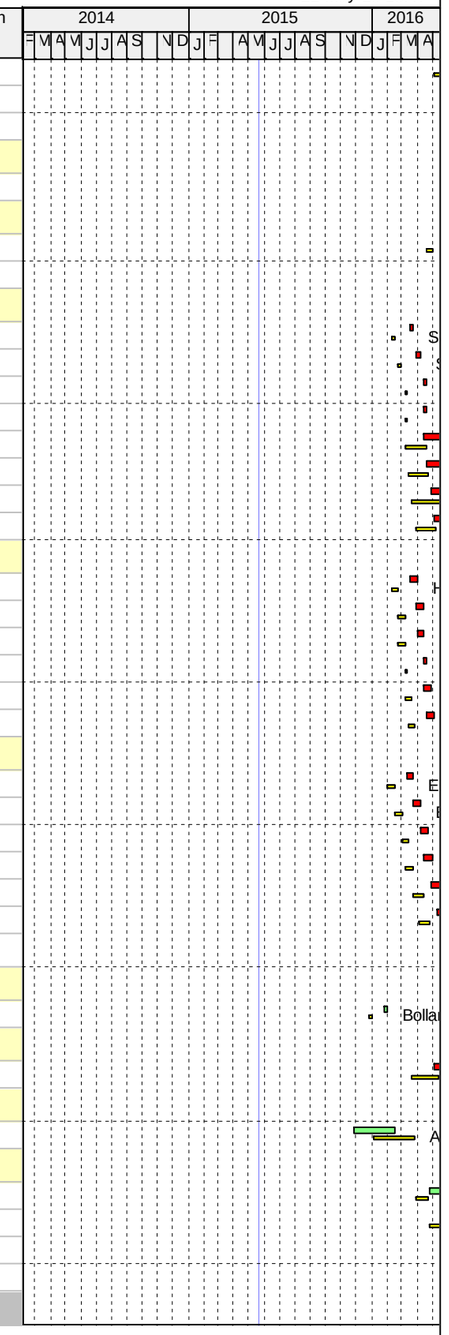
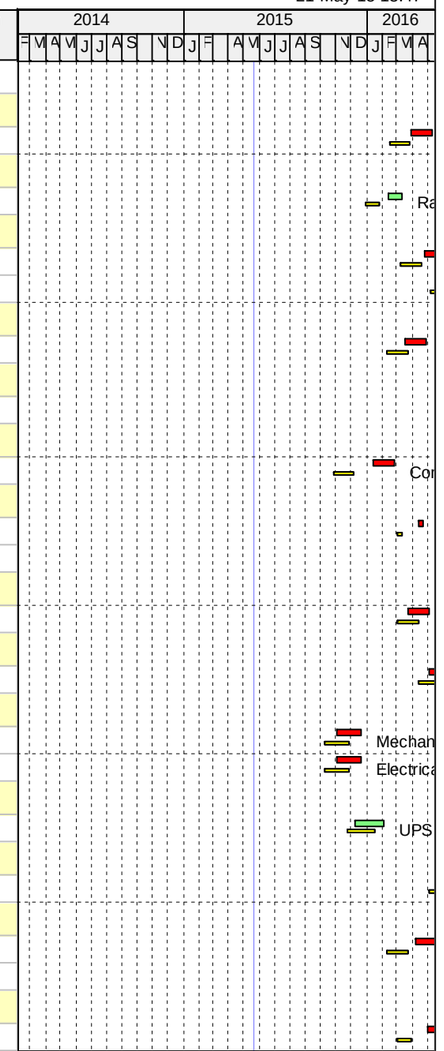
Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Duration	Activity % Complete	Total Float	BL Project Early Start	Early Start	Actual Start	BL Project Early Finish	Early Finish	Actual Finish
Testing & Commisssioning												
Medical Equipment: Major												
MECHCLOS	Major Medical equipment testing & commissioning	30	30	0	0%	-28	15-Feb-16	29-Mar-16		25-Mar-16	09-May-16	
Radiation Protection												
CLOSE100	Radiation shielding testing	20	20	0	0%	14	29-Dec-15	12-Feb-16		26-Jan-16	11-Mar-16	
Wet Standpipe System Piping												
FSCLOSE1:	Wet fire suppression equipment testing & commissioning: MART & Bed T	30	30	0	0%	-48	08-Mar-16	26-Apr-16		19-Apr-16	07-Jun-16	
CLOSE240	Wet fire suppression equipment testing & commissioning: Existing Buildin	30	30	0	0%	-47	09-May-16	15-Jun-16		17-Jun-16	26-Jul-16	
Clean-Agent Fire Suppression												
FSCLOSE1-	Clean-agent fire suppression equipment testing & commissioning	30	30	0	0%	-20	11-Feb-16	17-Mar-16		24-Mar-16	28-Apr-16	
Plumbing												
PCLOSE120	Plumbing equipment testing & commissioning	30	30	0	0%	-57	18-May-16	28-Jun-16		29-Jun-16	09-Aug-16	
Compressed Air & Vacuum, Medical Gas Distribution												
PCLOSE200	Compressed air & vacuum systems testing & commissioning	30	30	0	0%	-17	26-Oct-15	14-Jan-16		07-Dec-15	25-Feb-16	
Laboratory Gas Alarms												
CON9280	Test Gas alarm system (MS2)	6	6	0	0%	-51	03-Mar-16	13-Apr-16		11-Mar-16	21-Apr-16	
CON10950	Test Gas alarm system (MS2A)	5	5	0	0%	-27	17-May-16	28-Jul-16		24-May-16	03-Aug-16	
General Requirements for Mechanical Work												
MECHCLOS	HVAC equipment testing & commissioning	30	30	0	0%	-25	03-Mar-16	24-Mar-16		14-Apr-16	05-May-16	
HVAC DDC & Secondary Controls												
MECHCON-	DDC System testing & commissioning	30	30	0	0%	-18	14-Apr-16	05-May-16		26-May-16	16-Jun-16	
Packaged Generators												
MCLOSE220	Mechanical Generator testing & commissioning	35	35	0	0%	-17	08-Oct-15	03-Nov-15		26-Nov-15	22-Dec-15	
MCLOSE230	Electrical Generator testing & commissioning	35	35	0	0%	-17	08-Oct-15	03-Nov-15		26-Nov-15	22-Dec-15	
UPS												
ELECCLOS	UPS testing & commissioning	40	40	0	0%	40	24-Nov-15	10-Dec-15		18-Jan-16	03-Feb-16	
Lighting Control Systems												
ELECCLOS	Lighting control system testing & commissioning	20	20	0	0%	-75	06-May-16	08-Aug-16		03-Jun-16	02-Sep-16	
Fire Detection and Alarm System												
FACLOSE15	Fire Alarm system equipment testing & commissioning MS2	30	30	0	0%	-66	09-Feb-16	07-Apr-16		22-Mar-16	19-May-16	
FACLOSE25	Fire Alarm system equipment testing & commissioning MS2A	57	57	0	0%	-27	28-Jun-16	04-Aug-16		15-Sep-16	21-Oct-16	
Communications (work-by-owner)												
CON\MMCL	COMM Systems testing & commissioning	20	20	0	0%	-43	01-Mar-16	03-May-16		29-Mar-16	31-May-16
